ID	Task Mode	Task Name	Duration	Start	Finish	Free Slack	Predecessors	Resource Names
1		**Github Repo Creatior**	**232 days**	**Thu 2/9/17**	**Sat 12/30/17**	**0 days**		
2		Personal Wiki page	1 day	Thu 2/9/17	Thu 2/9/17	0 days		
3		Project wiki page cı	232 days	Fri 2/10/17	Sat 12/30/17	10 days	2	
4		Weekly issue creati	232 days	Fri 2/10/17	Sat 12/30/17	10 days	2	
5		**Requirements**	**4 days**	**Thu 2/16/17**	**Tue 2/21/17**	**0 days**		
6		**Requirements Ana**	**2 days**	**Thu 2/16/17**	**Sun 2/19/17**	**0 days**		
7		Discussing the pı	1 day	Thu 2/16/17	Thu 2/16/17	0 days		
8		Asking unclear p	2 days	Fri 2/17/17	Sun 2/19/17	0 days	7	
9		**Requirements Elici**	**2 days**	**Mon 2/20/17**	**Tue 2/21/17**	**0 days**		
10		Talking to the cu	1 day	Mon 2/20/17	Mon 2/20/17	0 days	8	
11		Understanding a	1 day	Tue 2/21/17	Tue 2/21/17	1 day	10	
12		**Mock-ups**	**13 days**	**Thu 2/23/17**	**Mon 3/13/17**	**0 days**		

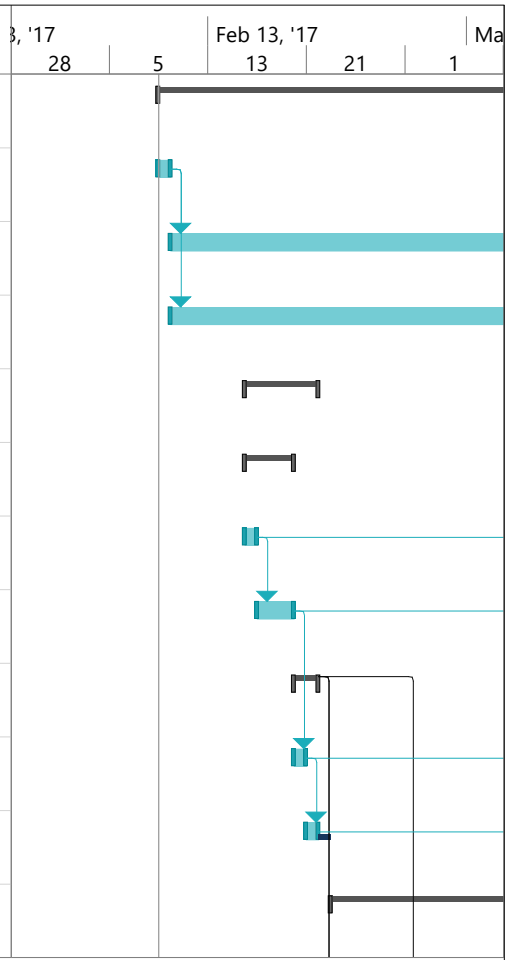

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

ID	Task Mode	Task Name	Duration	Start	Finish	Free Slack	Predecessors	Resource Names
13		**Android and Web**	**3 days**	**Thu 2/23/17**	**Mon 2/27/17**	**0 days**	**9**	
14		Designing Sign-U	3 days	Thu 2/23/17	Mon 2/27/17	10 days		
15		Designing Profile	3 days	Thu 2/23/17	Mon 2/27/17	10 days		
16		Concert/User Se	3 days	Thu 2/23/17	Mon 2/27/17	10 days		
17		**Mockup Scenario (	**13 days**	**Thu 2/23/17**	**Mon 3/13/17**	**0 days**	**9**	
18		Leroy Velasquez	2 days	Sat 3/11/17	Mon 3/13/17	0 days		Kemal Berk
19		John Smith	3 days	Thu 2/23/17	Mon 2/27/17	10 days		
20		Sarp and Mert	2 days	Sat 3/11/17	Mon 3/13/17	0 days		Furkan
21		Requirements & Desig	0 days	Tue 3/14/17	Tue 3/14/17	25 days	7,8,10,11,14,15,1	
22		**Diagram Creation**	**24 days**	**Thu 3/2/17**	**Tue 4/4/17**	**0 days**	**9**	
23		**Use Case Diagram**	**3 days**	**Thu 3/2/17**	**Mon 3/6/17**	**0 days**		
24		Concert Creatior	3 days	Thu 3/2/17	Mon 3/6/17	0 days		

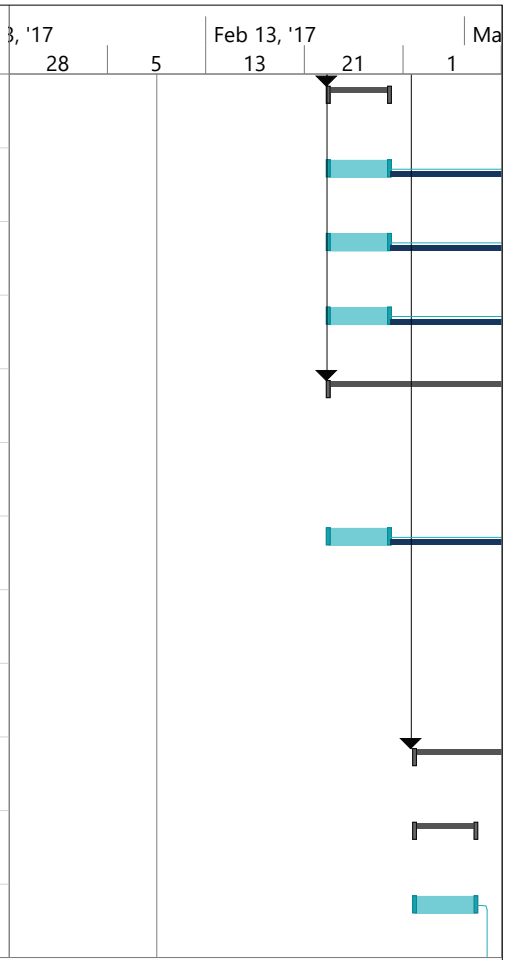

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

ID	Task Mode	Task Name	Duration	Start	Finish	Free Slack	Predecessors	Resource Names
25		View Concert an	3 days	Thu 3/2/17	Mon 3/6/17	0 days		
26		Search Concert a	3 days	Thu 3/2/17	Mon 3/6/17	0 days		
27		Registration/Sign	3 days	Thu 3/2/17	Mon 3/6/17	0 days		
28		Sign In	3 days	Thu 3/2/17	Mon 3/6/17	0 days		
29		Get Recommend	3 days	Thu 3/2/17	Mon 3/6/17	0 days		
30		Follow Another U	3 days	Thu 3/2/17	Mon 3/6/17	0 days		
31		Mark a Concert A	3 days	Thu 3/2/17	Mon 3/6/17	0 days		
32		Class Diagram	3 days	Tue 3/7/17	Thu 3/9/17	0 days	24,25,26,27,28,29	
33		Sequence Diagram	4 days	Fri 3/10/17	Wed 3/15/17	0 days	32	
34		Activity Diagram	14 days	Thu 3/16/17	Tue 4/4/17	9 days	33	
35		Diagram Creation	0 days	Tue 4/18/17	Tue 4/18/17	194 days	34,21	
36		**Planning**	**39 days**	**Tue 3/14/17**	**Fri 5/5/17**	**0 days**		

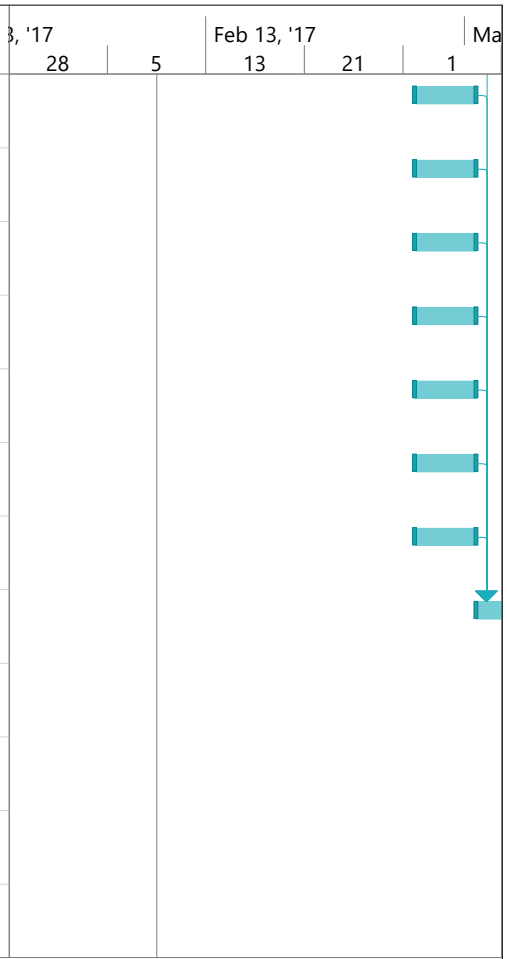

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

ID	Task Mode	Task Name	Duration	Start	Finish	Free Slack	Predecessors	Resource Names
37		Communication Plan	4 days	Thu 3/16/17	Tue 3/21/17	213 days		
38		**Project Plan**	**11 days**	**Tue 3/14/17**	**Tue 3/28/17**	**0 days**		
39		Milestone Creation	11 days	Tue 3/14/17	Tue 3/28/17	29 days		
40		Test Plan	14 days	Tue 4/4/17	Fri 4/21/17	190 days		
41		Responsibility Assignment Matrix	14 days	Tue 4/18/17	Fri 5/5/17	180 days		
42		Project Plan	0 days	Tue 5/9/17	Tue 5/9/17	179 days	39	
43		**Testing**	**65 days**	**Mon 10/16/**	**Fri 1/12/18**	**0 days**		
44		Creating Test Cases	65 days	Mon 10/16/17	Fri 1/12/18	0 days		
45		**Big Revision**	**16 days**	**Fri 9/29/17**	**Fri 10/20/17**	**0 days**		
46		Plan Review	16 days	Fri 9/29/17	Fri 10/20/17	60 days		
47		Task Distribution	16 days	Fri 9/29/17	Fri 10/20/17	60 days		
48		Responding on Feedbacks	16 days	Fri 9/29/17	Fri 10/20/17	60 days		

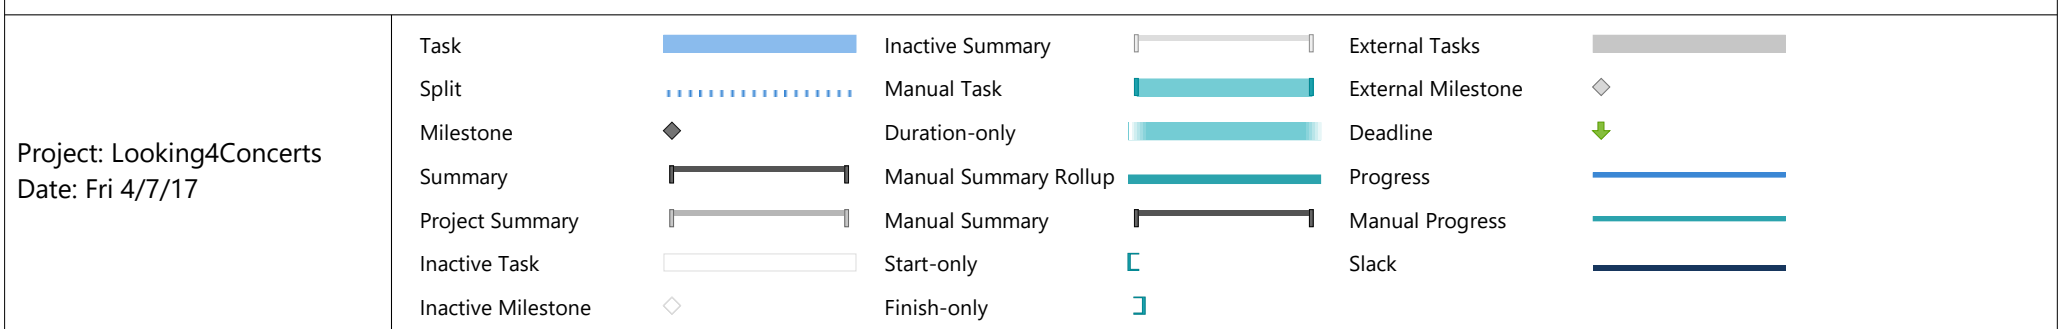

ID	Task Mode	Task Name	Duration	Start	Finish	Free Slack	Predecessors	Resource Names
49		Database	0 days	Sat 10/21/17	Sat 10/21/17	61 days	53,54,55,56	
50		**Implementation**	**37 days**	**Sun 10/8/17**	**Tue 11/28/17**	**0 days**		
51		**Back-End Developments**	**28 days**	**Sun 10/8/17**	**Wed 11/15/17**	**0 days**		**Haluk Alper,Oğuzhan**
52		**Database System Design / Implementation**	**10 days**	**Sun 10/8/17**	**Fri 10/20/17**	**0 days**		**Haluk Alper,Oğuzhan**
53		Database Plan	1 day	Sun 10/8/17	Sun 10/8/17	10 days		Haluk Alper,Oğuzhan
54		DB Modeling	3 days	Tue 10/10/17	Thu 10/12/17	6 days		Haluk Alper,Oğuz
55		User Table Im	7 days	Thu 10/12/17	Fri 10/20/17	0 days		Haluk Alper,Oğuz
56		Concert Table	7 days	Thu 10/12/17	Fri 10/20/17	0 days		Haluk Alper,Oğuz
57		**Algorithm Imple**	**17 days**	**Tue 10/24/17**	**Wed 11/15/**	**0 days**		**Haluk Alper,Oğu**
58		Search Algorit	3 days	Tue 10/24/17	Thu 10/26/17	0 days		Haluk Alper,Oğuz
59		Recommenda	6 days	Fri 10/27/17	Fri 11/3/17	0 days	58	Haluk Alper,Oğuz

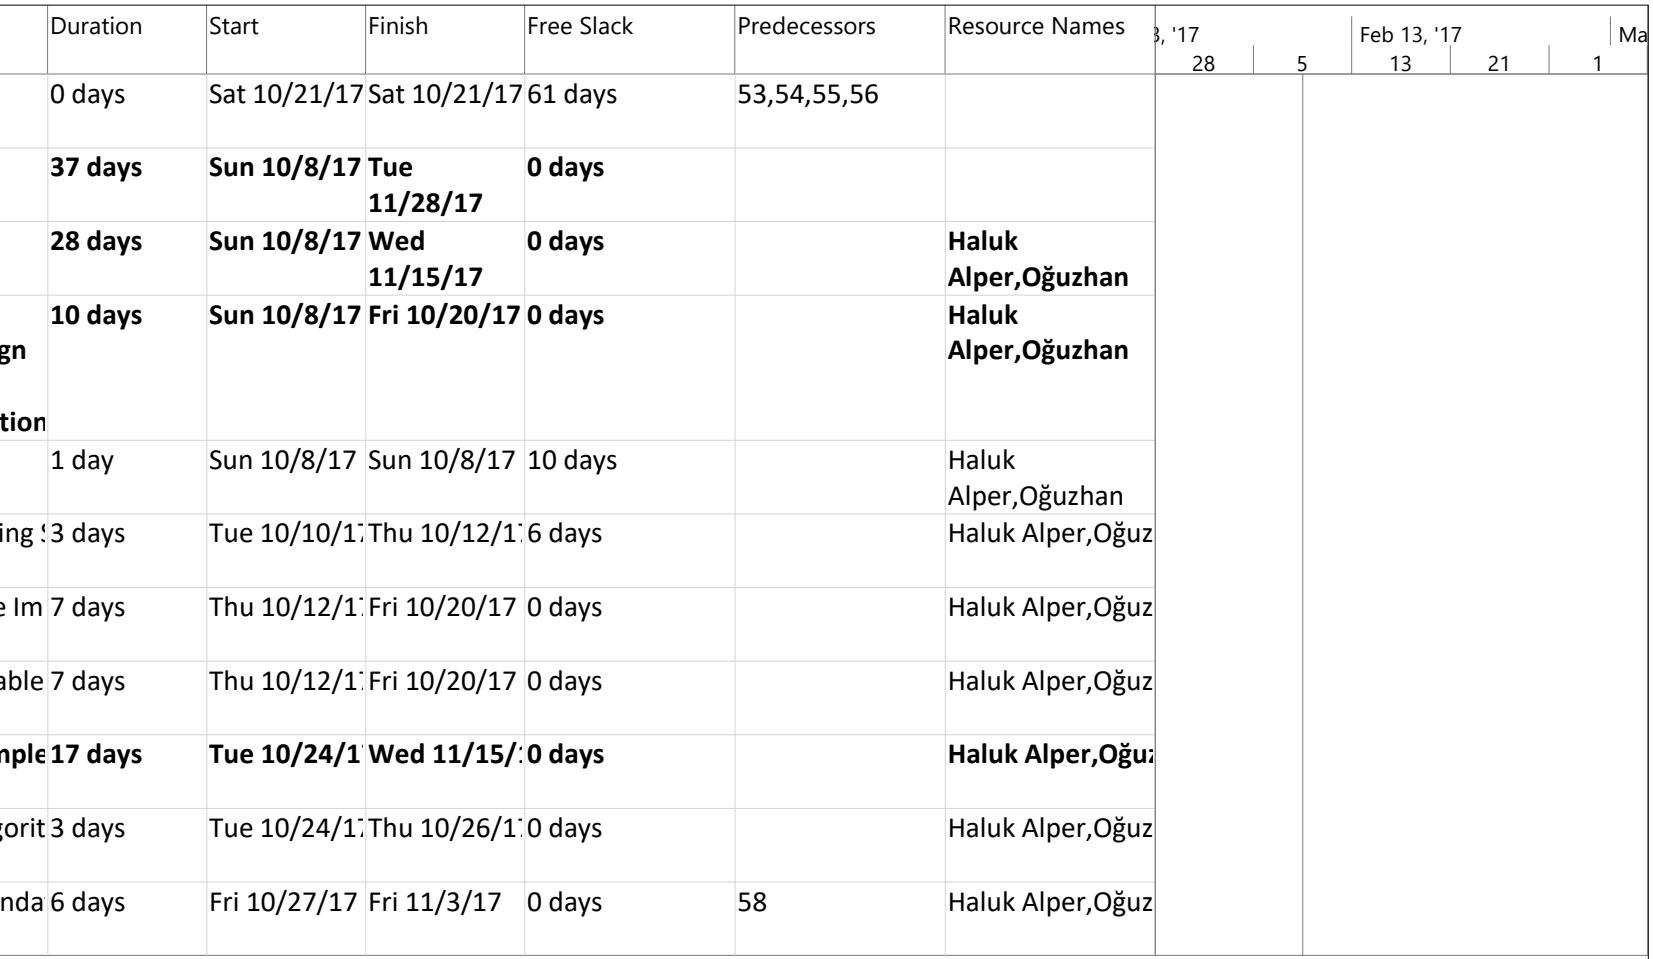

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

ID	Task Mode	Task Name	Duration	Start	Finish	Free Slack	Predecessors	Resource Names
60		Notifications A	5 days	Mon 11/6/17	Fri 11/10/17	0 days	59	Haluk Alper,Oğuz
61		Concert Info A	3 days	Mon 11/13/1	Wed 11/15/1	42 days	60	Haluk Alper,Oğuz
62		**Front-End Develop**	**36 days**	**Tue 10/10/1**	**Tue 11/28/1**	**0 days**		
63		**Web Developments**	**36 days**	**Tue 10/10/17**	**Tue 11/28/17**	**0 days**		**Kemal Berk,Bekir**
64		Git Connectio	2 days	Tue 10/10/1	Wed 10/11/1	0 days		Kemal Berk,Bekir
65		jsp Connectio	3 days	Thu 10/12/1	Mon 10/16/1	0 days	64	Kemal Berk,Bekir
66		Login Page Im	5 days	Tue 10/17/1	Mon 10/23/1	0 days	65	Kemal Berk,Bekir
67		Search Page Ir	5 days	Tue 10/24/1	Mon 10/30/1	0 days	66	Kemal Berk,Bekir
68		Notifications F	6 days	Tue 10/31/1	Tue 11/7/17	0 days	67	Kemal Berk,Bekir
69		Search Results	5 days	Wed 11/8/17	Tue 11/14/1	0 days	68	Kemal Berk,Bekir
70		User Page Imp	5 days	Wed 11/15/1	Tue 11/21/1	0 days	69	Kemal Berk,Bekir
71		Concert Page	5 days	Wed 11/22/1	Tue 11/28/1	33 days	70	Kemal Berk,Bekir

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

ID	Task Mode	Task Name	Duration	Start	Finish	Free Slack	Predecessors	Resource Names
72		**Android Developm**	**36 days**	**Tue 10/10/1**	**Tue 11/28/1**	**0 days**		**Elif,Furkan**
73		Build a workspac	1 day	Tue 10/10/1	Tue 10/10/1	0 days		Elif,Furkan
74		Login Page Imple	8 days	Wed 10/11/1	Fri 10/20/17	0 days	73	Elif,Furkan
75		Concert Page Im	14 days	Mon 10/23/1	Thu 11/9/17	0 days	74	Elif,Furkan
76		User Profile Impl	5 days	Fri 11/10/17	Thu 11/16/1	0 days	75	Elif,Furkan
77		Database Conne	8 days	Fri 11/17/17	Tue 11/28/1	33 days	76	Elif,Furkan
78		Designing Android and Web UI	0 days	Fri 11/17/17	Fri 11/17/17	41 days	76	
79		**Documentation**	**9 days**	**Thu 11/16/1**	**Wed 11/29/**	**0 days**		
80		Project Process Do	2 days	Thu 11/16/1	Fri 11/17/17	0 days		
81		Tutorial Creation	5 days	Mon 11/20/1	Fri 11/24/17	2 days	80	
82		Release	0 days	Wed 11/29/1	Wed 11/29/1	33 days	81	

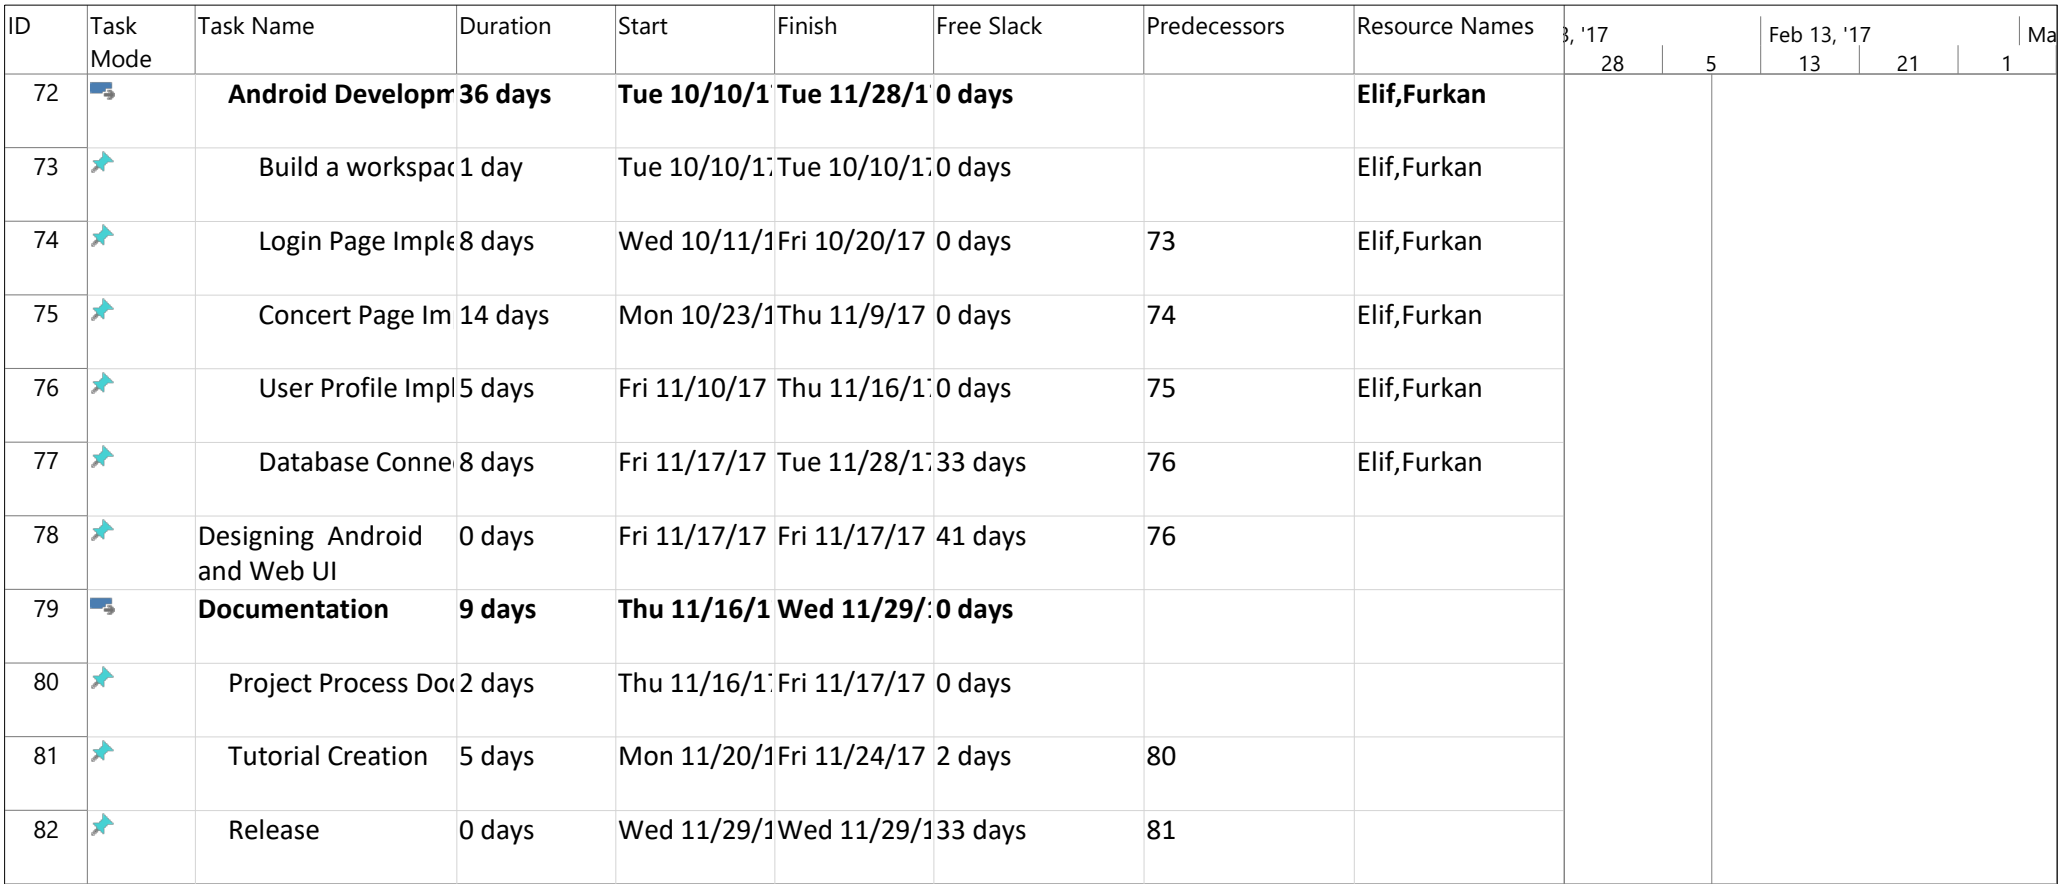

Project: Looking4Concerts
Date: Fri 4/7/17

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress
Slack

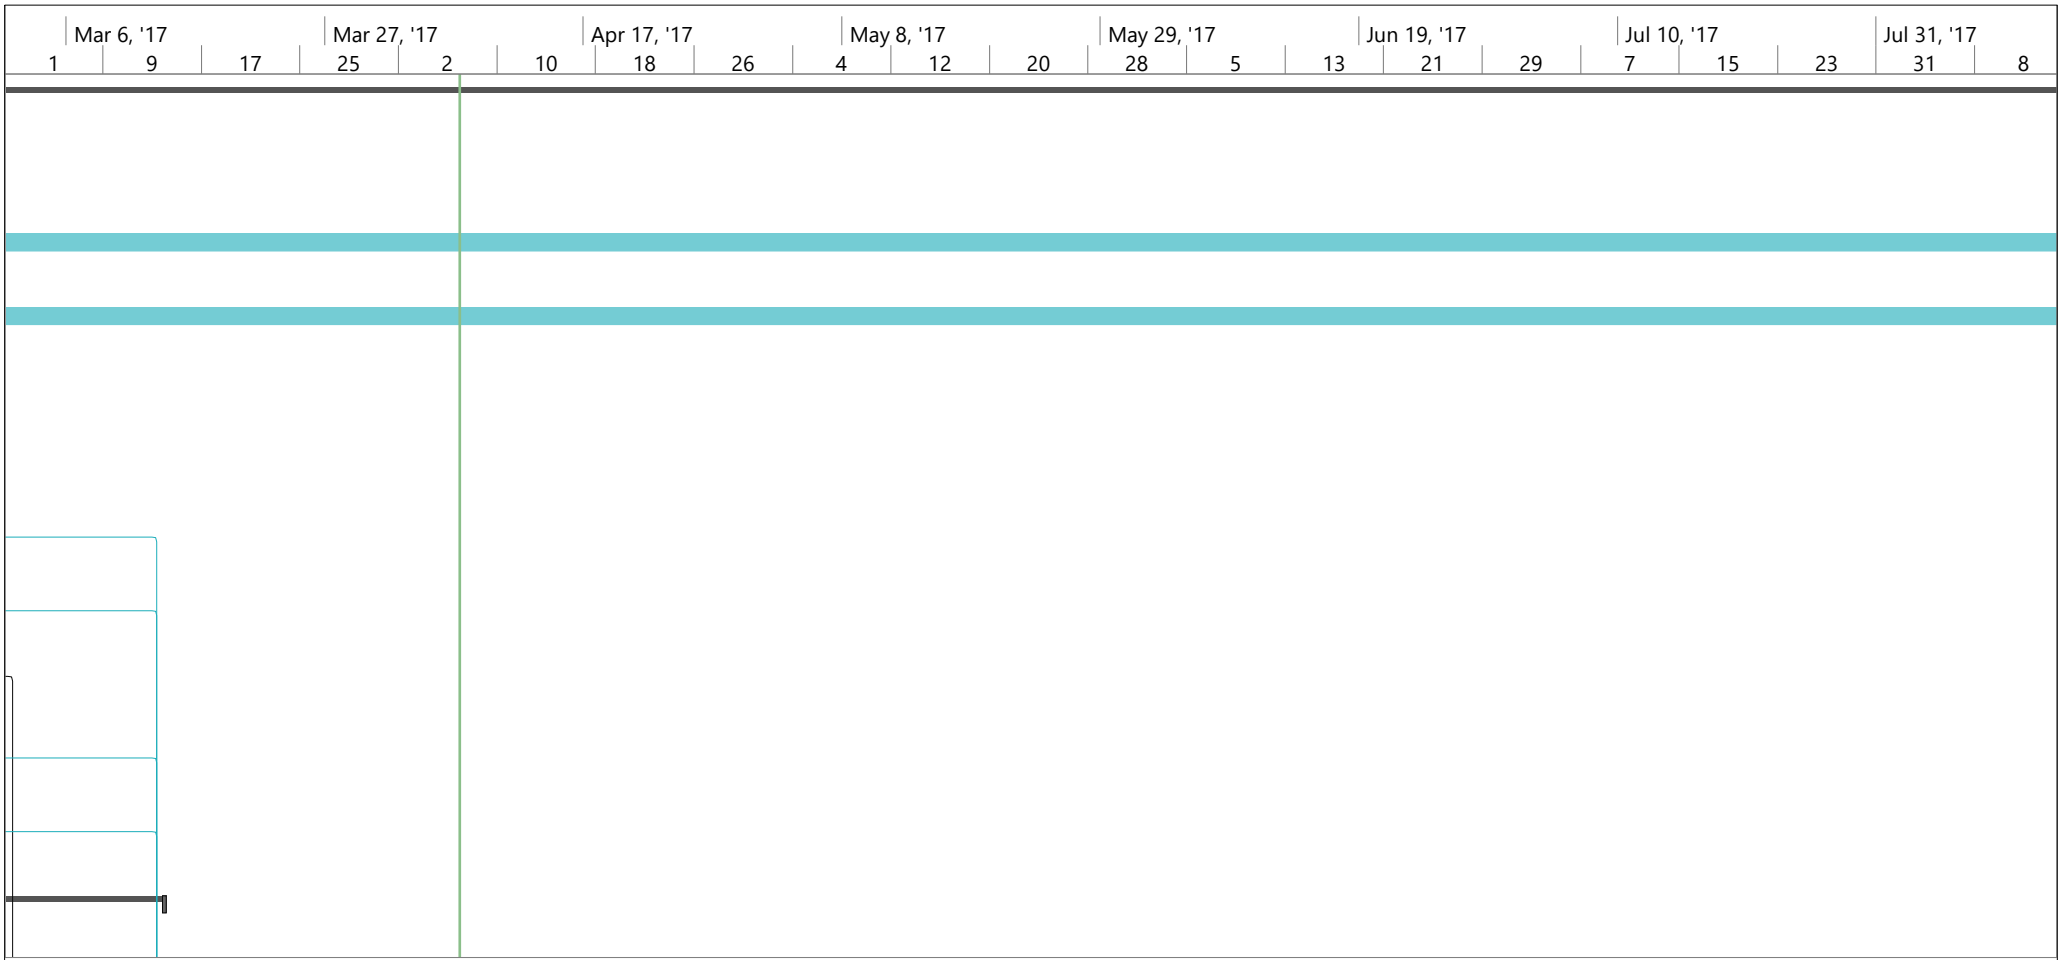

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

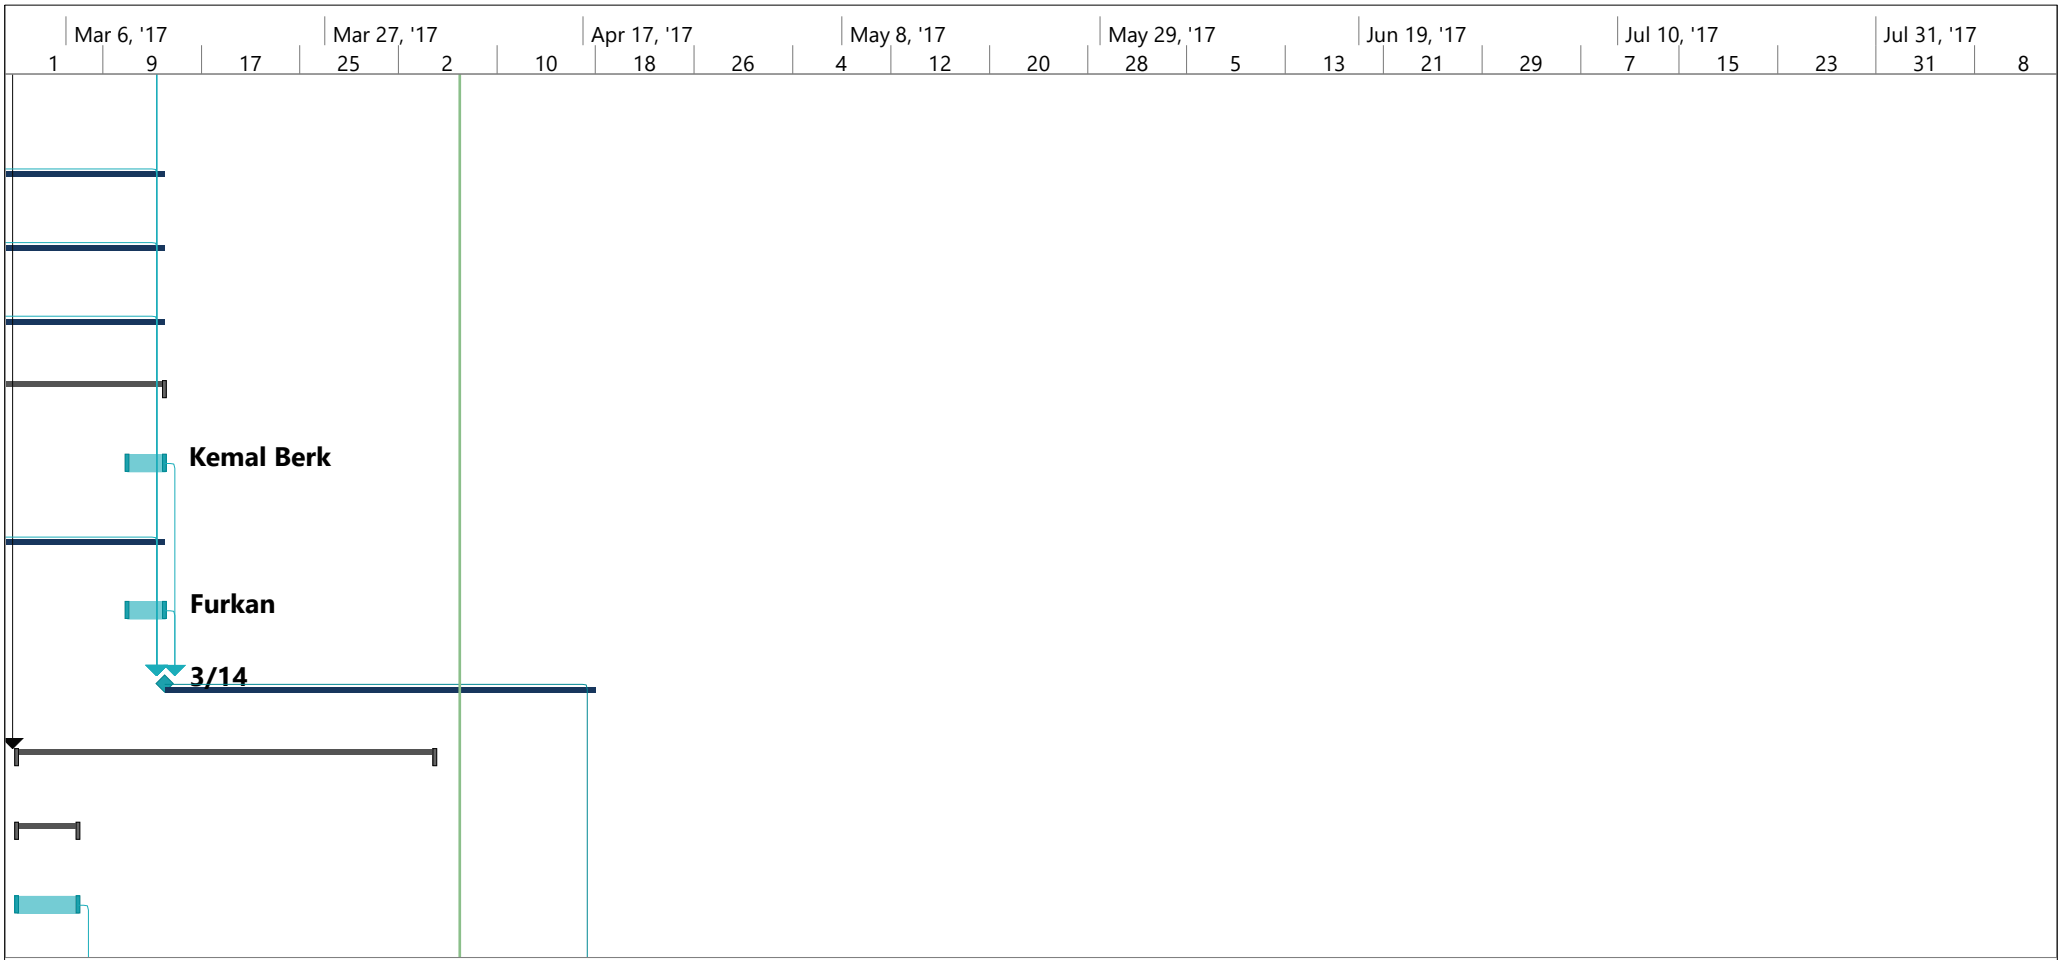

Project: Looking4Concerts
Date: Fri 4/7/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only		Slack	
Inactive Milestone		Finish-only			

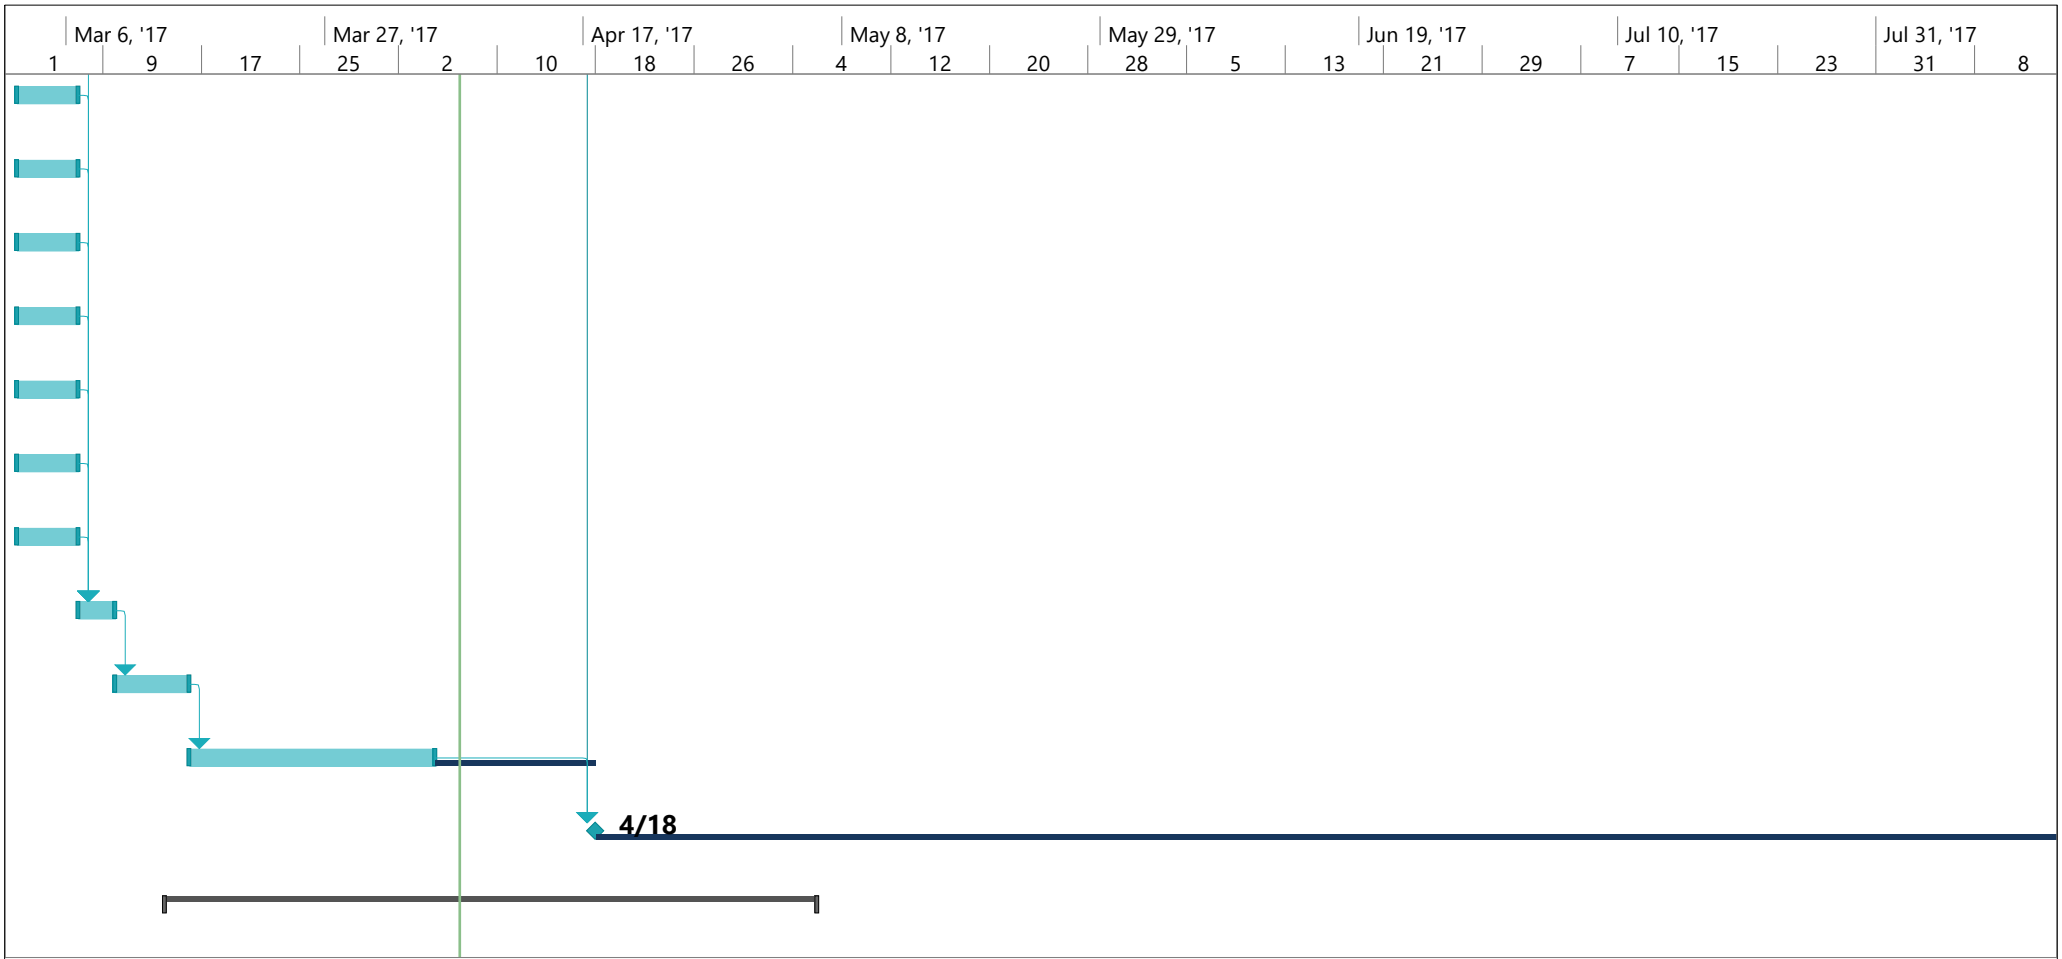

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

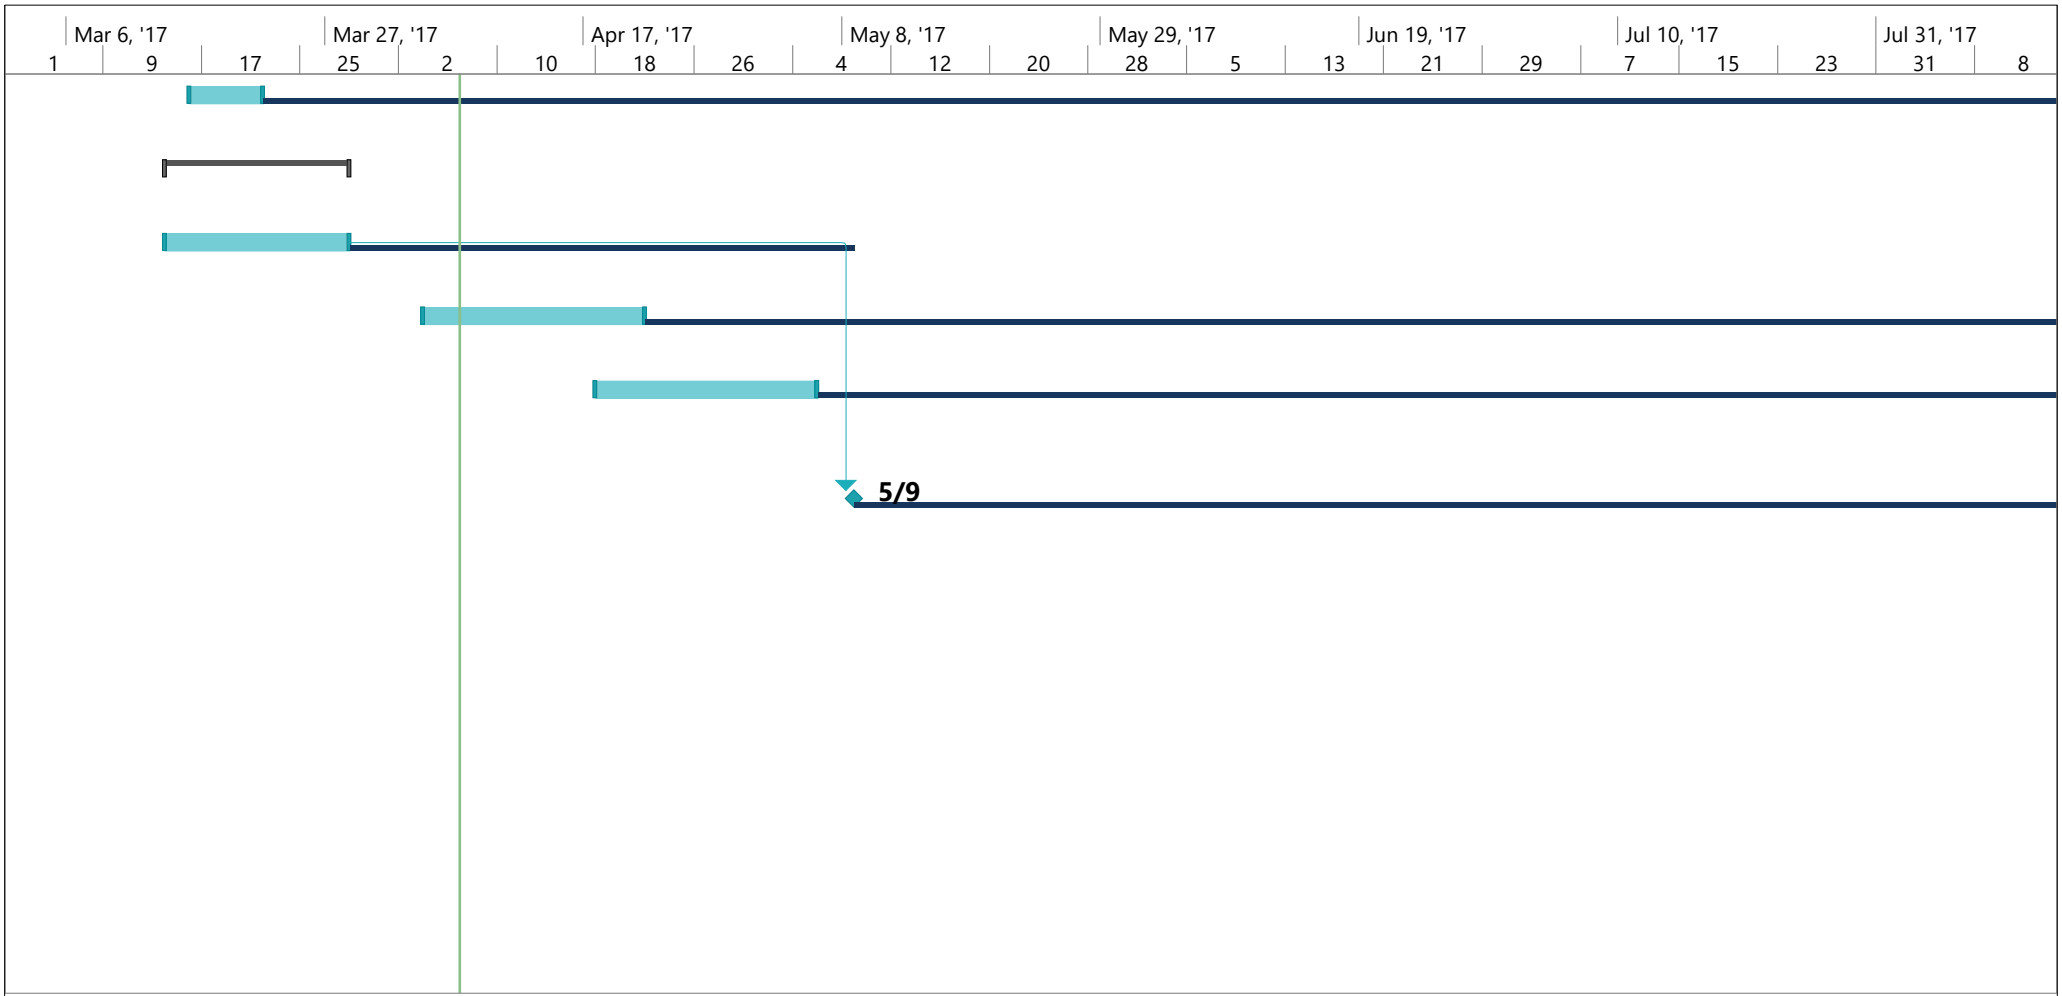

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

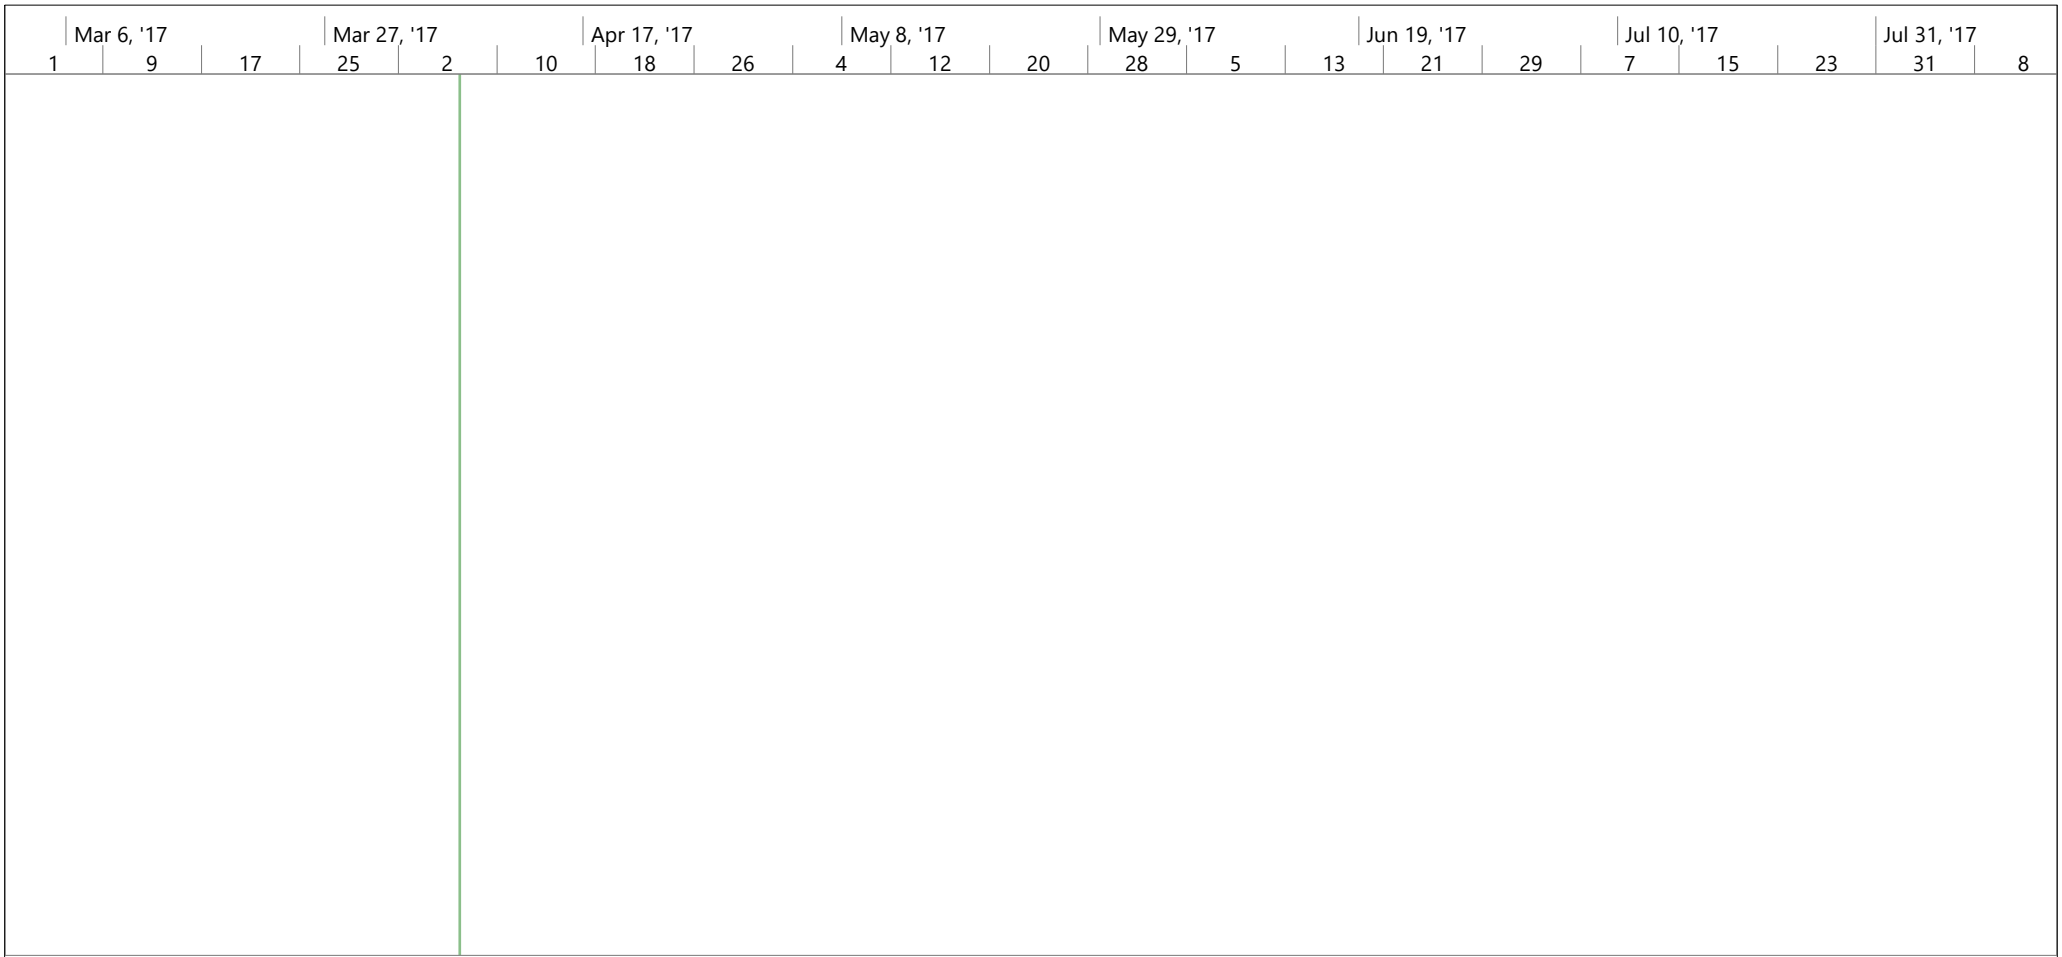

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

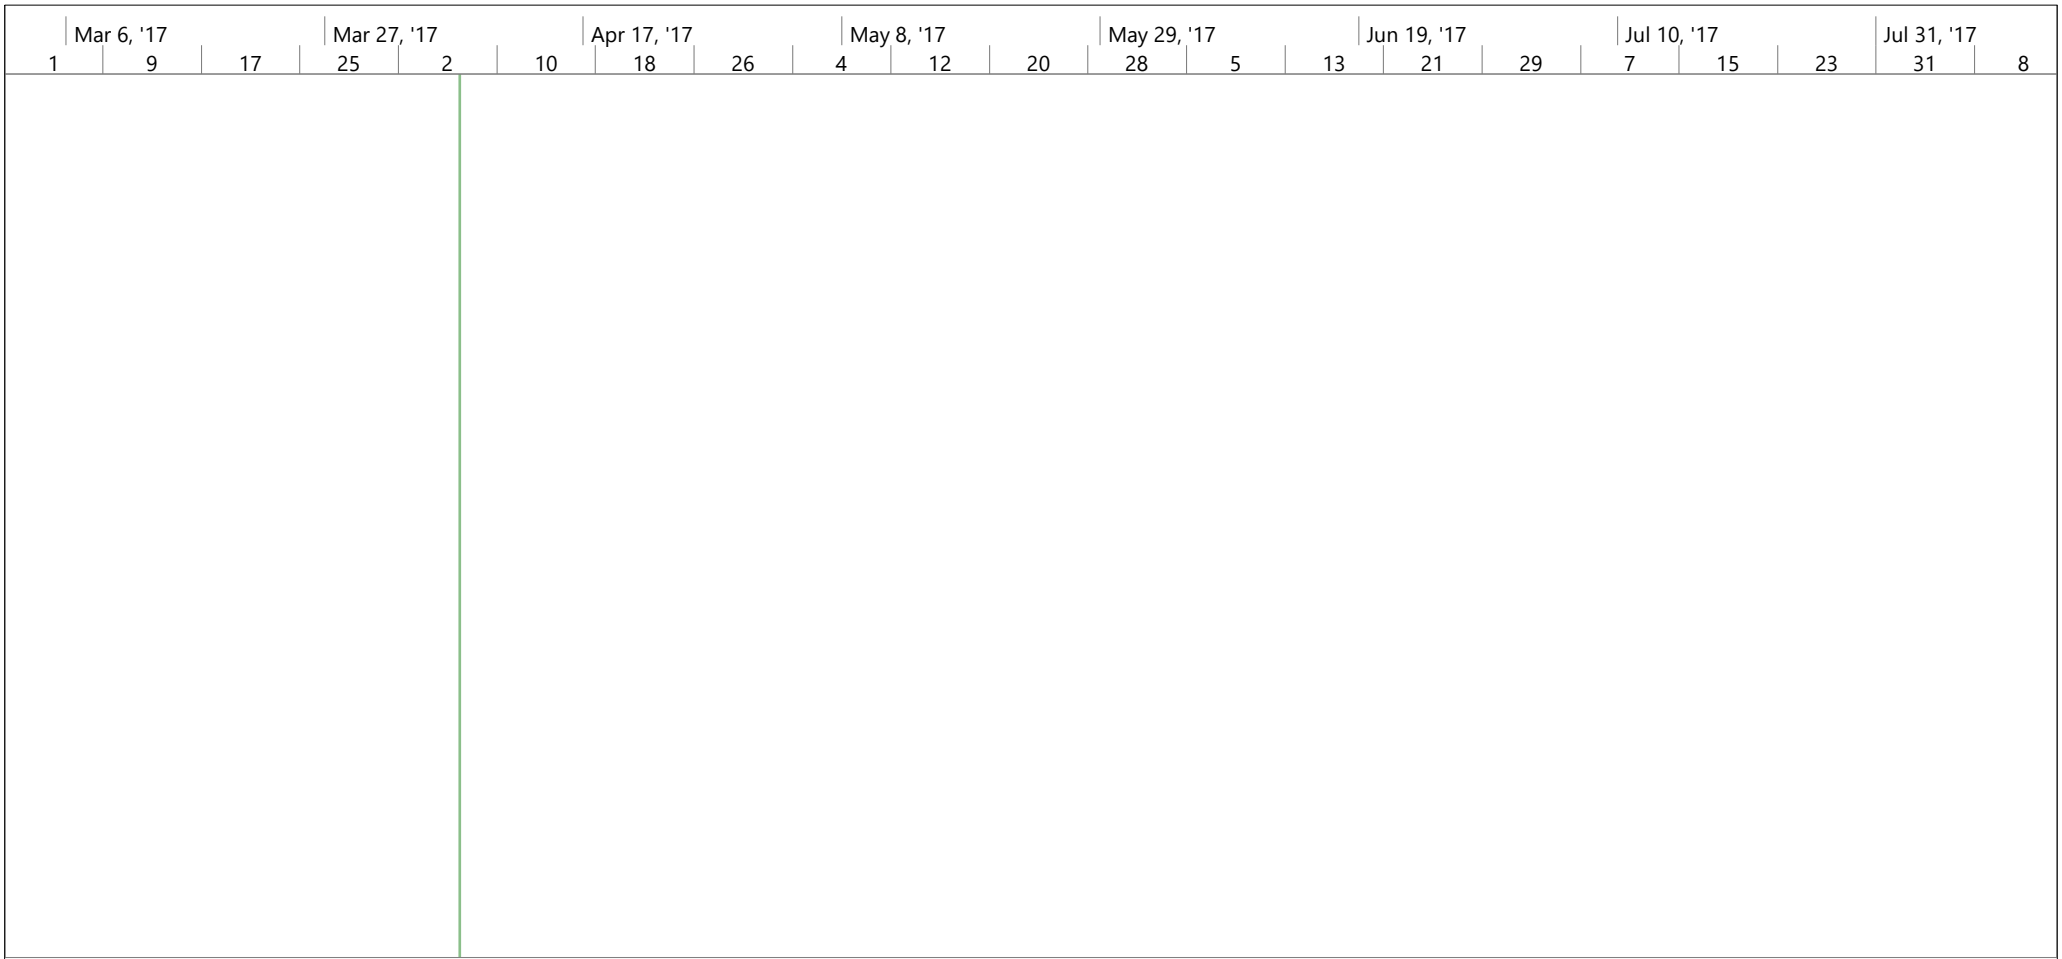

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

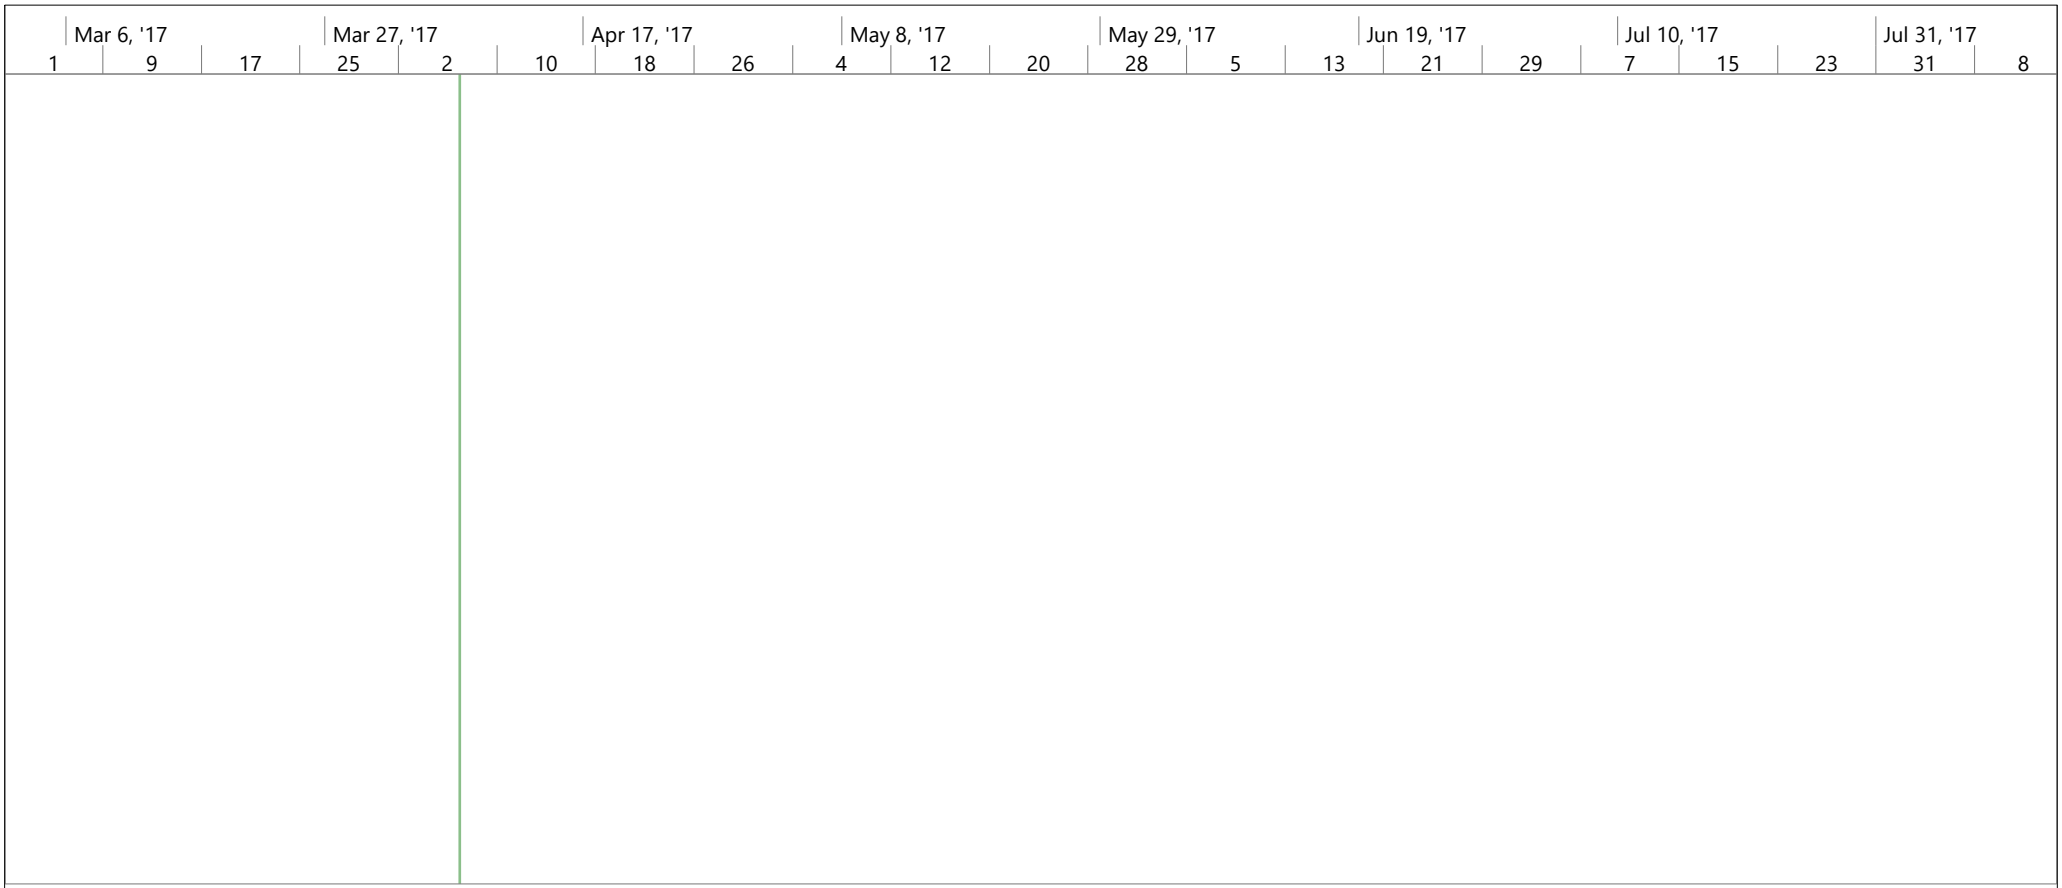

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

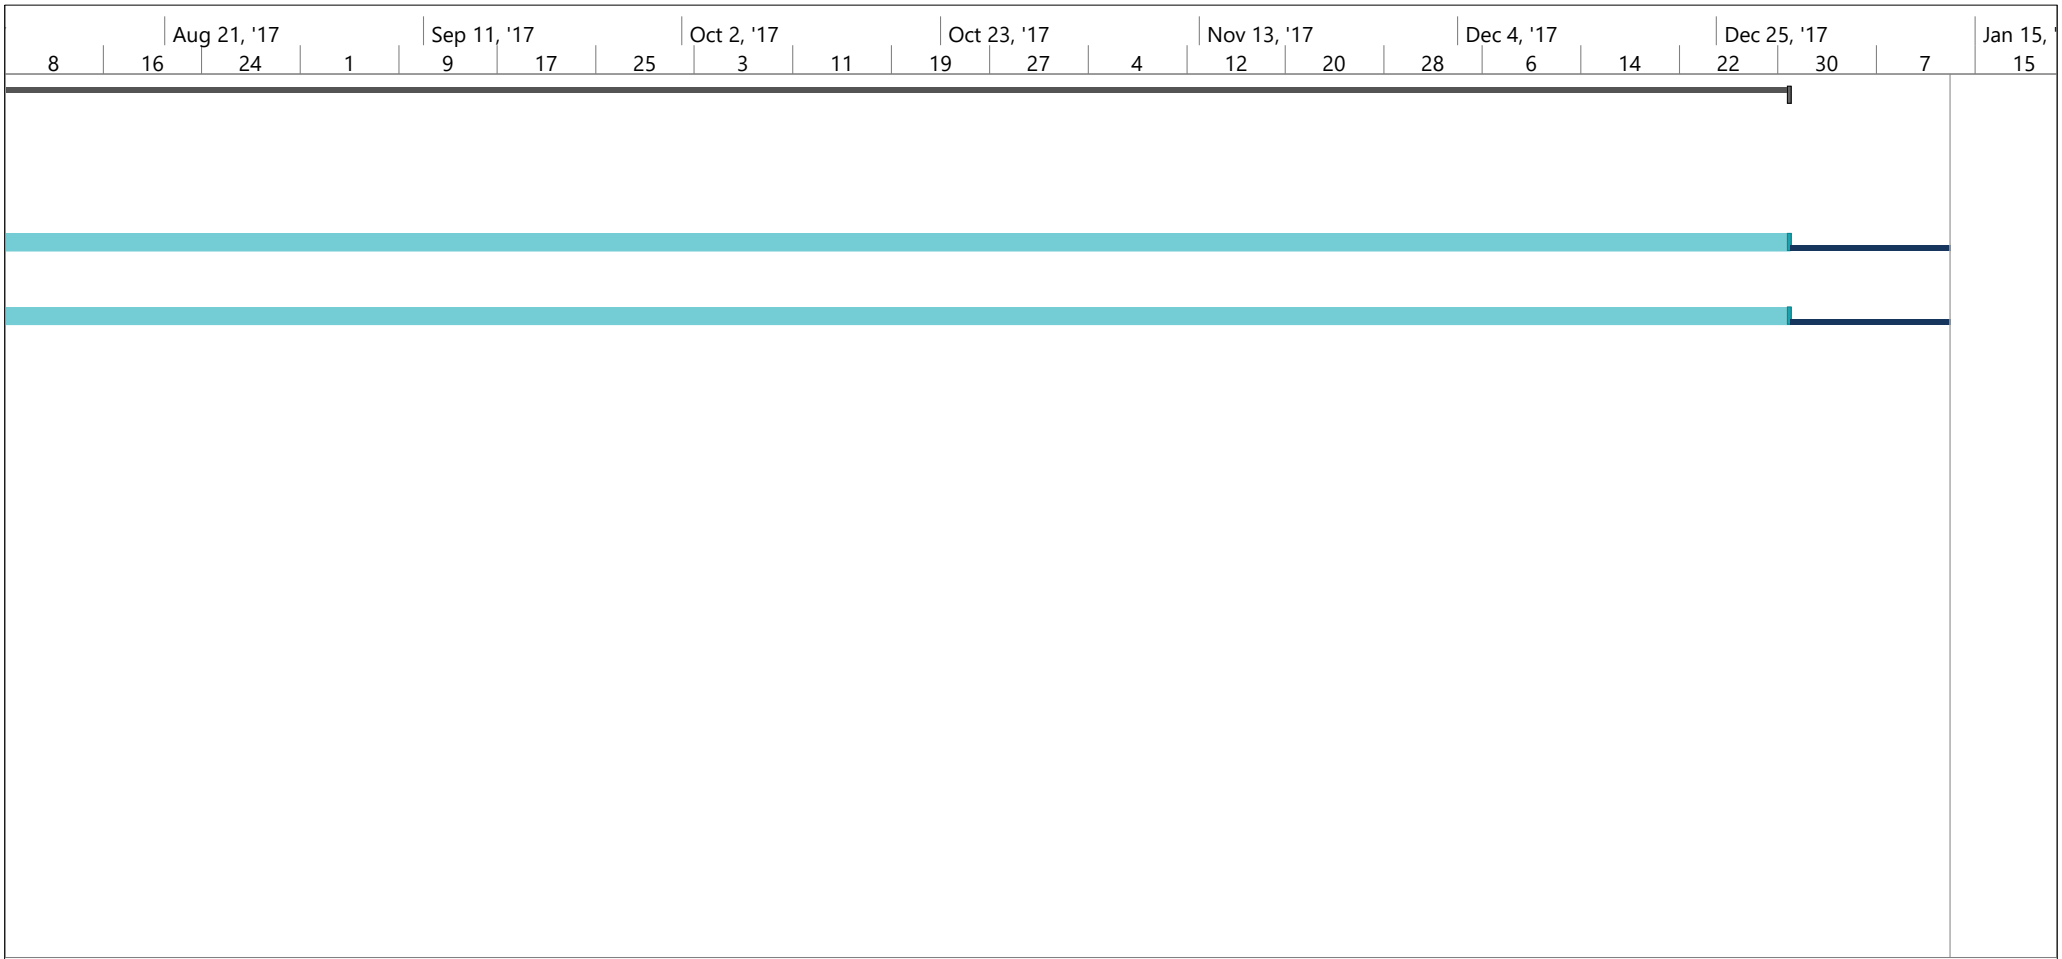

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

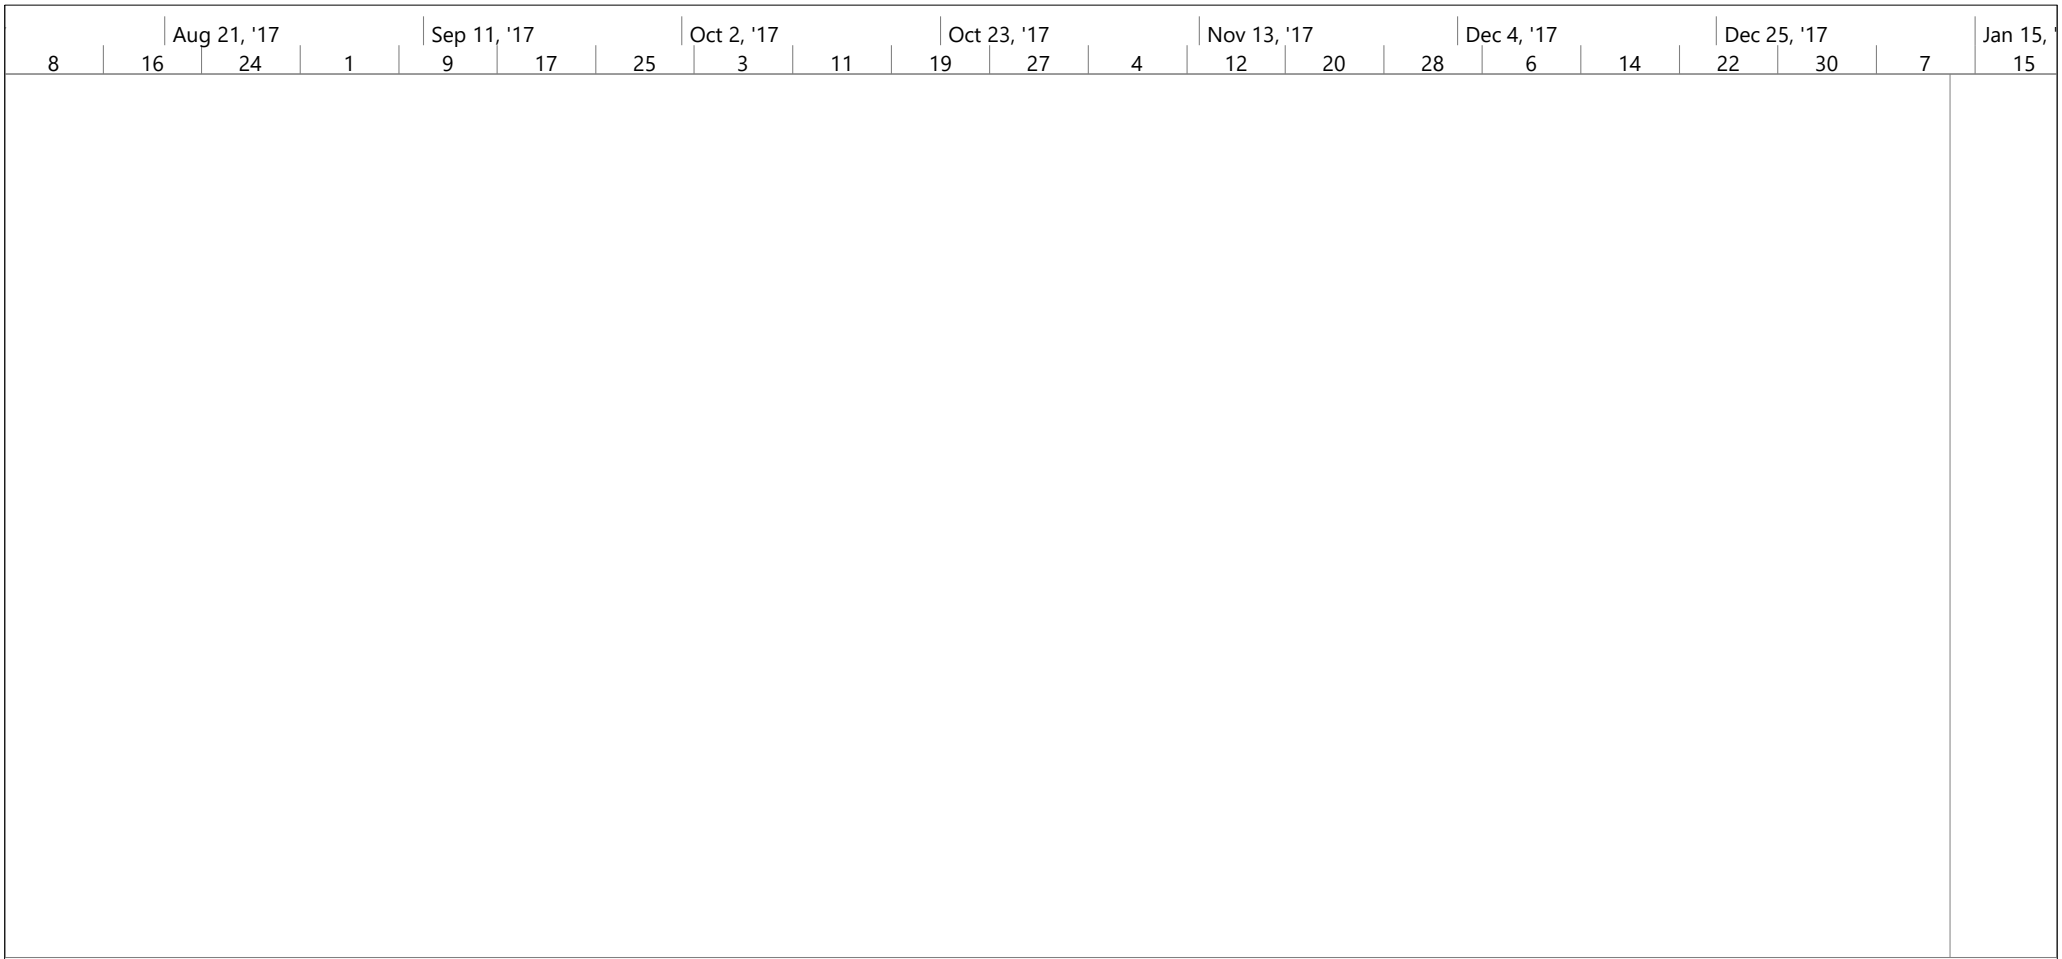

Project: Looking4Concerts
Date: Fri 4/7/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only		Slack	
Inactive Milestone		Finish-only			

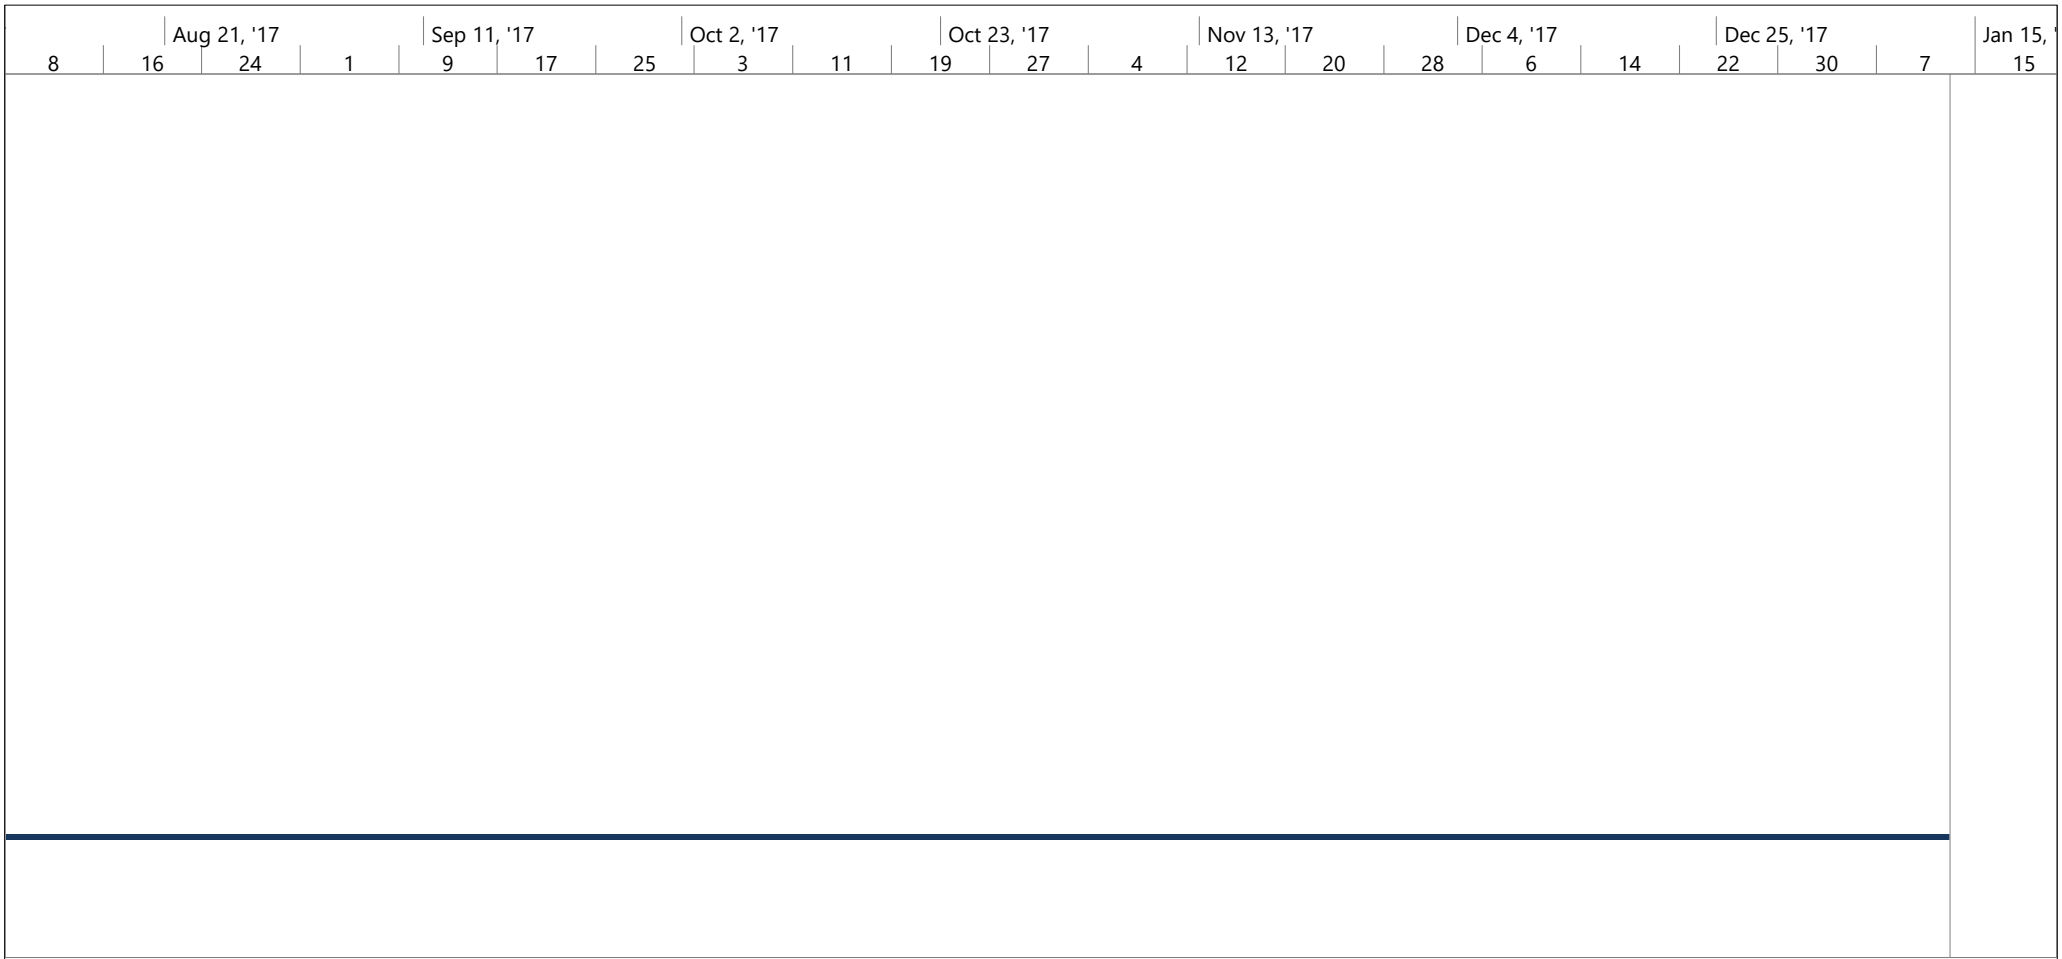

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

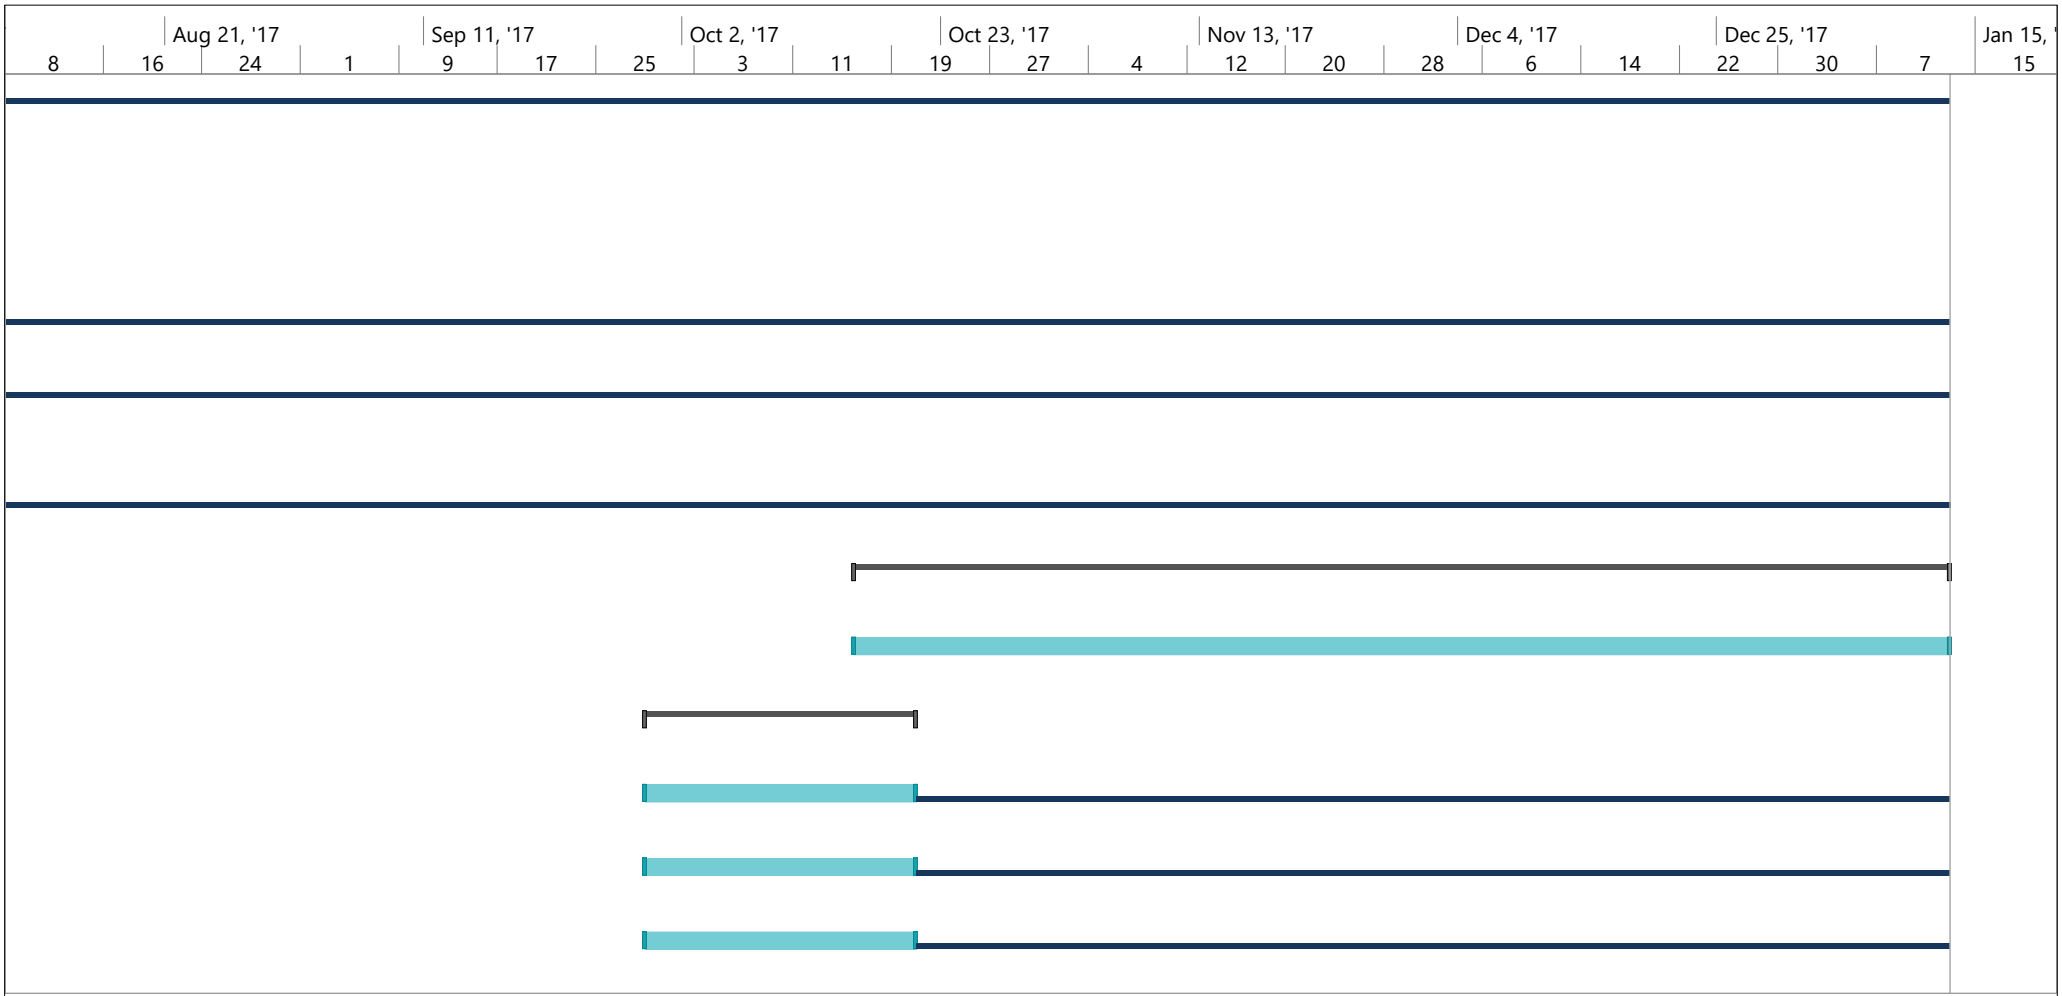

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

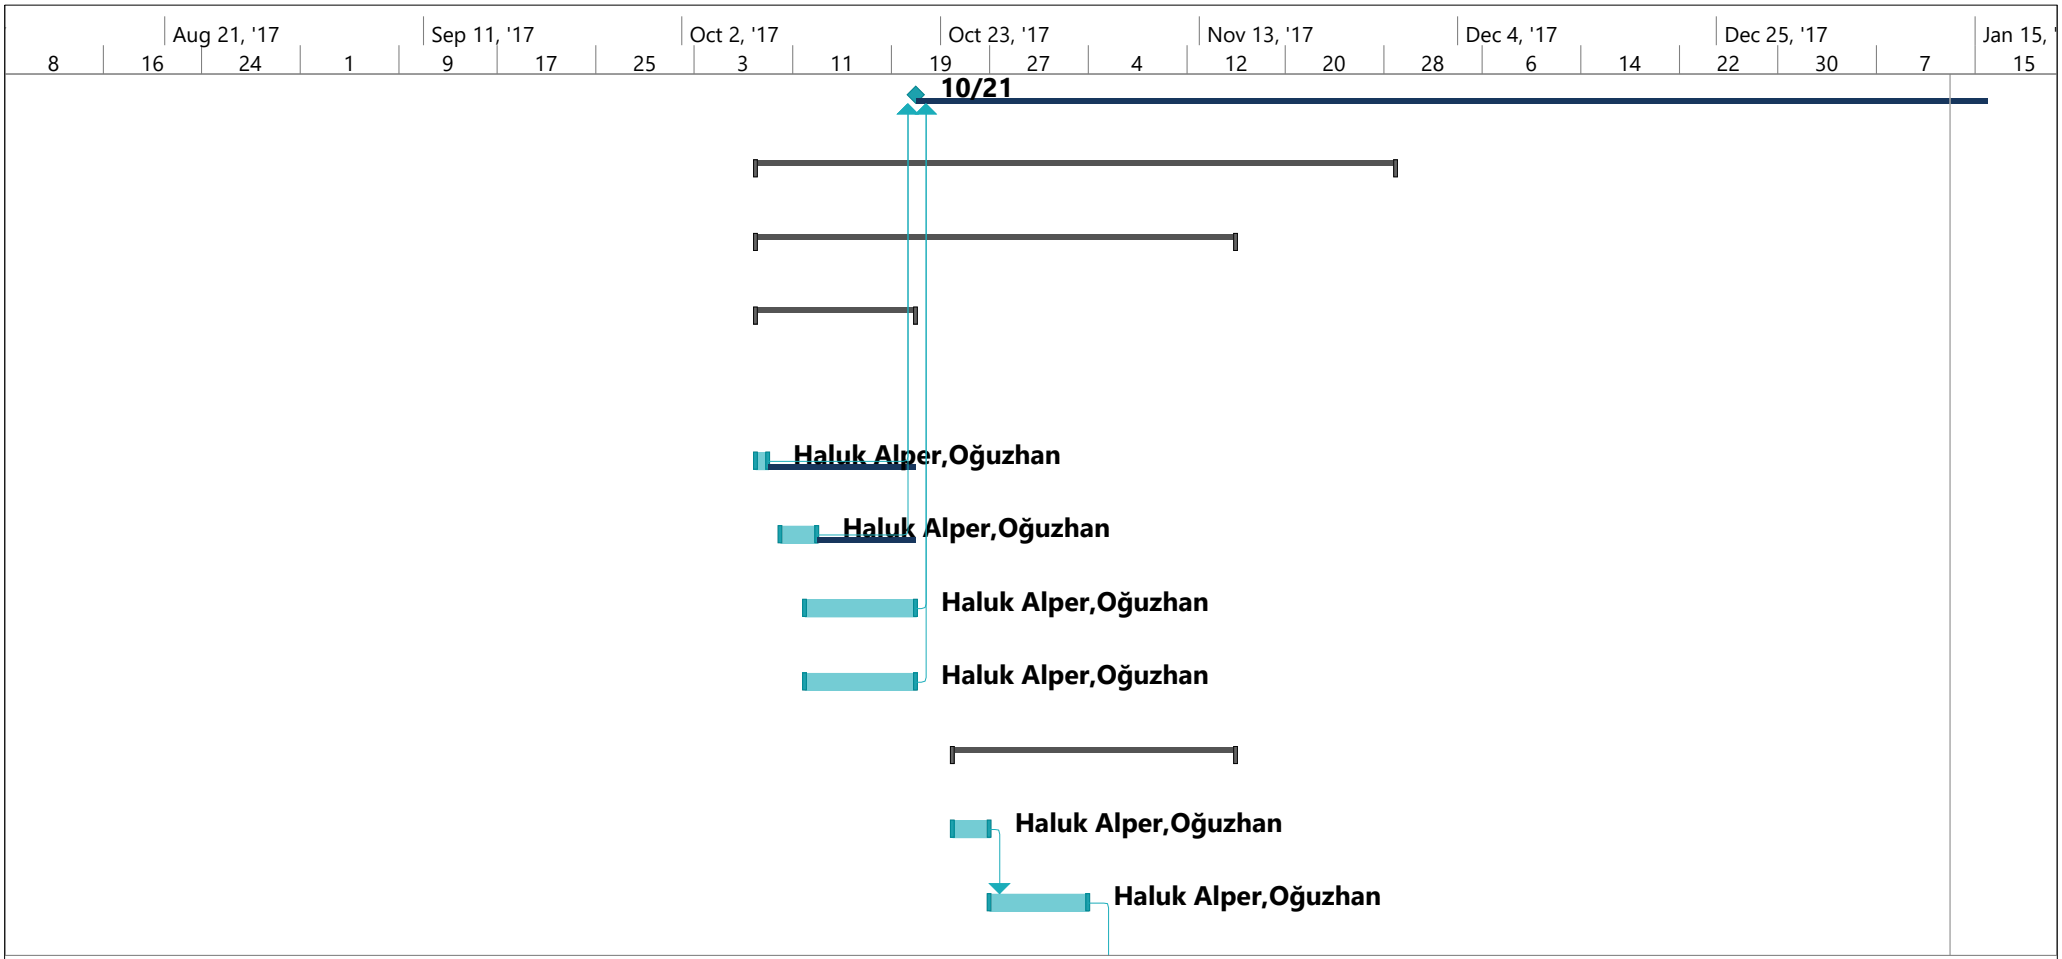

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

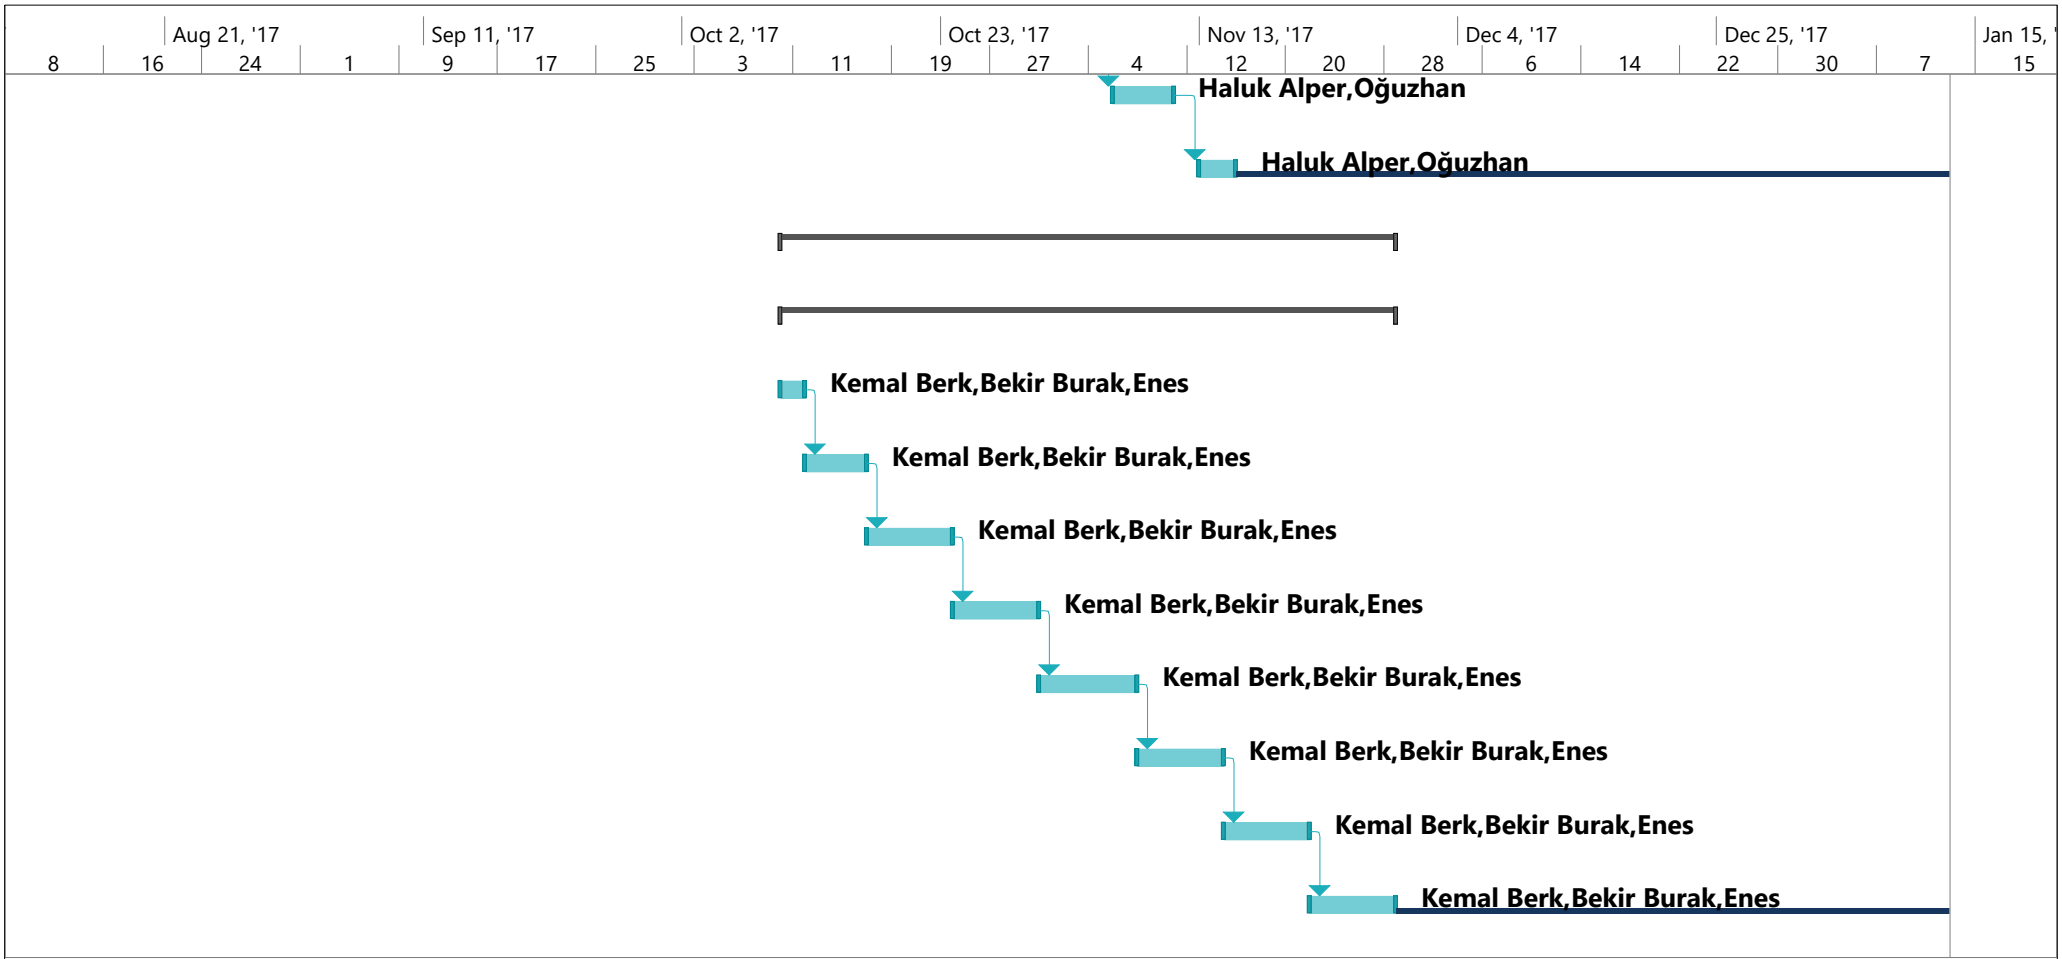

Project: Looking4Concerts
Date: Fri 4/7/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only		Slack	
Inactive Milestone		Finish-only			

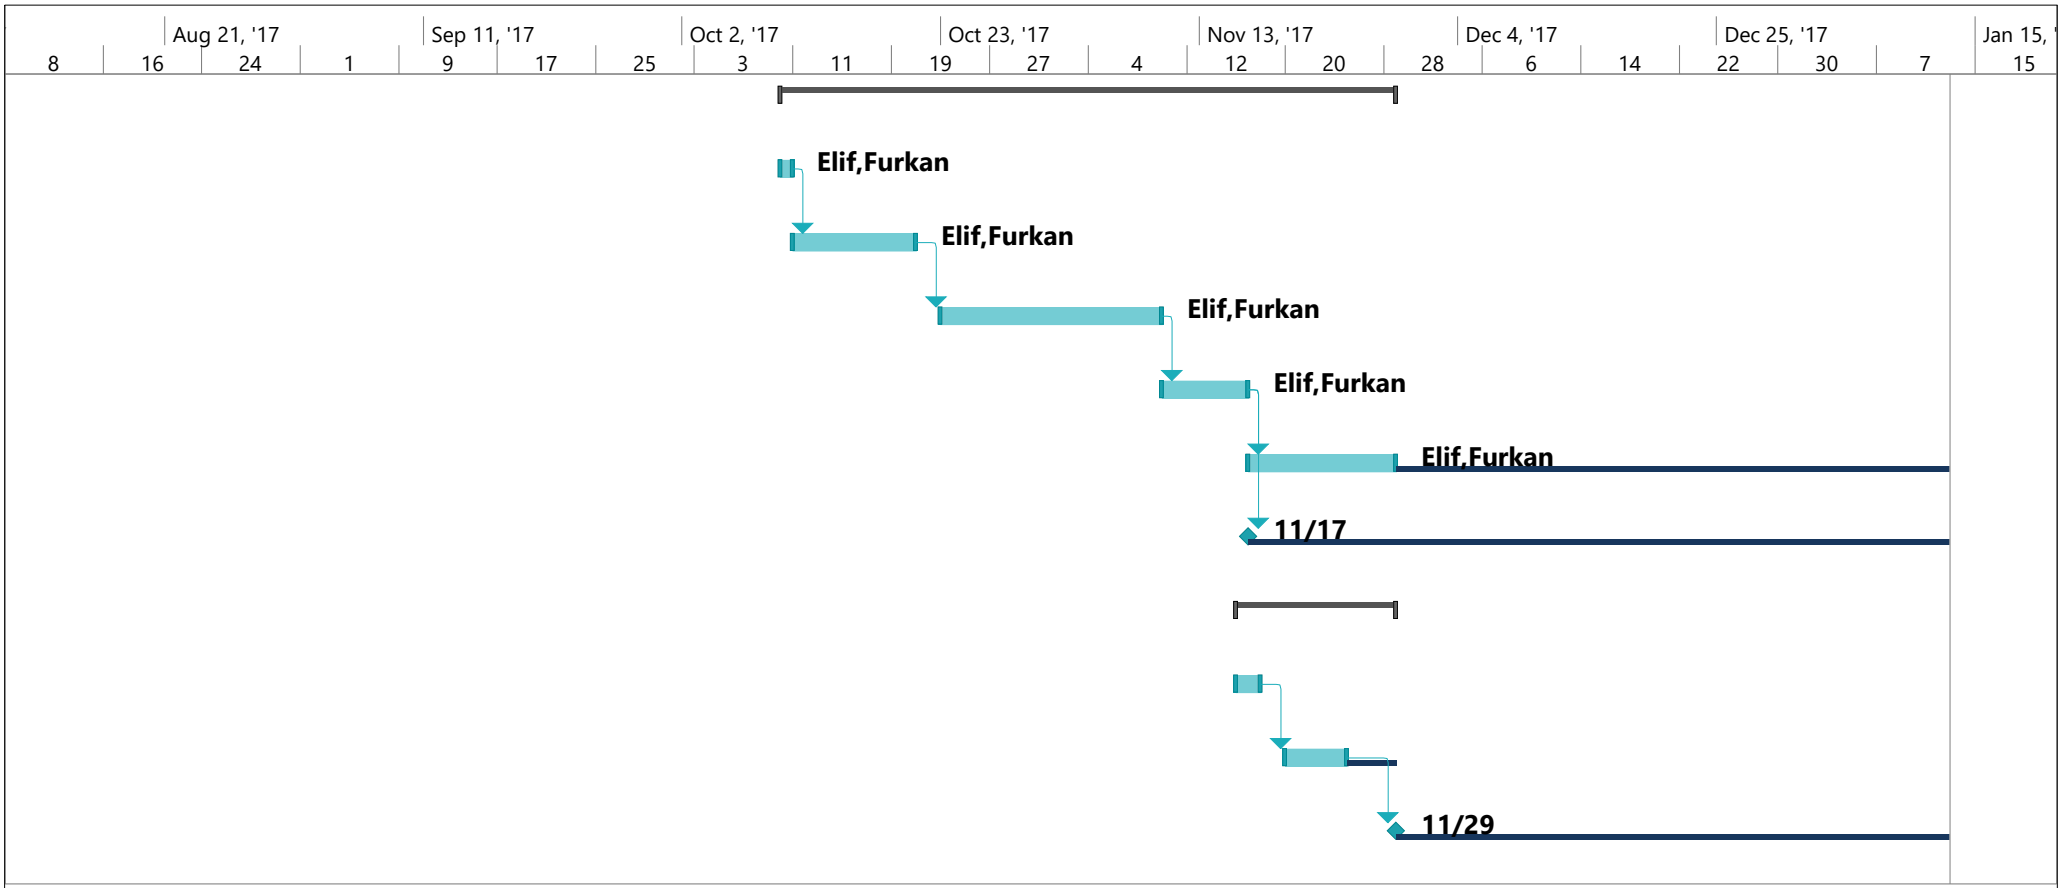

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

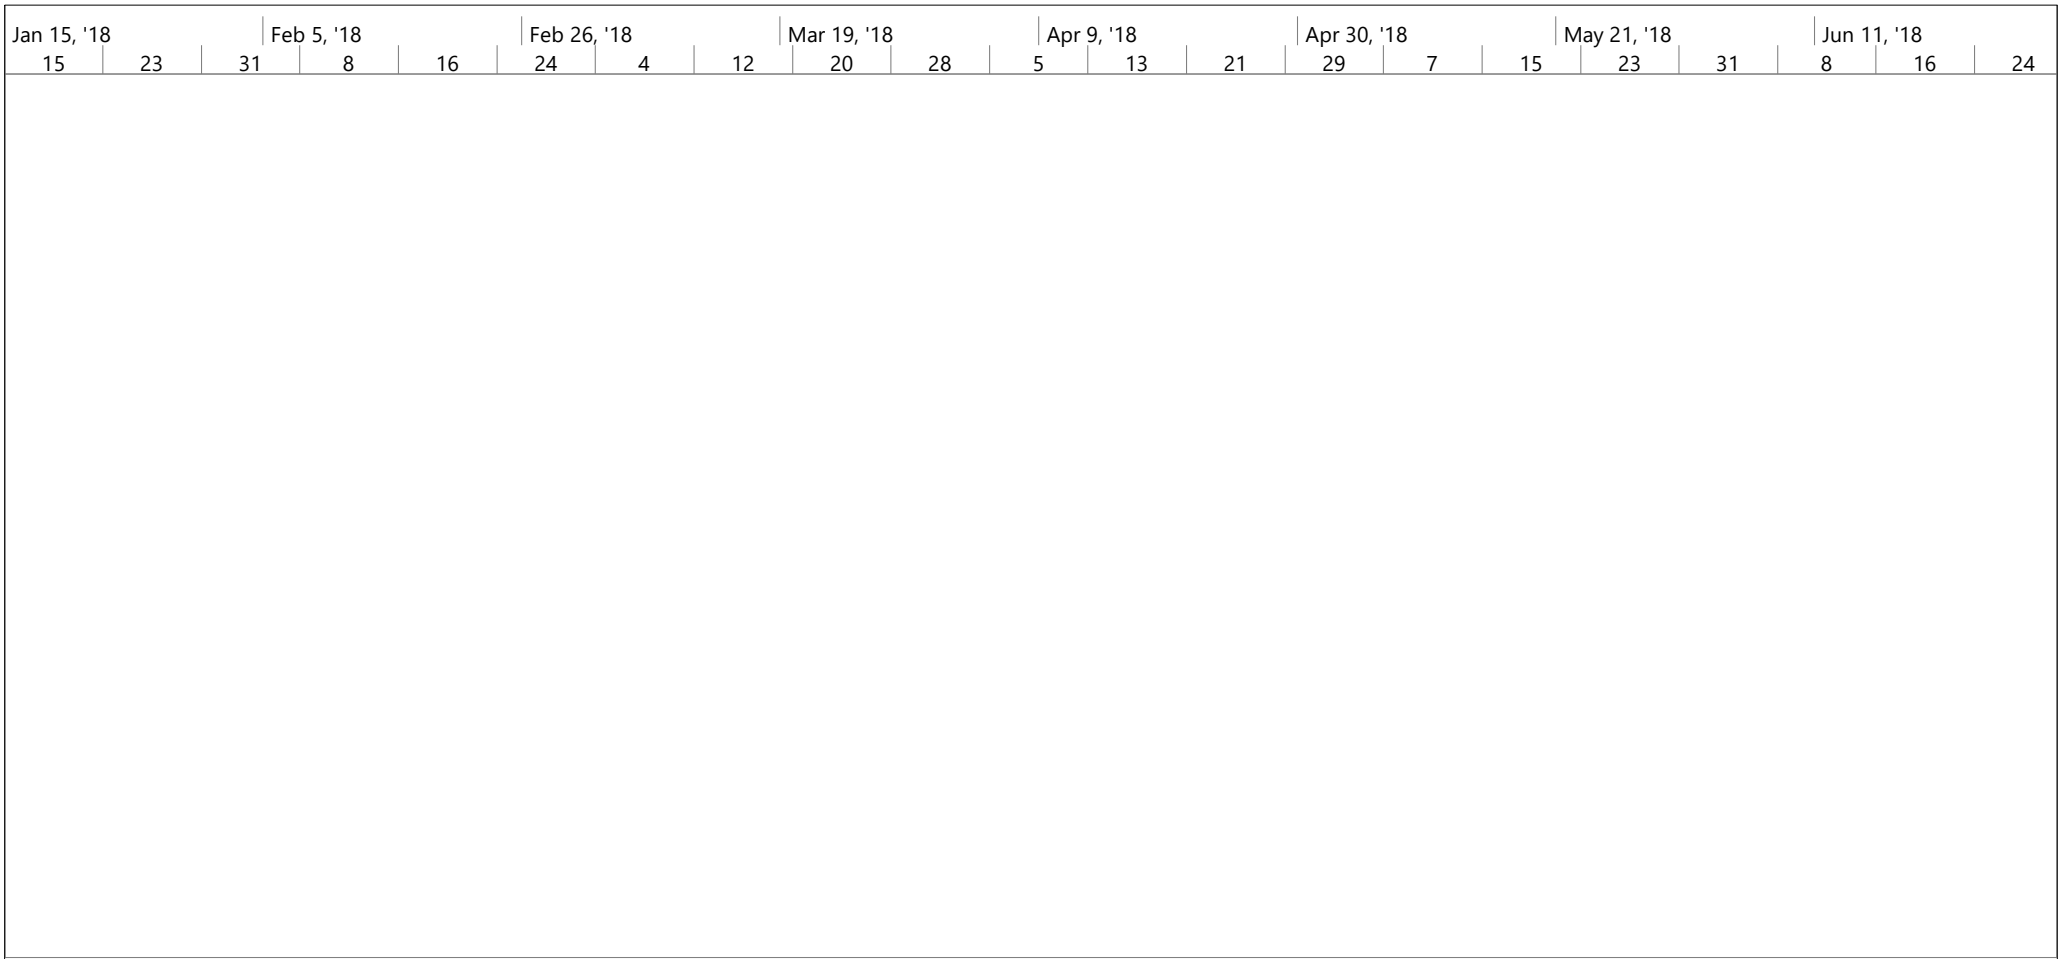

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

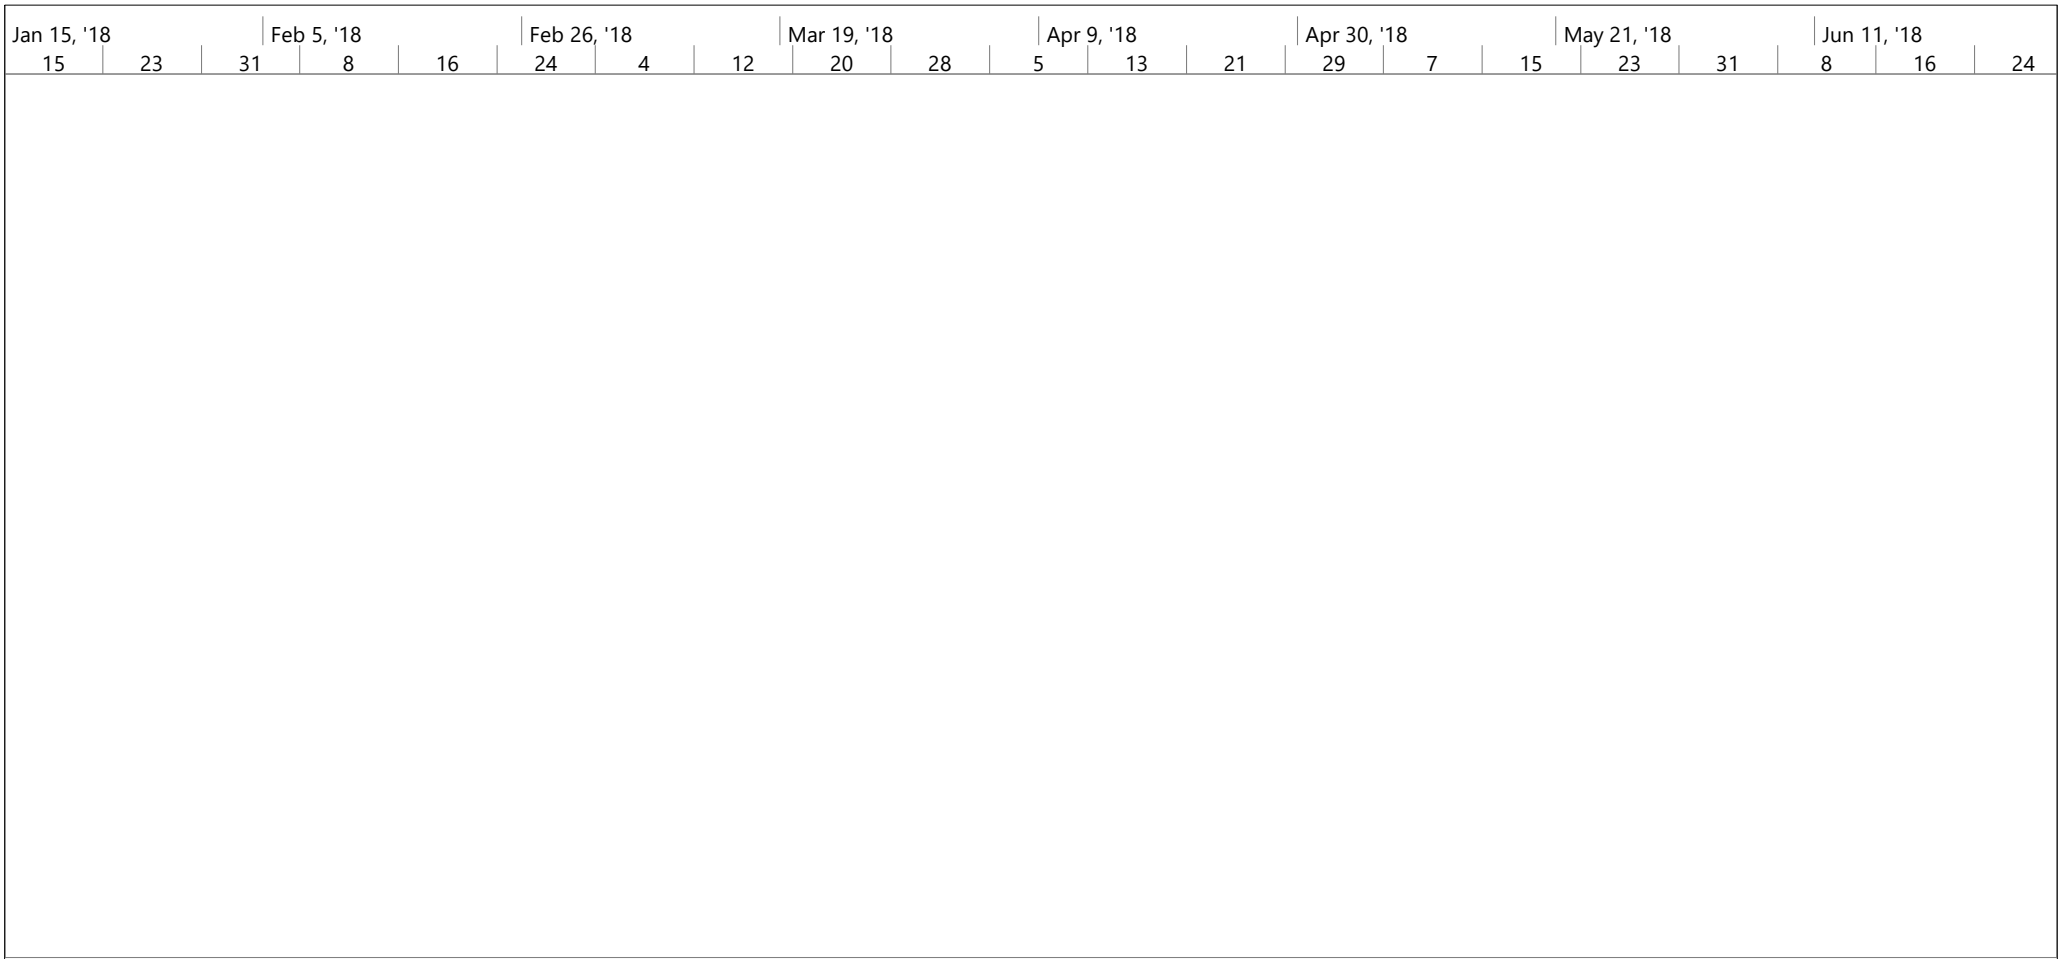

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

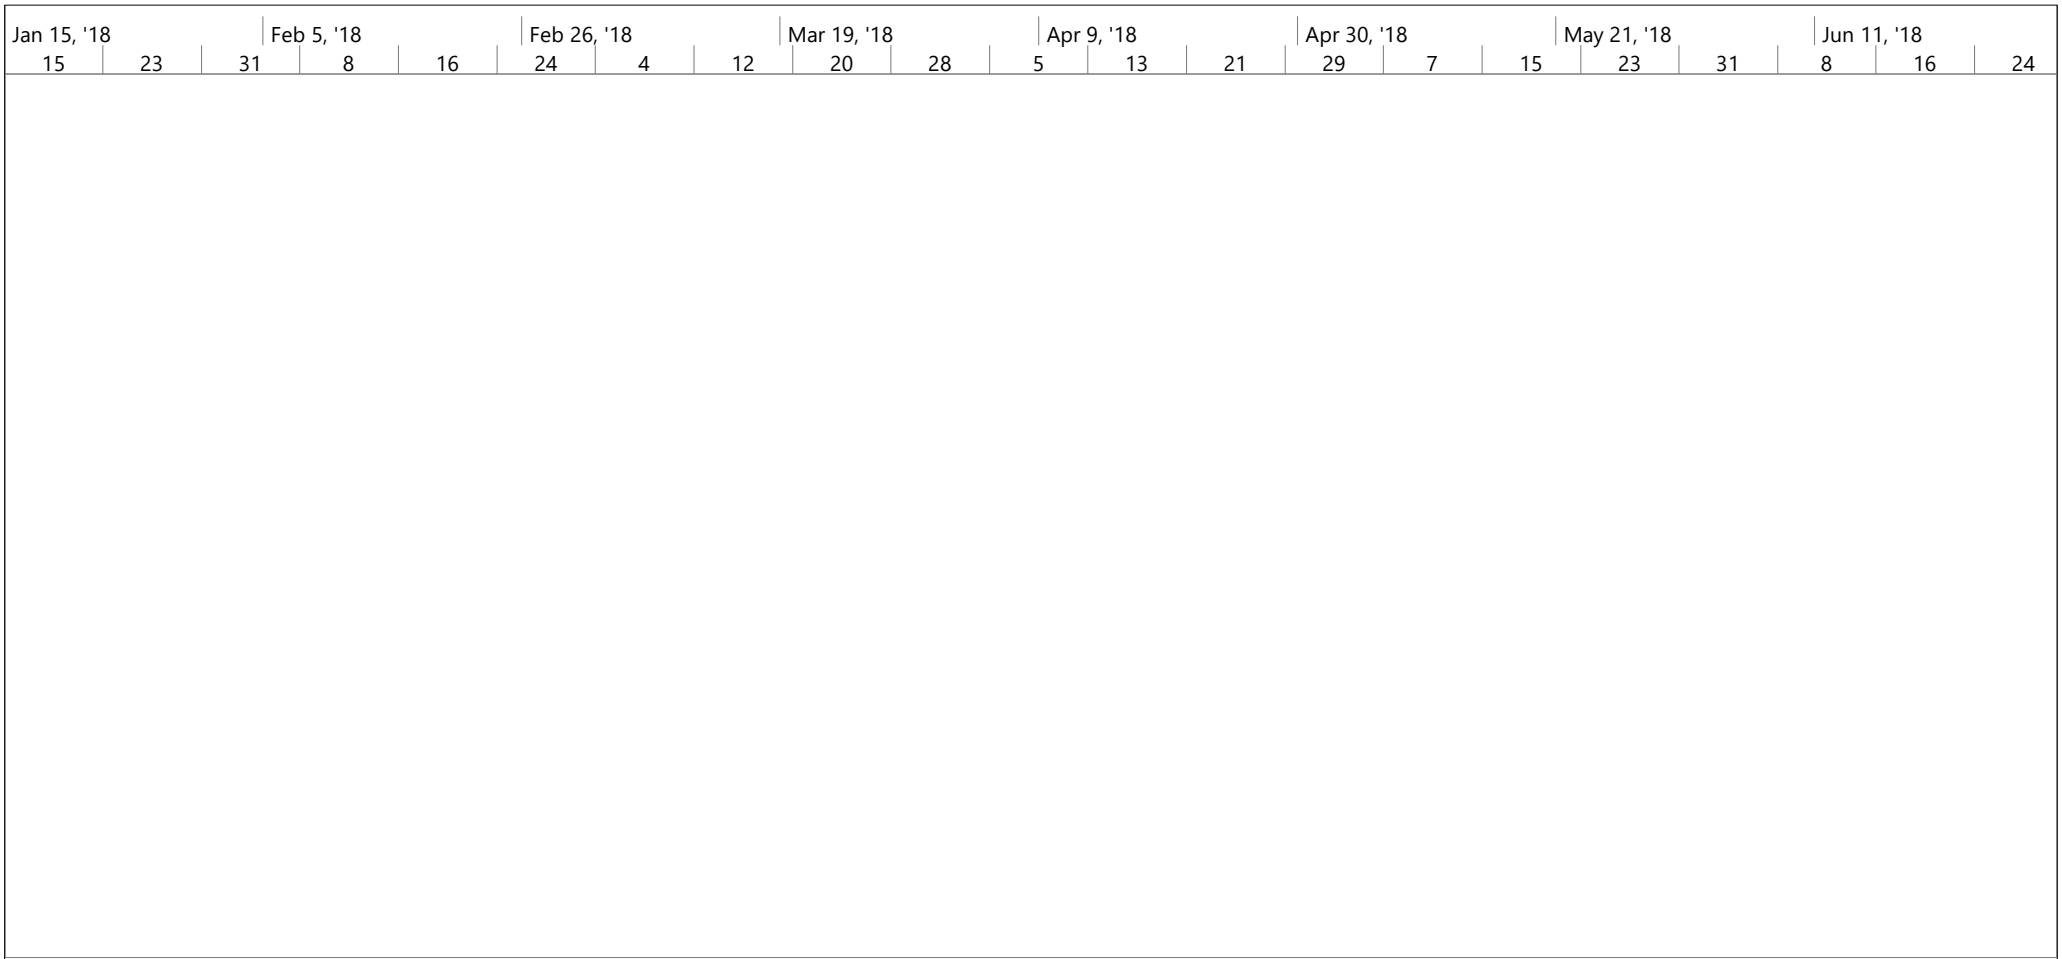

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

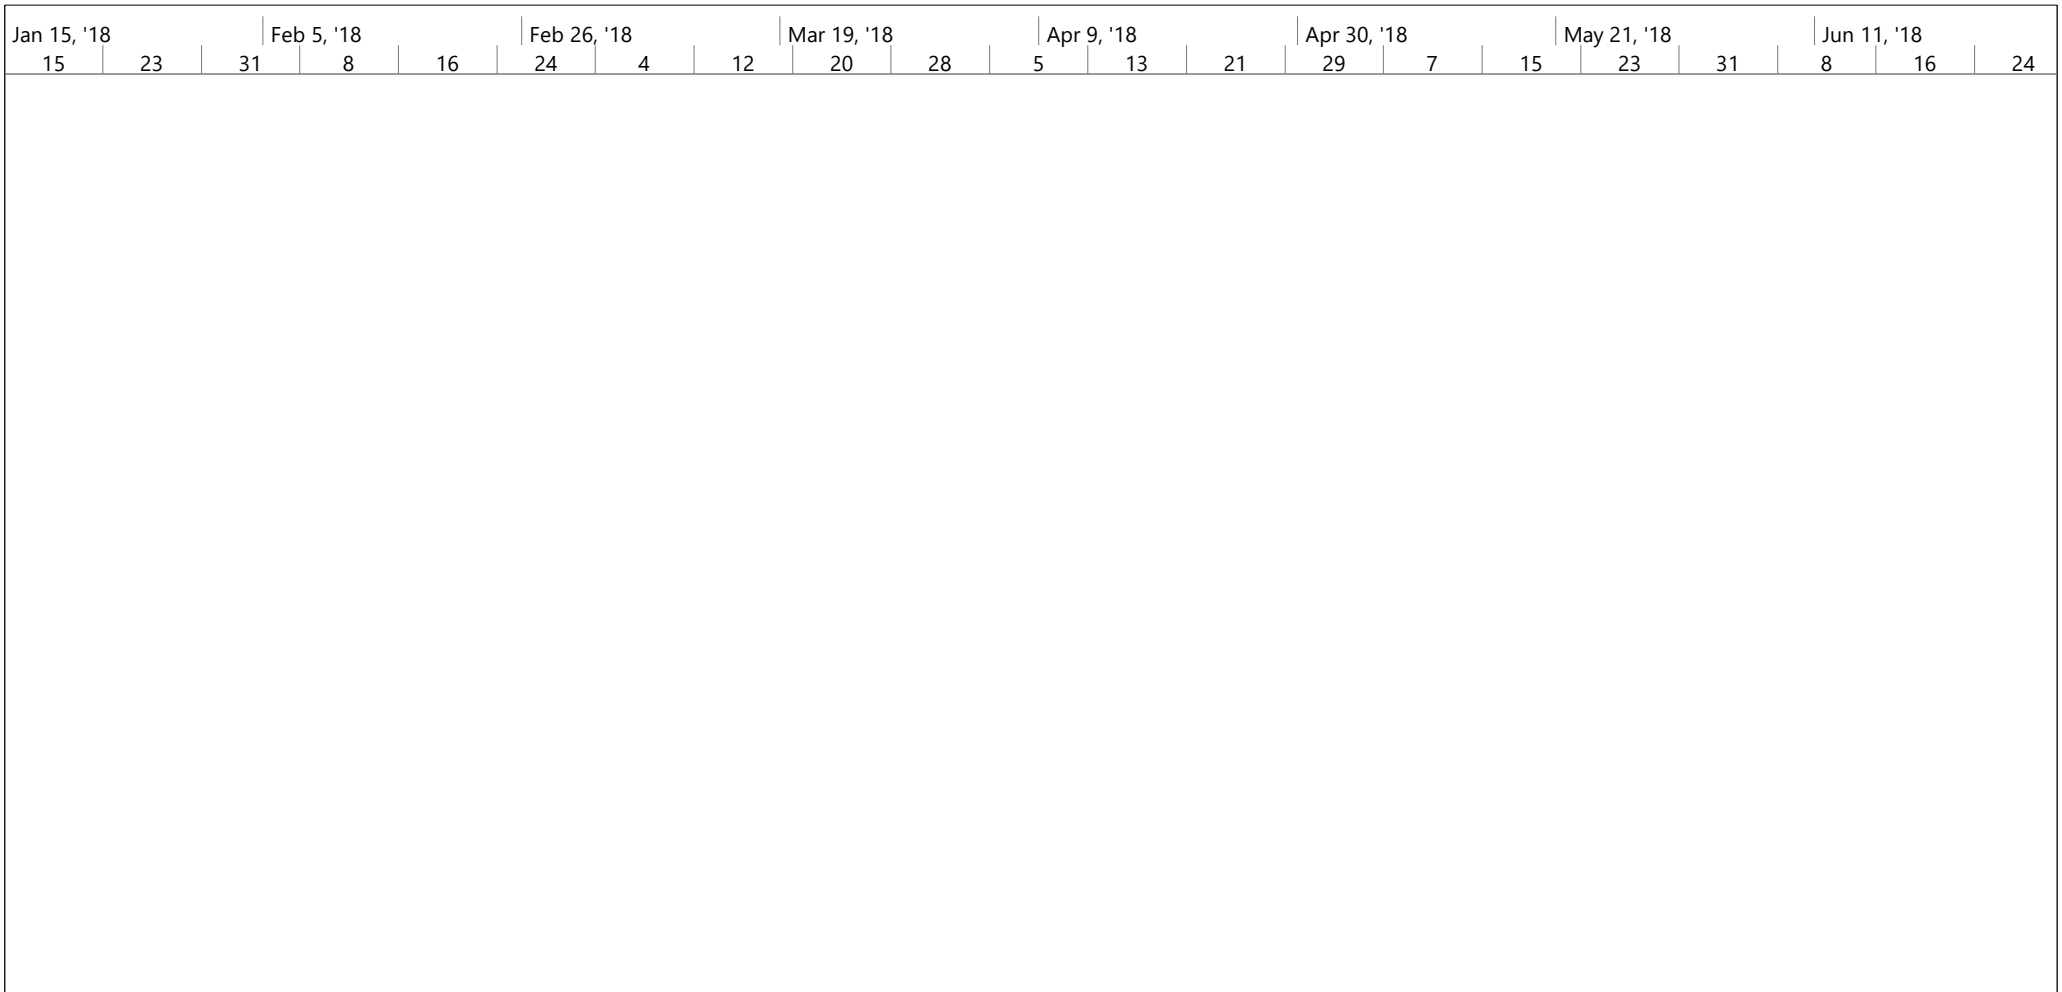

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

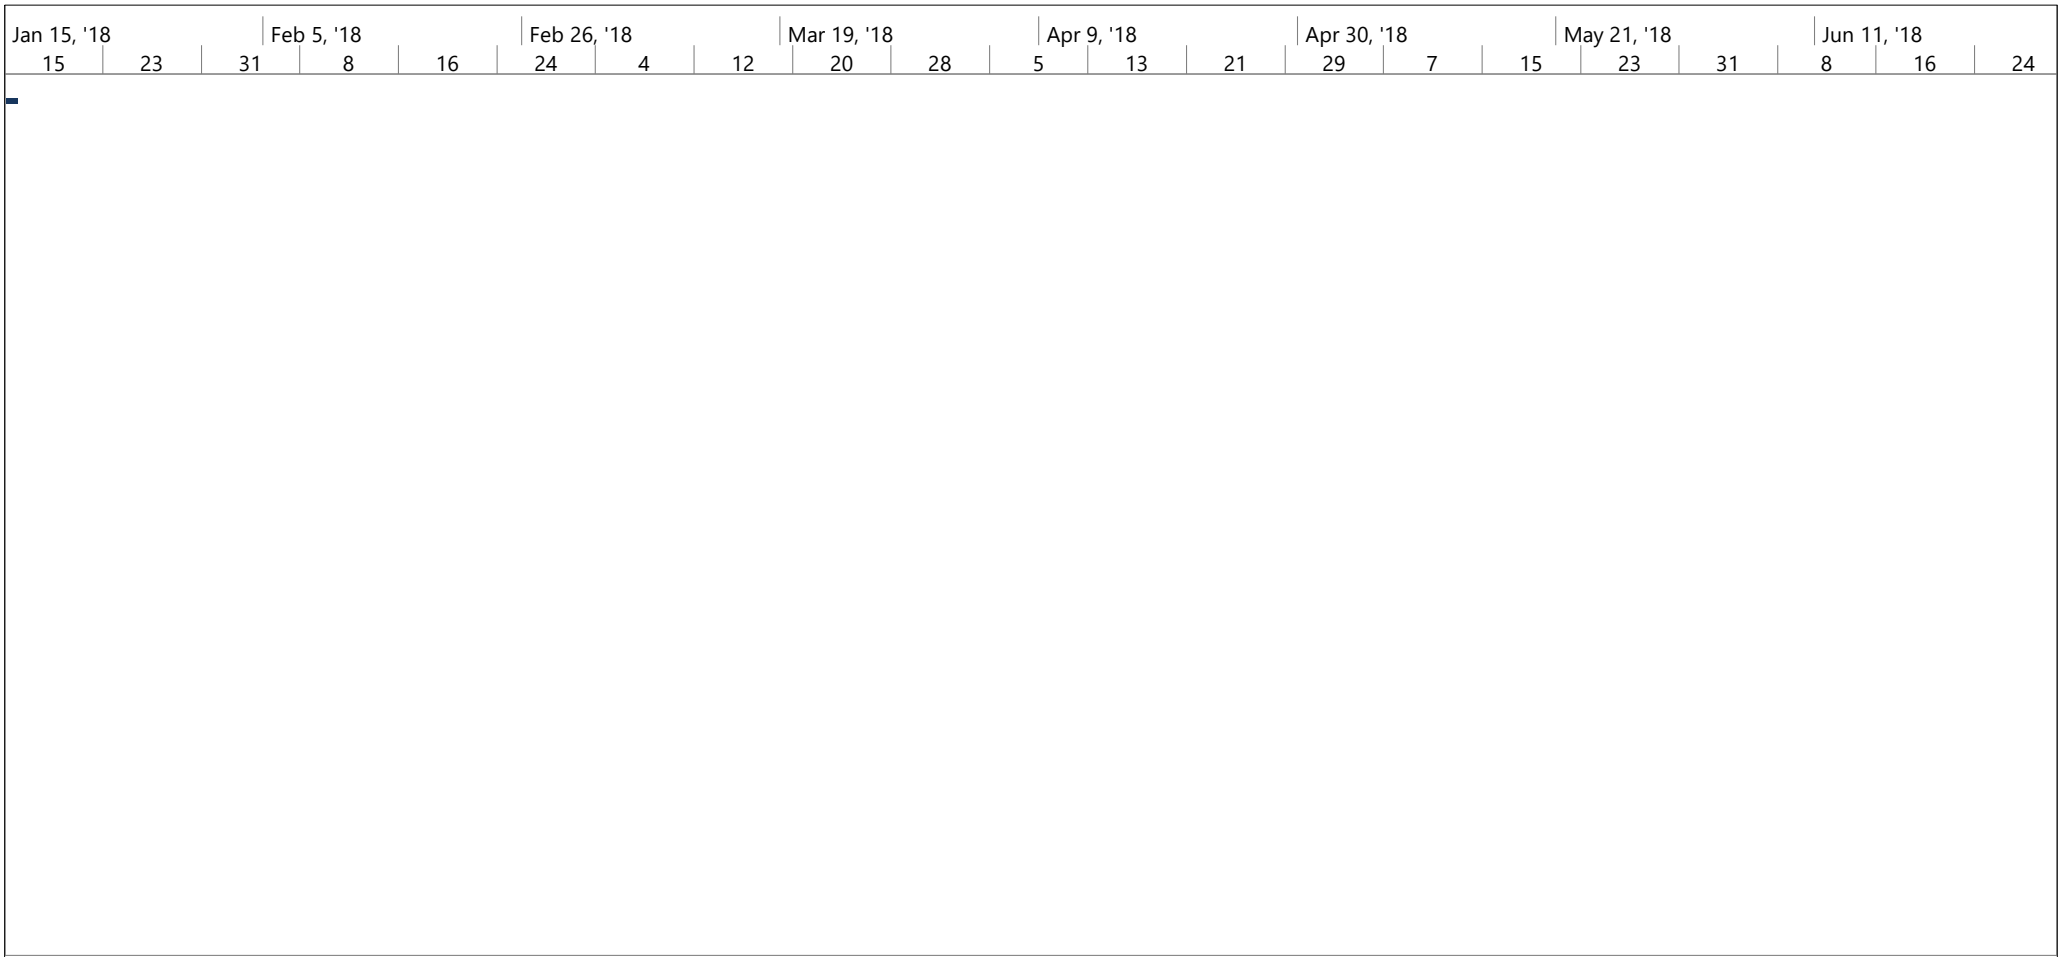

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

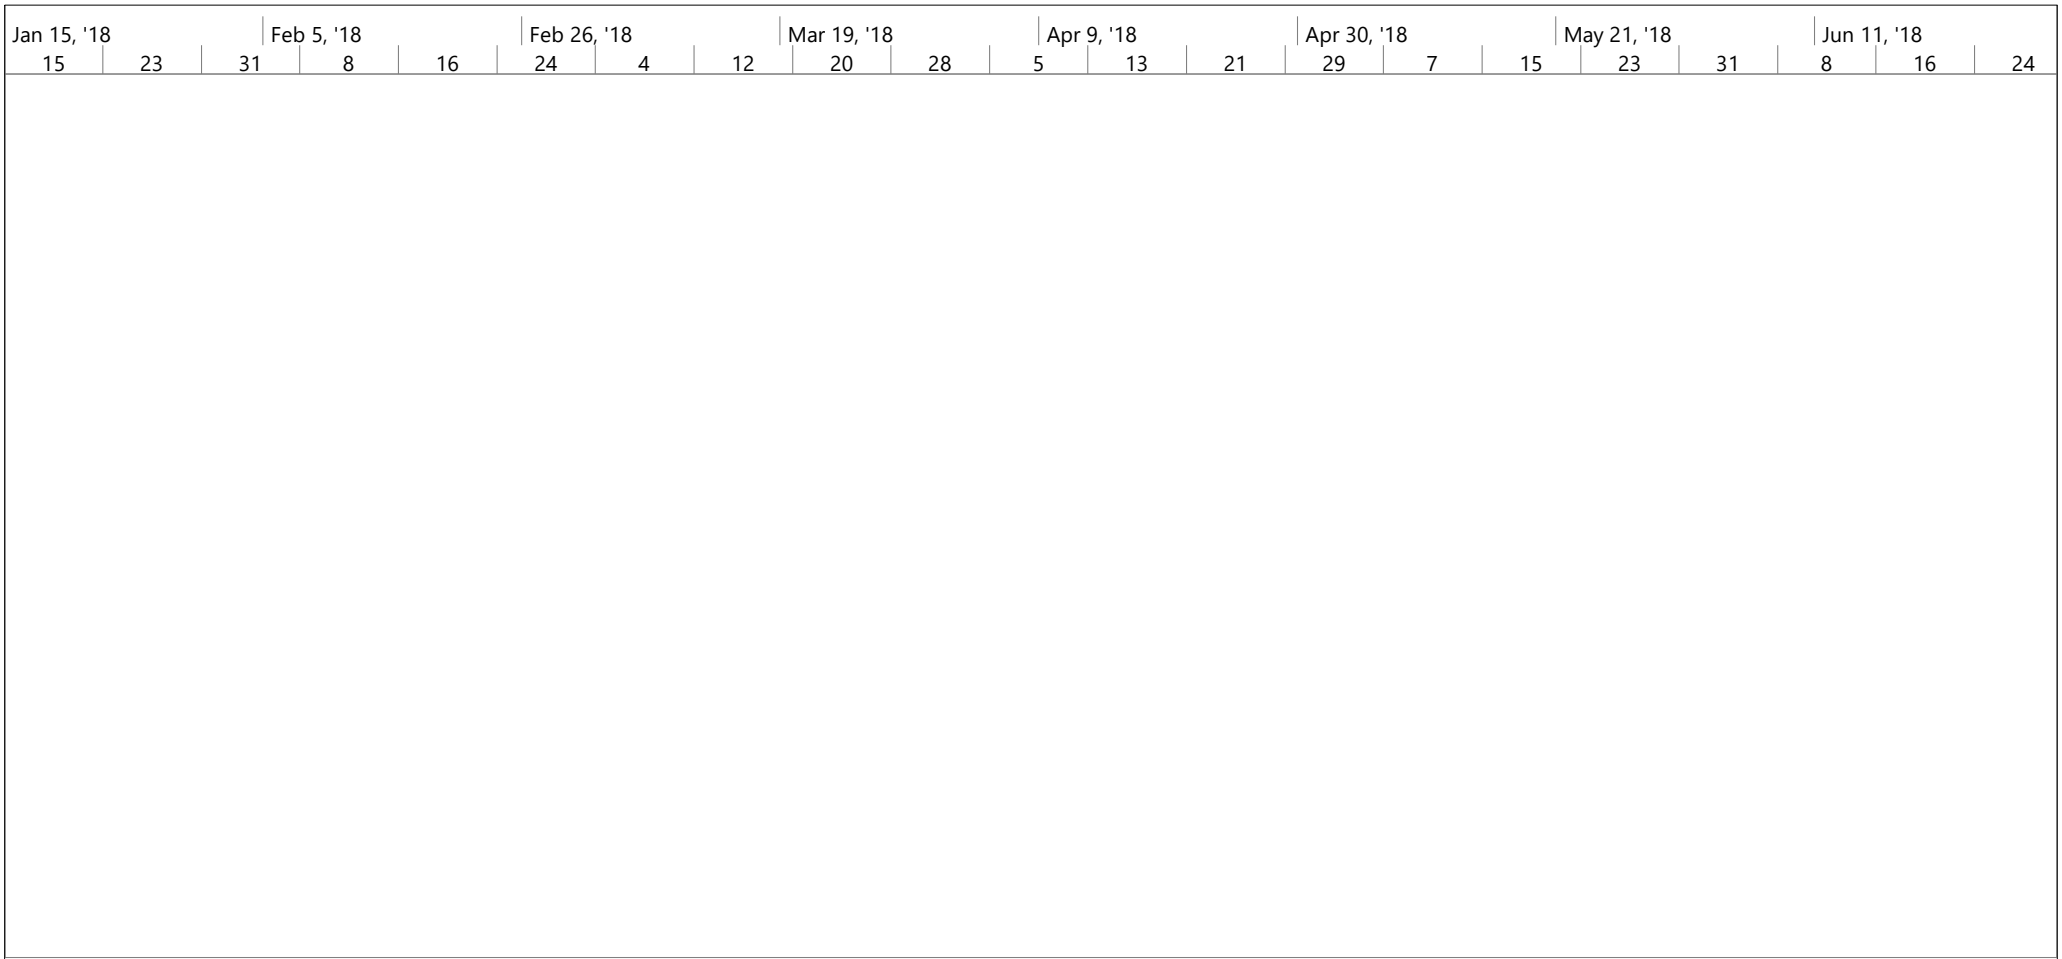

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

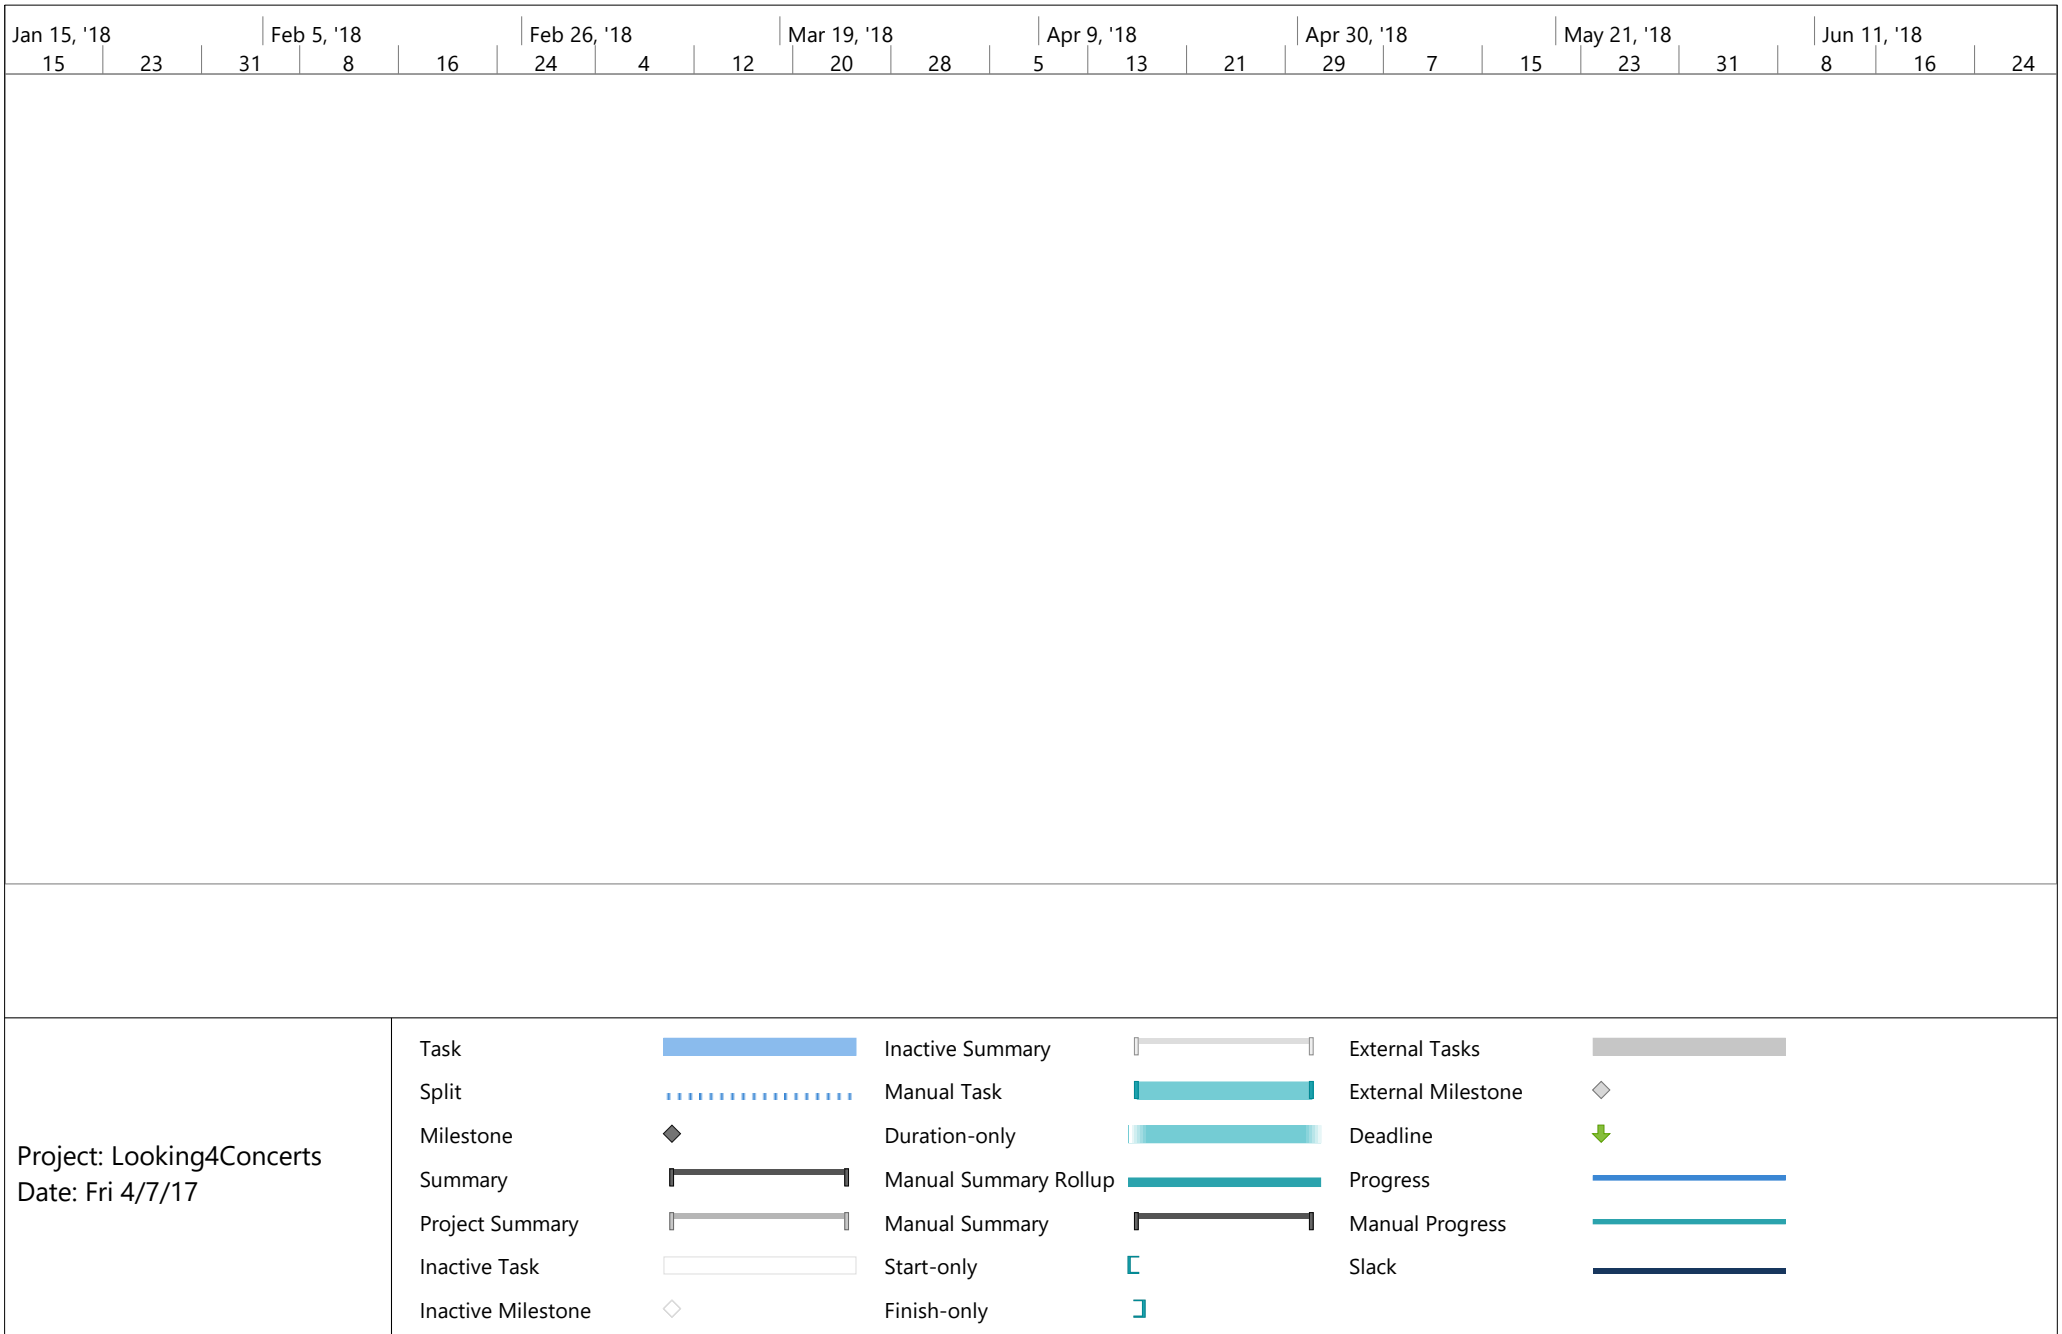

Project: Looking4Concerts
Date: Fri 4/7/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	
