ID		Task Mode	Task Name	Duration	Start	Finish	Free Slack	Predecessors	Resource Names
1			**Github Repo Creatior**	**232 days**	**Thu 09.02.17**	**Sat 30.12.17**	**0 days**		
2			Personal Wiki page	1 day	Thu 09.02.17	Thu 09.02.17	0 days		
3			Project wiki page c	232 days	Fri 10.02.17	Sat 30.12.17	10 days	2	
4			Weekly issue creat	232 days	Fri 10.02.17	Sat 30.12.17	10 days	2	
5			**Requirements**	**4 days**	**Thu 16.02.17**	**Tue 21.02.17**	**0 days**		
6			**Requirements Ana**	**2 days**	**Thu 16.02.17**	**Sun 19.02.17**	**0 days**		
7			Discussing the pı	1 day	Thu 16.02.17	Thu 16.02.17	0 days		
8			Asking unclear p	2 days	Fri 17.02.17	Sun 19.02.17	0 days	7	
9			**Requirements Elici**	**2 days**	**Mon 20.02.1**	**Tue 21.02.17**	**0 days**		
10			Talking to the cu	1 day	Mon 20.02.1	Mon 20.02.1	0 days	8	
11			Understanding a	1 day	Tue 21.02.17	Tue 21.02.17	1 day	10	
12			**Mock-ups**	**13 days**	**Thu 23.02.17**	**Mon 13.03.1**	**0 days**		
13			**Android and Web**	**3 days**	**Thu 23.02.17**	**Mon 27.02.1**	**0 days**	**9**	
14			Designing Sign-U	3 days	Thu 23.02.17	Mon 27.02.1	10 days		
15			Designing Profile	3 days	Thu 23.02.17	Mon 27.02.1	10 days		
16			Concert/User Se	3 days	Thu 23.02.17	Mon 27.02.1	10 days		
17			**Mockup Scenario (	13 days**	**Thu 23.02.17**	**Mon 13.03.1**	**0 days**	**9**	
18			Leroy Velasquez	2 days	Sat 11.03.17	Mon 13.03.1	0 days		Kemal Berk
19			John Smith	3 days	Thu 23.02.17	Mon 27.02.1	10 days		
20			Sarp and Mert	2 days	Sat 11.03.17	Mon 13.03.1	0 days		Furkan
21			Requirements & Desi	0 days	Tue 14.03.17	Tue 14.03.17	25 days	7;8;10;11;14;15;1	
22			**Diagram Creation**	**24 days**	**Thu 02.03.17**	**Tue 04.04.17**	**0 days**	**9**	
23			**Use Case Diagram**	**3 days**	**Thu 02.03.17**	**Mon 06.03.1**	**0 days**		

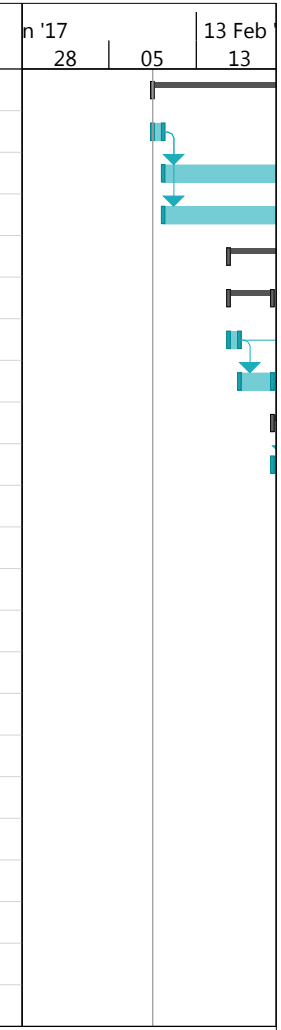

Project: Looking4Concerts
Date: Tue 03.10.17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only		Slack	
Inactive Milestone		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Free Slack	Predecessors	Resource Names
24		Concert Creatior	3 days	Thu 02.03.17	Mon 06.03.17	0 days		
25		View Concert an	3 days	Thu 02.03.17	Mon 06.03.17	0 days		
26		Search Concert a	3 days	Thu 02.03.17	Mon 06.03.17	0 days		
27		Registration/Sigr	3 days	Thu 02.03.17	Mon 06.03.17	0 days		
28		Sign In	3 days	Thu 02.03.17	Mon 06.03.17	0 days		
29		Get Recommenc	3 days	Thu 02.03.17	Mon 06.03.17	0 days		
30		Follow Another I	3 days	Thu 02.03.17	Mon 06.03.17	0 days		
31		Mark a Concert /	3 days	Thu 02.03.17	Mon 06.03.17	0 days		
32		Class Diagram	3 days	Tue 07.03.17	Thu 09.03.17	0 days	24;25;26;27;28;29	
33		Sequence Diagram	4 days	Fri 10.03.17	Wed 15.03.17	0 days	32	
34		Activity Diagram	14 days	Thu 16.03.17	Tue 04.04.17	9 days	33	
35		Diagram Creation	0 days	Tue 18.04.17	Tue 18.04.17	194 days	34;21	
36		**Planning**	**39 days**	**Tue 14.03.17**	**Fri 05.05.17**	**0 days**		
37		Communication Plan	4 days	Thu 16.03.17	Tue 21.03.17	213 days		
38		**Project Plan**	**11 days**	**Tue 14.03.17**	**Tue 28.03.17**	**0 days**		
39		Milestone Creation	11 days	Tue 14.03.17	Tue 28.03.17	29 days		
40		Test Plan	14 days	Tue 04.04.17	Fri 21.04.17	190 days		
41		Responsibility Assignment Matrix	14 days	Tue 18.04.17	Fri 05.05.17	180 days		
42		Project Plan	0 days	Tue 09.05.17	Tue 09.05.17	179 days	39	
43		**Testing**	**65 days**	**Mon 16.10.17**	**Fri 12.01.18**	**0 days**		



ID	Task Mode	Task Name	Duration	Start	Finish	Free Slack	Predecessors	Resource Names
44		Creating Test Cases	65 days	Mon 16.10.17	Fri 12.01.18	0 days		
45		**Big Revision**	**16 days**	**Fri 29.09.17**	**Fri 20.10.17**	**0 days**		
46		Plan Review	16 days	Fri 29.09.17	Fri 20.10.17	60 days		
47		Task Distribution	16 days	Fri 29.09.17	Fri 20.10.17	60 days		
48		Responding on Feedbacks	16 days	Fri 29.09.17	Fri 20.10.17	60 days		
49		Database	0 days	Sat 21.10.17	Sat 21.10.17	61 days	54;55;56	
50		**Implementation**	**42 days**	**Mon 02.10.17**	**Tue 28.11.17**	**0 days**		
51		**Back-End Developments**	**33 days**	**Mon 02.10.17**	**Wed 15.11.17**	**0 days**		Kemal Berk;Enes;H
52		**Database System Design / Implementation**	**14 days**	**Mon 02.10.17**	**Thu 19.10.17**	**0 days**		**Oğuzhan;Kemal Berk;Enes;Haluk;**
53		AWS Deployment	2 days	Tue 10.10.17	Wed 11.10.17	0 days	57	Kemal Berk;Enes;Haluk;
54		DB Modeling	3 days	Mon 02.10.17	Wed 04.10.17	4 days		Oğuzhan;Kemal B
55		User Table Im	7 days	Wed 11.10.17	Thu 19.10.17	1 day	53;54	Oğuzhan;Kemal B
56		Concert Table	7 days	Wed 11.10.17	Thu 19.10.17	1 day	53;54	Oğuzhan;Kemal B
57		API Implementation	6 days	Mon 02.10.17	Mon 09.10.17	0 days		Kemal Berk;Enes;Haluk;

n '17 28 | 05 | 13 Feb 13

Project: Looking4Concerts
Date: Tue 03.10.17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

ID	Task Mode	Task Name	Duration	Start	Finish	Free Slack	Predecessors	Resource Names
58		**Algorithm Implementation**	**17 days**	**Tue 24.10.17**	**Wed 15.11.17**	**0 days**		**Oğuzhan;Kemal Berk;Enes;Haluk;(**
63		**Front-End Developments**	**37 days**	**Mon 02.10.17**	**Tue 21.11.17**	**0 days**		Haluk;Enes;
64		**Web Developments**	**37 days**	**Mon 02.10.17**	**Tue 21.11.17**	**0 days**		**Enes;Haluk;Alper**
65		Create Concert Page Implementati	9 days	Mon 02.10.17	Thu 12.10.17	0 days		Haluk;Enes;Alpert
66		Git Connectio	2 days	Tue 10.10.17	Wed 11.10.17	67 days		Enes;Haluk;Alpert
67		Login Page Im	5 days	Fri 13.10.17	Thu 19.10.17	2 days	65	Enes;Haluk;Alpert
68		Search Page Ir	5 days	Tue 24.10.17	Mon 30.10.17	0 days	67	Enes;Haluk;Alpert
69		Notifications F	6 days	Tue 31.10.17	Tue 07.11.17	0 days	68	Enes;Haluk;Alpert
70		Search Results	5 days	Wed 08.11.17	Tue 14.11.17	0 days	69	Enes;Haluk;Alpert
71		User Page Imp	5 days	Wed 15.11.17	Tue 21.11.17	38 days	70	Enes;Haluk;Alpert
72		Concert Page	9 days	Mon 16.10.17	Thu 26.10.17	56 days		Enes;Haluk;Alpert
73		**Android Developments**	**42 days**	**Mon 02.10.17**	**Tue 28.11.17**	**0 days**		Elif;Pınar;Fu
74		Create Concert Page Implementation	9 days	Mon 02.10.17	Thu 12.10.17	0 days		Elif;Pınar;Furkan;(
75		Login Page Imple	8 days	Fri 13.10.17	Tue 24.10.17	58 days	74	Elif;Furkan;Pınar;(
76		Concert Page Im	9 days	Mon 16.10.17	Thu 26.10.17	10 days		Elif;Furkan;Pınar;(

n '17 | 28 | 05 | 13 Feb '1 | 13

Project: Looking4Concerts
Date: Tue 03.10.17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

ID	Task Mode	Task Name	Duration	Start	Finish	Free Slack	Predecessors	Resource Names
77		User Profile Imp	5 days	Fri 10.11.17	Thu 16.11.17	0 days	76	Elif;Furkan;Pınar;(
78		Database Conne	8 days	Fri 17.11.17	Tue 28.11.17	33 days	77	Elif;Furkan;Pınar;(
79		Designing Android and Web UI	0 days	Fri 17.11.17	Fri 17.11.17	41 days	77	
80		**Documentation**	**9 days**	**Thu 16.11.17**	**Wed 29.11.1**	**0 days**		
81		Project Process Do	2 days	Thu 16.11.17	Fri 17.11.17	0 days		
82		Tutorial Creation	5 days	Mon 20.11.1	Fri 24.11.17	2 days	81	
83		Release	0 days	Wed 29.11.1	Wed 29.11.1	33 days	82	



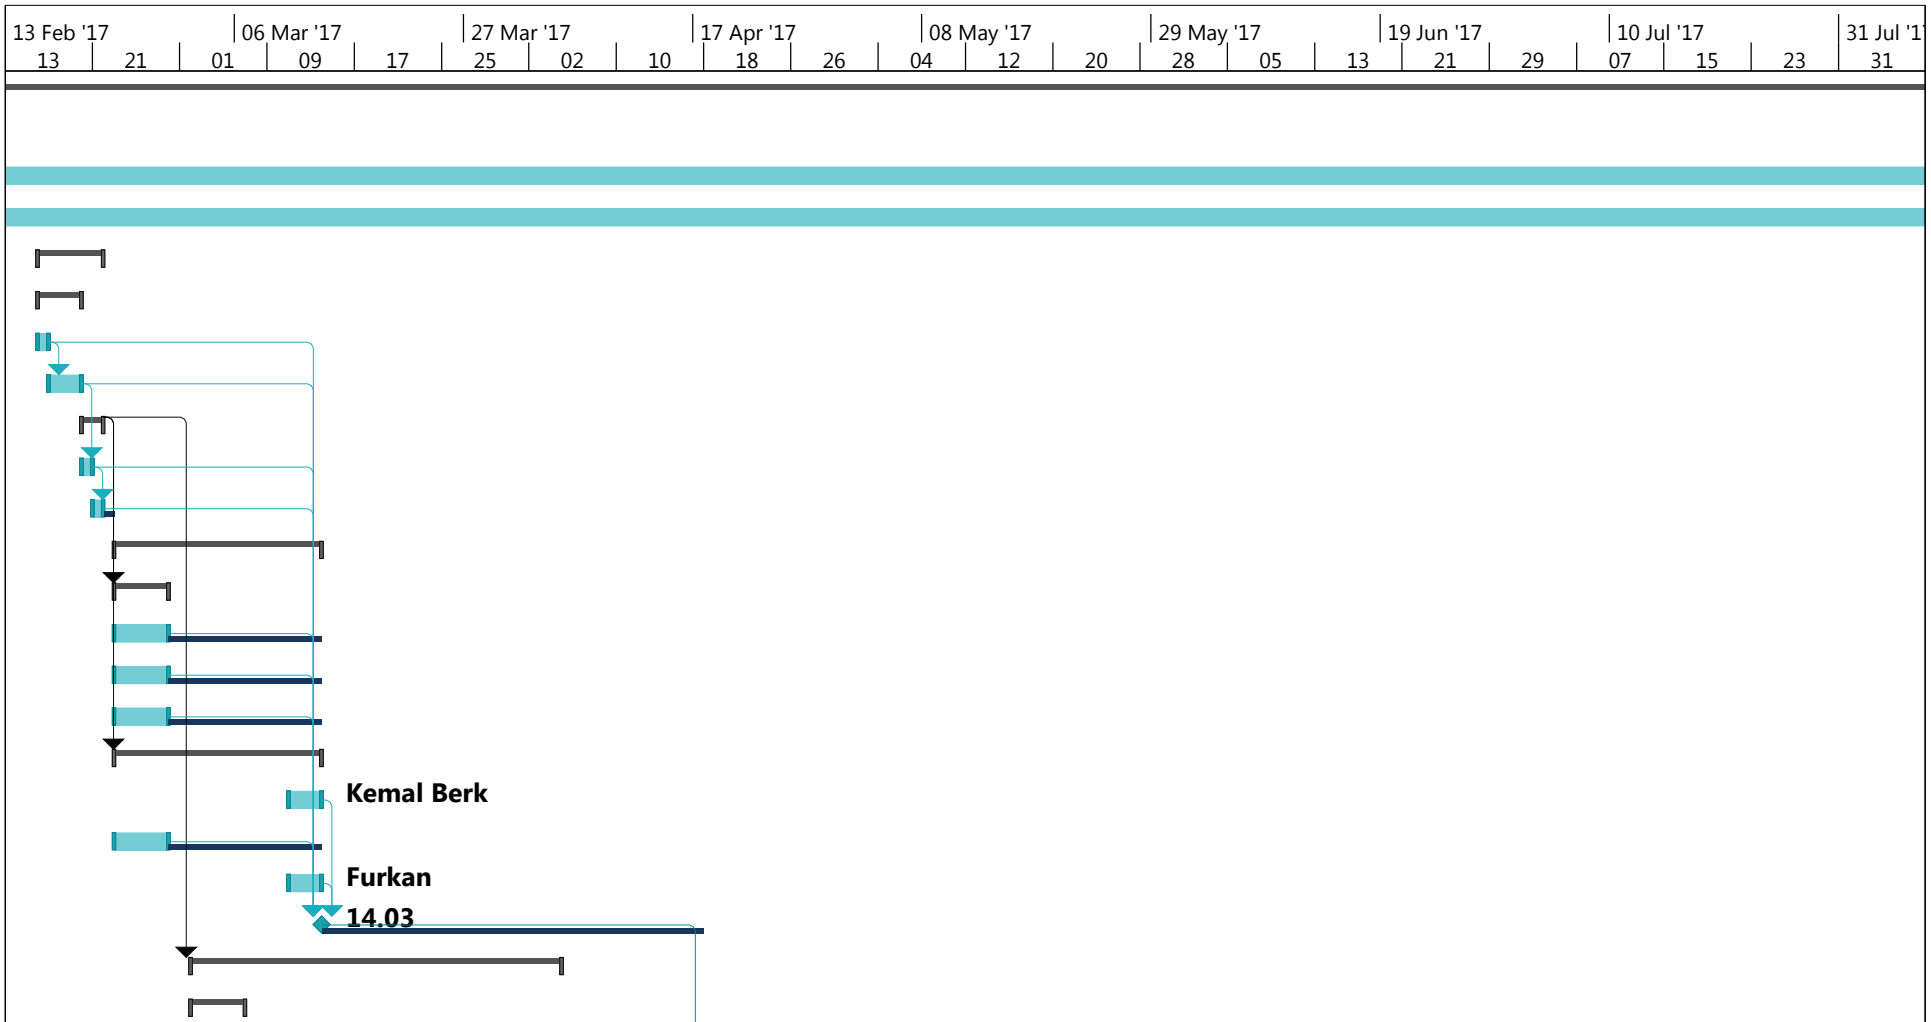

Project: Looking4Concerts
Date: Tue 03.10.17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only		Slack	
Inactive Milestone		Finish-only			

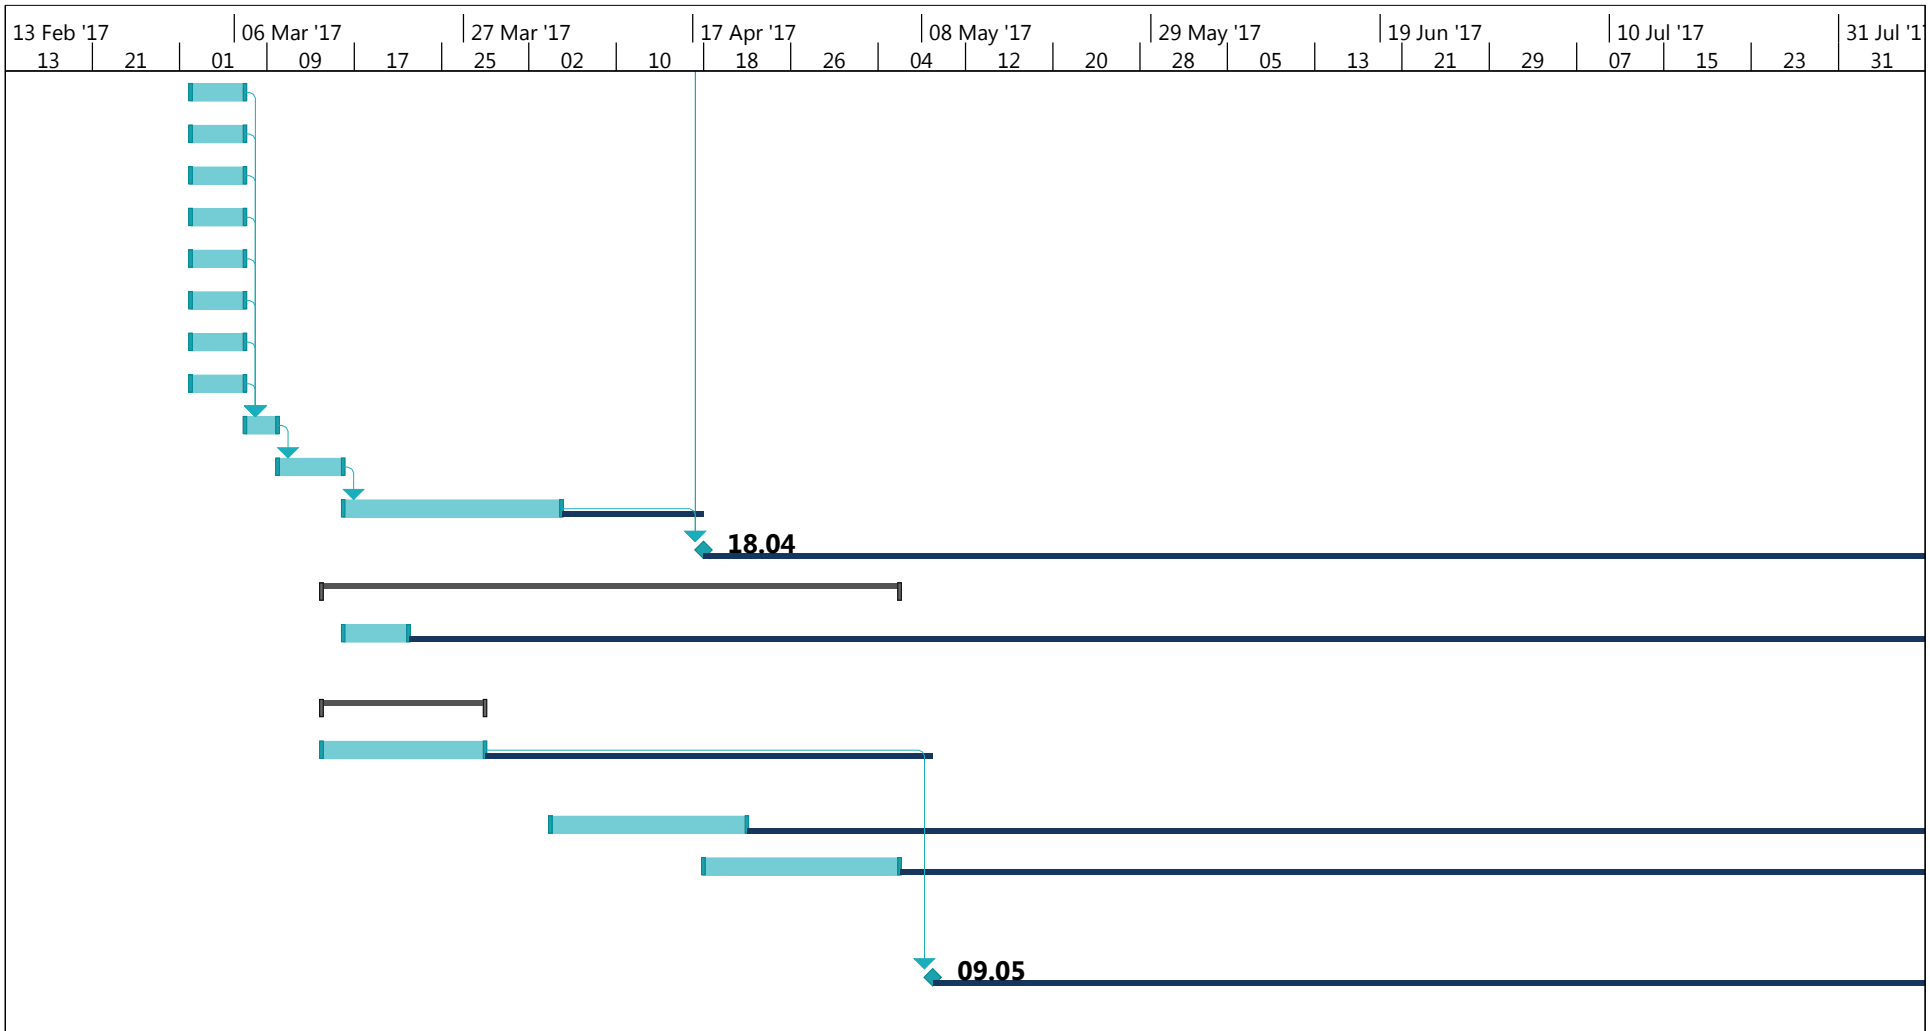

Project: Looking4Concerts
Date: Tue 03.10.17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only		Slack	
Inactive Milestone		Finish-only			

Project: Looking4Concerts
Date: Tue 03.10.17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only		Slack	
Inactive Milestone		Finish-only			

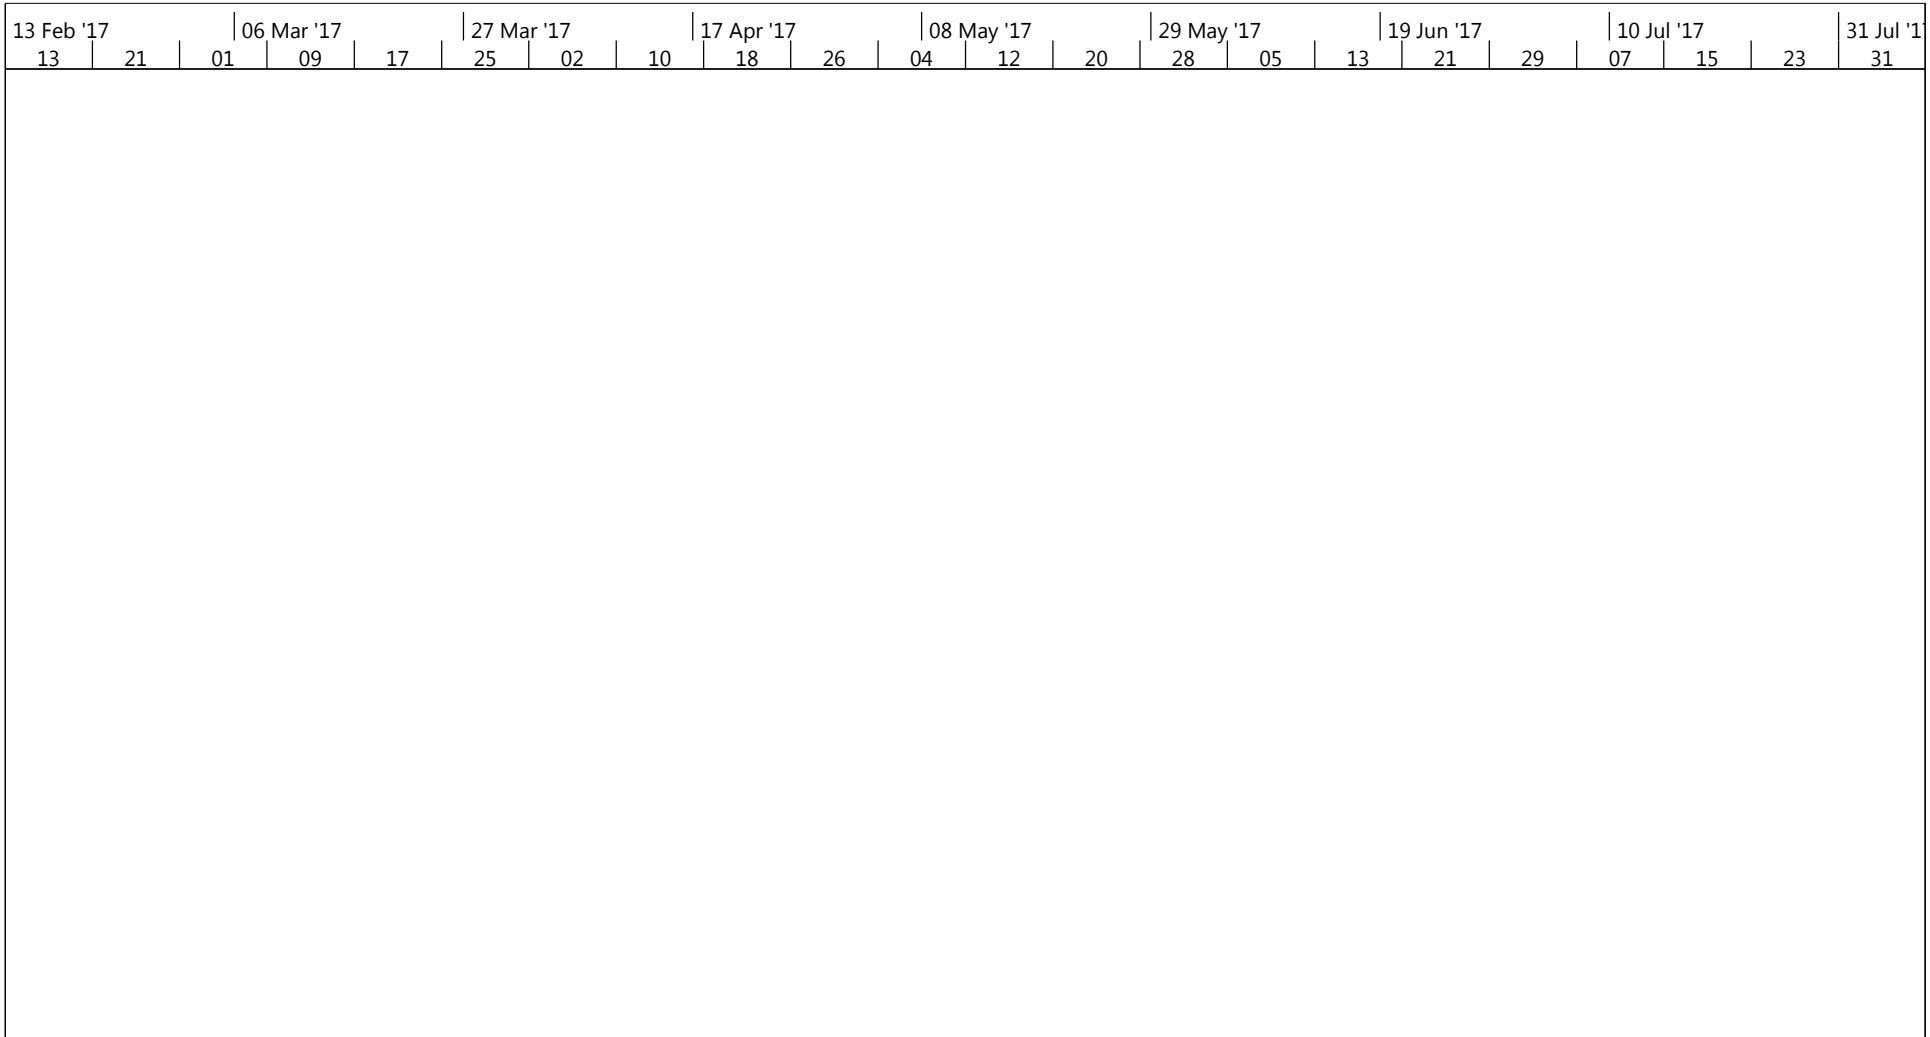

Project: Looking4Concerts
Date: Tue 03.10.17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	



Project: Looking4Concerts
Date: Tue 03.10.17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only		Slack	
Inactive Milestone		Finish-only			

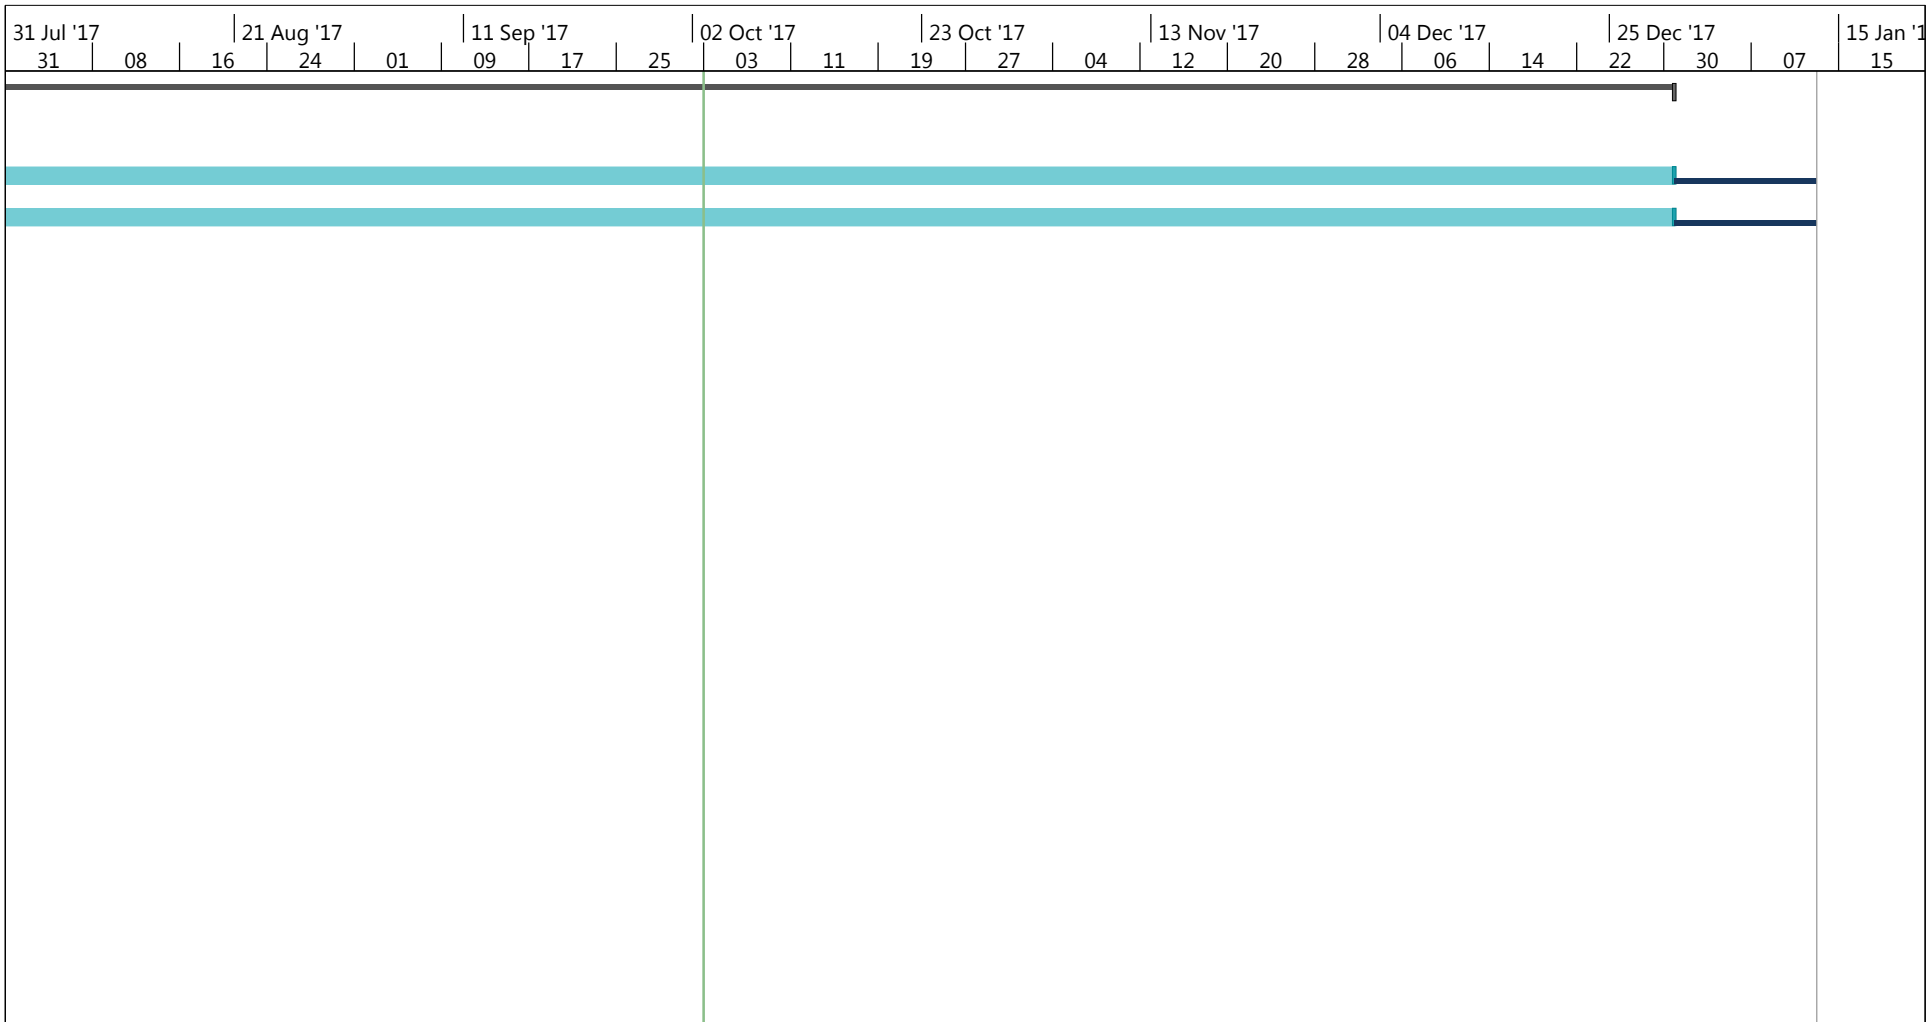

Project: Looking4Concerts
Date: Tue 03.10.17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	Slack
Inactive Milestone	Finish-only	

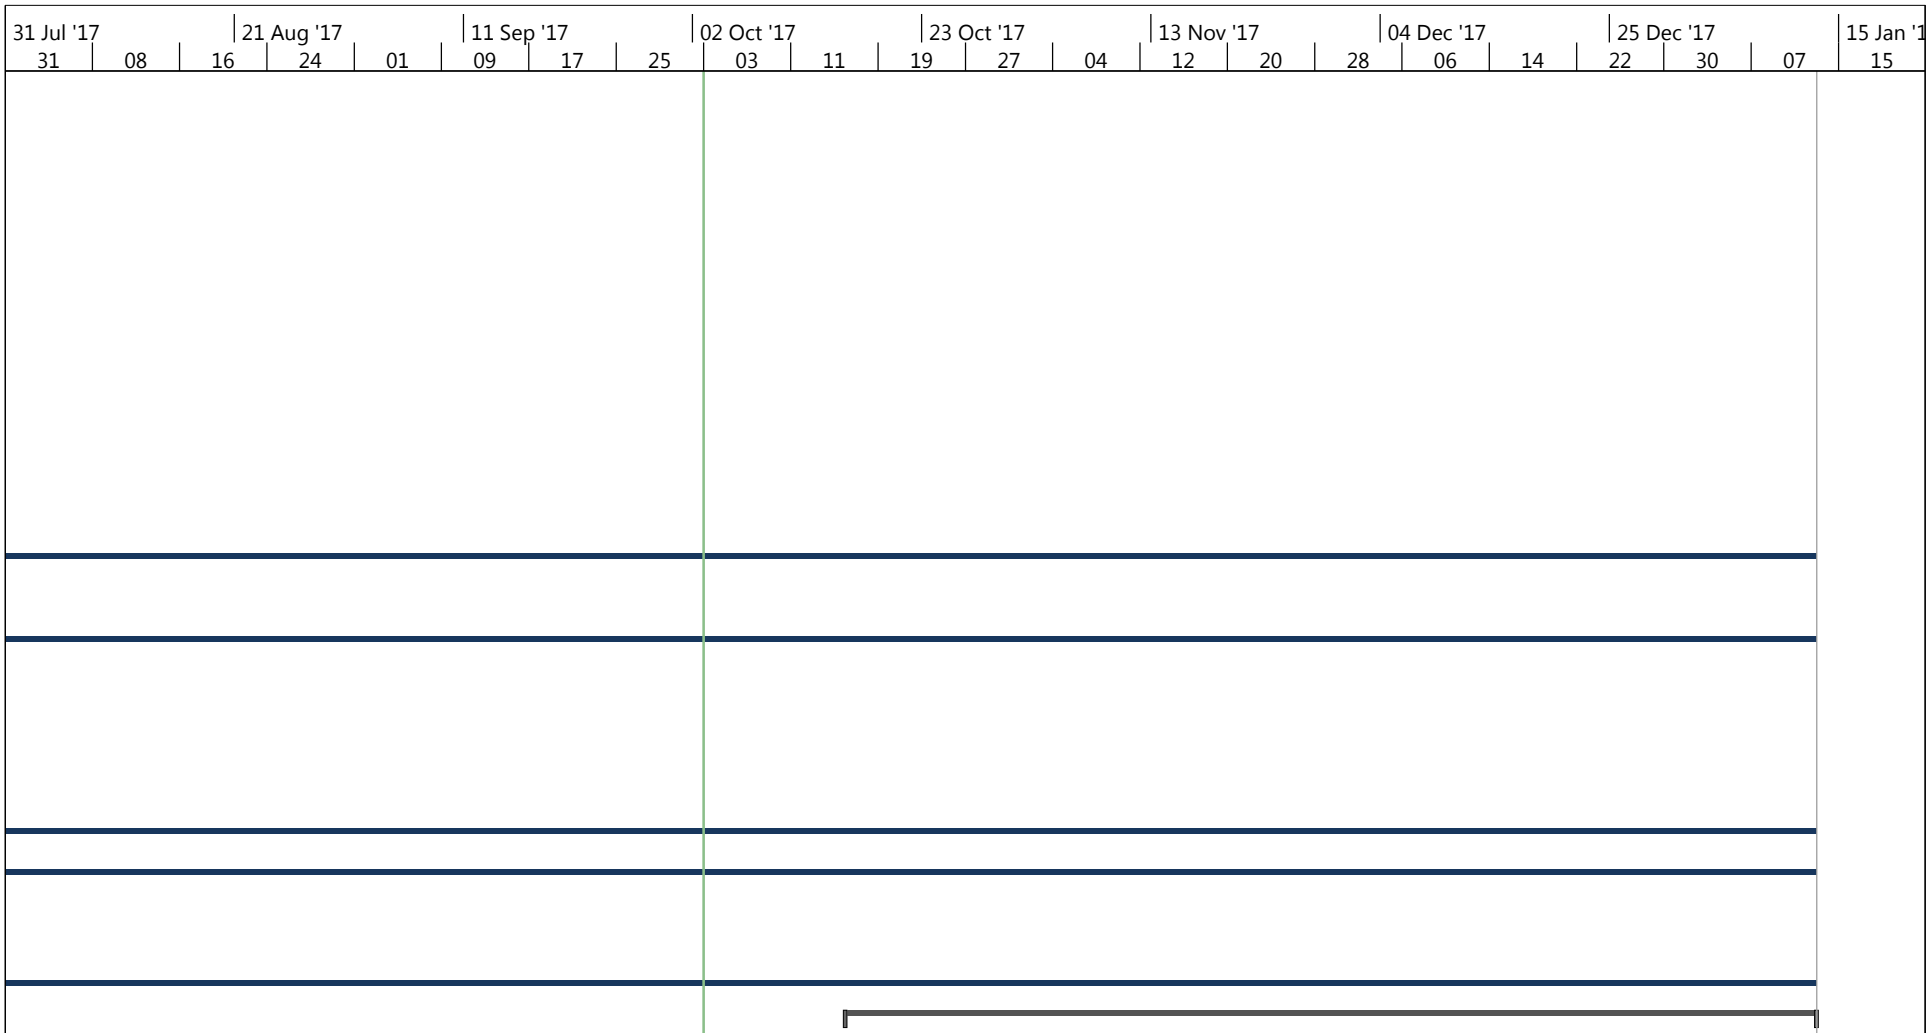

Project: Looking4Concerts
Date: Tue 03.10.17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only		Slack	
Inactive Milestone		Finish-only			

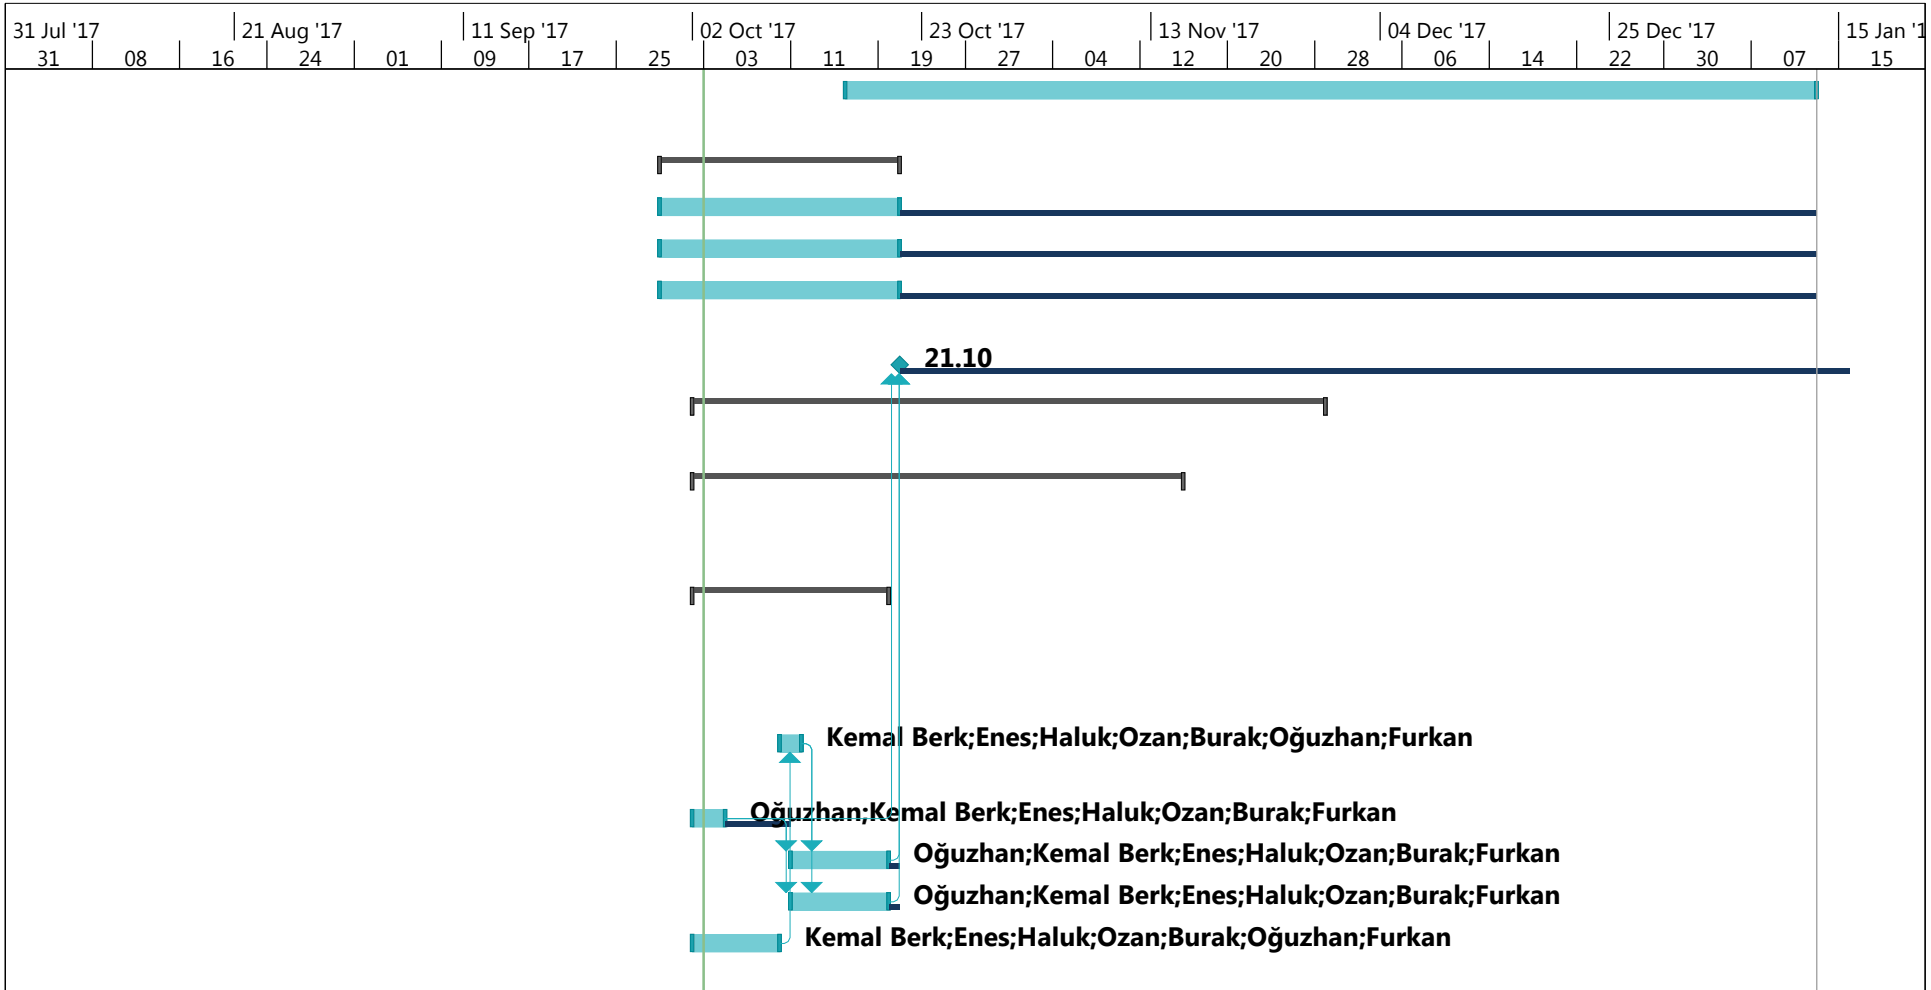

Project: Looking4Concerts
Date: Tue 03.10.17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only		Slack	
Inactive Milestone		Finish-only			

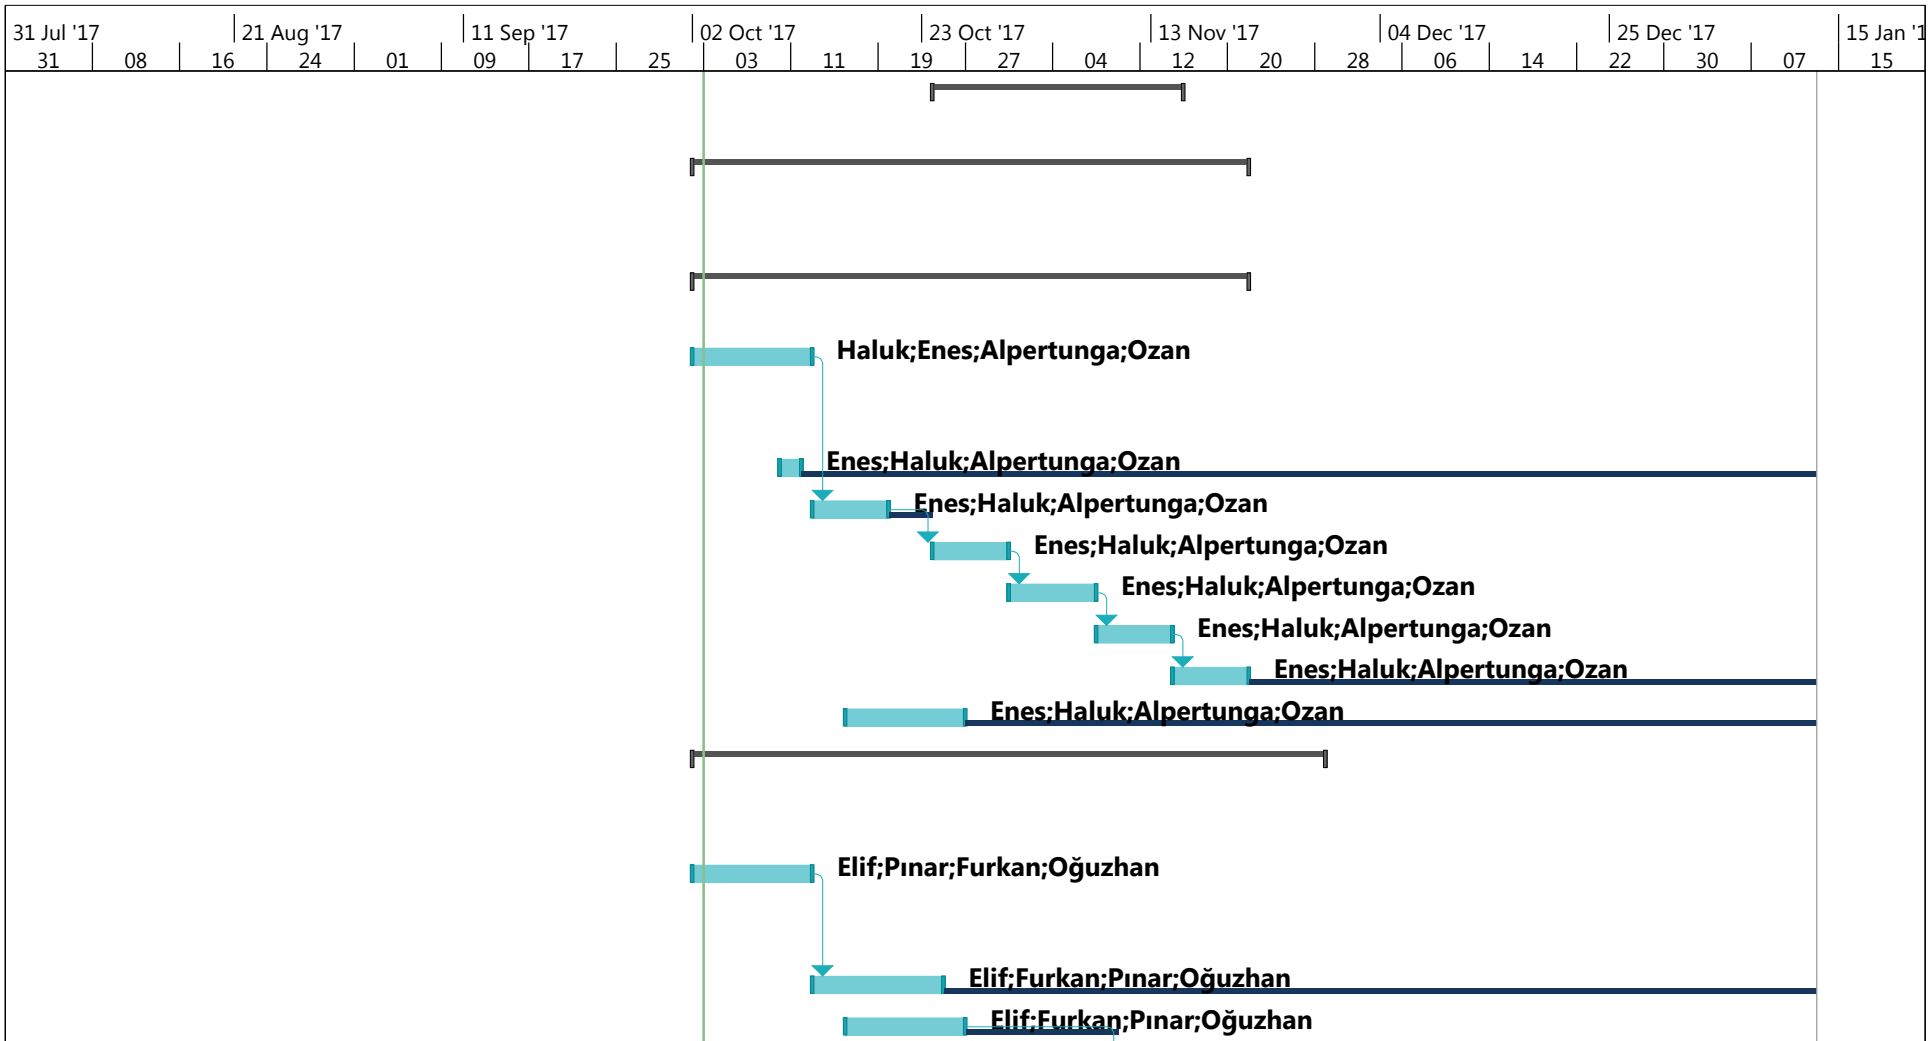

Project: Looking4Concerts
Date: Tue 03.10.17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only		Slack	
Inactive Milestone		Finish-only			

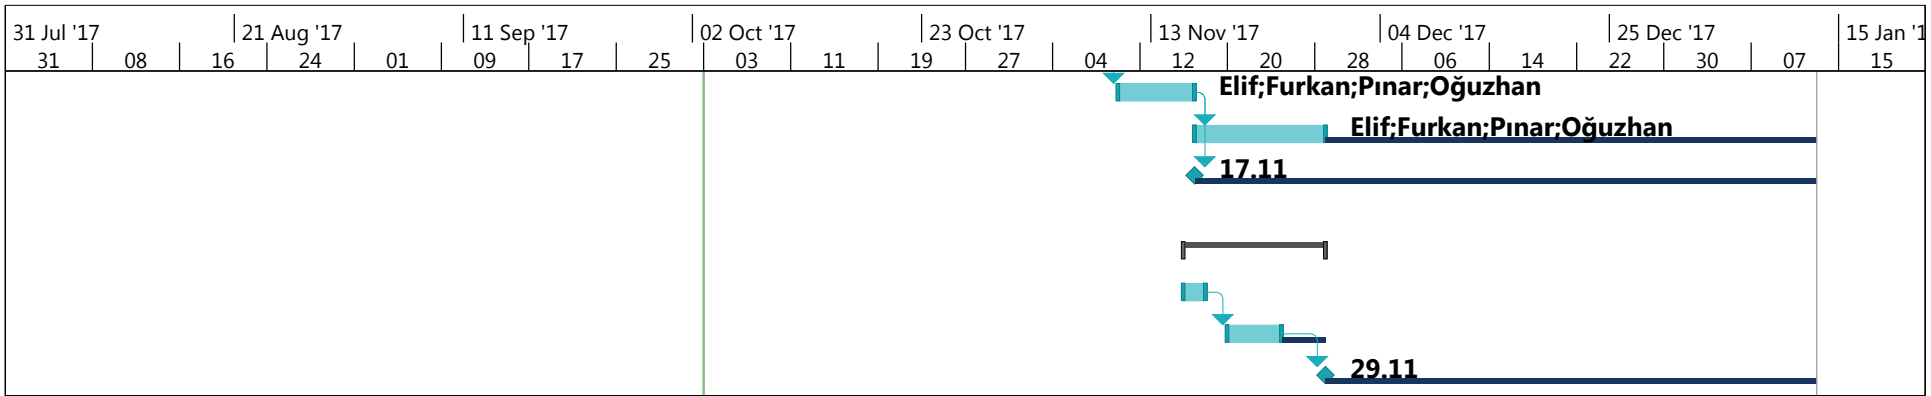

Project: Looking4Concerts
Date: Tue 03.10.17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only		Slack	
Inactive Milestone		Finish-only			

Project: Looking4Concerts
Date: Tue 03.10.17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only		Slack	
Inactive Milestone		Finish-only			

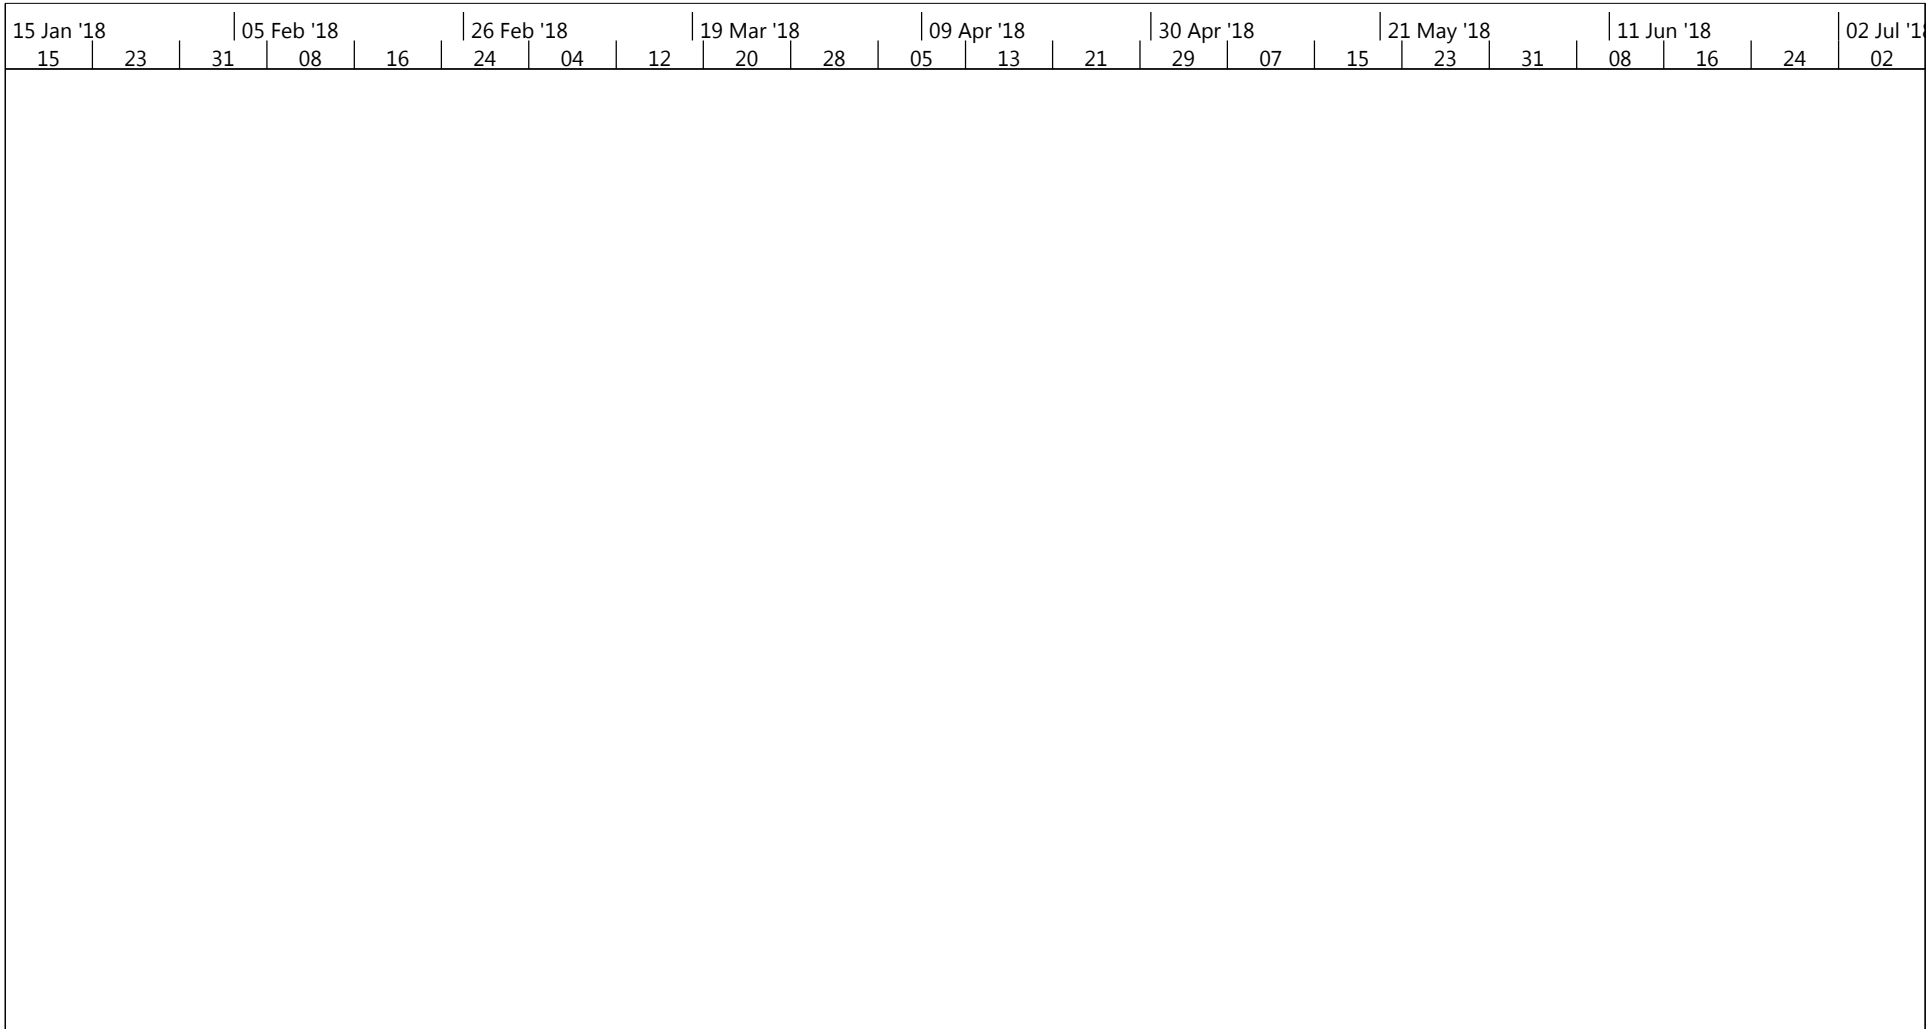

Project: Looking4Concerts
Date: Tue 03.10.17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only		Slack	
Inactive Milestone		Finish-only			

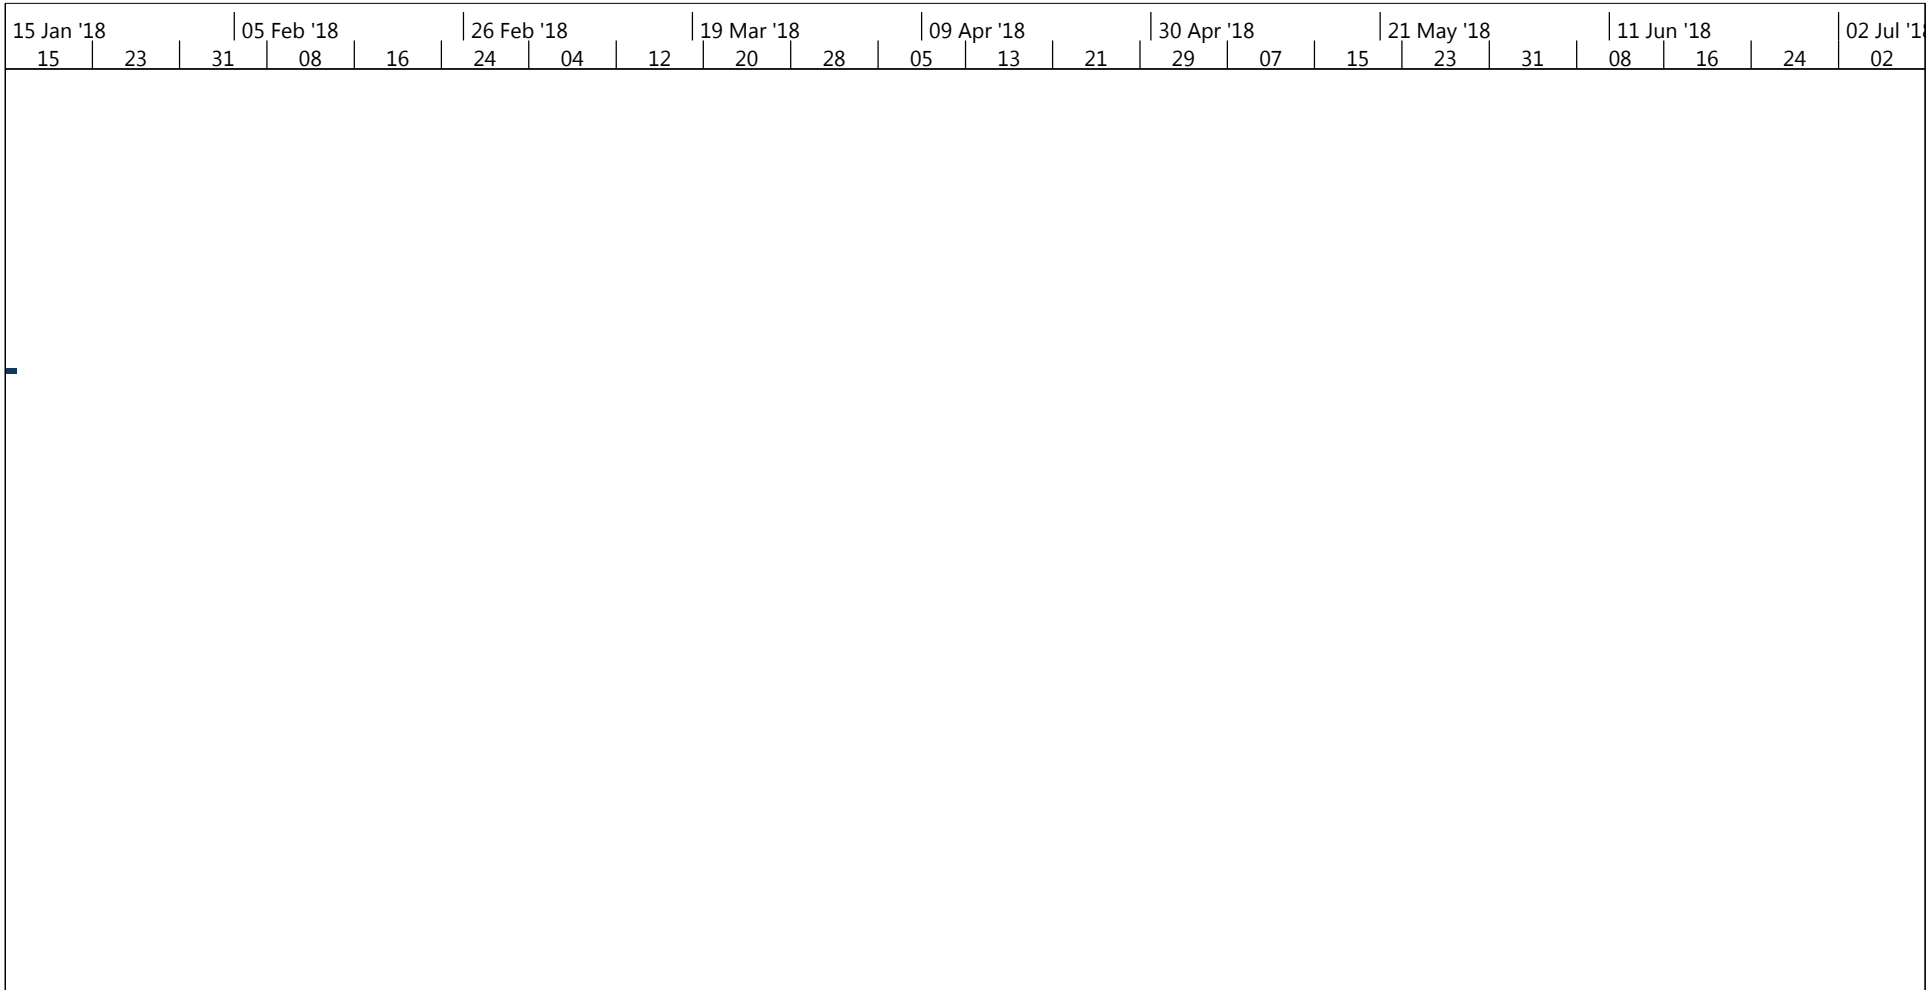

Project: Looking4Concerts
Date: Tue 03.10.17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only		Slack	
Inactive Milestone		Finish-only			

Project: Looking4Concerts
Date: Tue 03.10.17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only		Slack	
Inactive Milestone		Finish-only			



Project: Looking4Concerts
Date: Tue 03.10.17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only		Slack	
Inactive Milestone		Finish-only			
